

Ref. No: - CIPLA/EHS-ENV/KKB-III/04/2026

01.06.2026

**The Deputy Director General of Forests (Central),
West Central Zone,
Regional Office,
New Secretariate Building,
Opp. VCA Ground,
Civil Lines,
Nagpur-440 001.**

Subject: Half Yearly Environment Clearance Compliance Report

Ref. No: Environment clearance No. J-11011/47/2005-IA II (I) dated 13.10.2005.

Respected Sir,

With reference to the above subject, we are hereby submitting the six-monthly Environment clearance compliance report for the period of Dec -2025 to May-2026.

1. Point-wise compliance to clearance No. J-11011/48/2005-IA II (I) dated 13.10.2005.

This is for your information.

Kindly acknowledge receipt of the same.

Thanking You,

Your's faithfully,

For Cipla Ltd.



Authorized Signatory

Encl: As Above.

SIX MONTHLY COMPLIANCE STATUS TO THE CONDITIONS OF ENVIRONMENTAL CLERANCE FROM MOEF FOR THE PERIOD December 2025 To May 2026.

REF.NO. J-11011/47/2005- IAll (I) Dt.13.10.2005

Sr No.	Conditions as per EC dated 13.10.2005	Compliance Status as on date 01.06.2026
A	SPECIFIC CONDITIONS	
i.	The gaseous emissions (SO ₂ , NO _x , NH ₃ & HCl) and particulate matters, from various process units shall conform to the standards prescribed by the concerned authorities from time to time. At no time, the emission levels shall go beyond the stipulated standards. In the event of failure of pollution control system(s) adopted by the unit shall not be restarted until the control measures are rectified to achieve the desired efficiency.	Complied. The emission level at present fully conforms to the standards for the current CTO. The plan for monitoring of AAQ, work- zone air quality and source emissions to check the emission level is already put in place. We ensure to comply the given condition. Photocopy of Reports attached as per Annexure - I
ii.	Ambient Air Quality Monitoring Stations shall be set up in the down wind direction as well as where maximum ground level concentration are anticipated in consultation with the SPCB.	Complied. Site already fixed the locations for AAQ monitoring in the downwind direction as well as where maximum ground level concentration are anticipated in consultation with MPCB. Photocopy of Reports attached as per Annexure - II
iii.	For control of air emissions, the reactors shall be provided with scrubbers and stack height shall be as per the Central Pollution Control Board guidelines.	Complied. For control of air emission, scrubbers are provided, and stack height is provided as per CPCB guidelines. Photocopy of Reports attached as per Annexure – III
iv.	Spent solvents shall be recovered as far as possible & recovery shall not be less than 95 percent. During purification process, solvent vapors are emitted from purification tanks as fugitive emissions. Action shall be taken to reduce the emission as far as possible. Use of toxic solvents like Methylene Chloride (MDC) etc. shall be minimum. All venting equipment shall have recovery system.	Complied. Site will recover the solvent wherever possible. As being Pharma industry reusing recovered solvents in process is challenging as there is possibility of impurities from recovered solvent quality can affect the final products safety and efficacy. Spent solvents generate in industry are sold to authorized party for recovery of solvents as per consent condition. Two stage condensers have been provided for recovery on the reactors. It will be always our efforts to reduce the consumption of solvents like Methylene Chloride.

V.	Industry shall switch over to aqueous based coating film in place of use of Methylene Chloride in coating operation and to non-halogenated solvents in place of halogenated solvents in a phased manner.	Noted. Site is currently bulk drug manufacturer & do not carry out any coating activity by using Methylene Chloride. This condition is Not Applicable to our activity.
vi.	Hazardous and toxic waste generated during process like distillation residue, spent carbon, spent mixture solvents, process organic residue should be incinerated in a properly designed incinerator with energy recovery facility. The incinerator shall meet the CPCB standards and guidelines.	Complied. The site is using CHWTSDF/Authorized recycler facilities for disposal of above specified material. We are following this stipulation strictly and continue to follow the prescribed norms in future also. Annexure – IV
vii.	Hazardous air pollutants (HAP) emitted from the process shall be identified; assessment shall be made both for stack/vent emissions and work zone environment /ambient environment.	Complied. Site made adequate provision for emission control systems. Site is monitoring stack emissions as well as ambient air on quarterly basis as stipulated in CTO condition. Site also monitor emissions at work zone environment. Refer Photocopy's of Reports attached as Annexure - I & III.
viii.	Air emissions of VOC from reactor vents, material loading and unloading, acid gases (halogen acids, SO ₂ , etc.) fugitive emissions from pumps, valves, tanks, shall be monitored and emission shall be controlled. All the reactor vents shall be connected with a scrubbing system. The scrubbing liquid shall be treated in ETP.	Complied. Site has made adequate provision for this and scrubbing liquid shall be treated in ETP MEE VTFD system, same will be implemented in future also.
ix.	The company shall undertake following Waste minimization measures: Metering and control of quantities of active ingredients to minimize waste. Reduce of by products from the process as raw materials or as raw material Substitute in other processes. Use of automated filling to minimize spillage. Use of "Close Feed" system into batch reactors. Venting equipment through vapor recovery system. Use of high-pressure hoses for equipment cleaning to reduce wastewater generation	Complied. Site has followed waste minimization measures and the same will be implemented in future also.
x.	The effluent generation expansion shall not increase 150 m ³ /d. Effluent shall be segregated into high and low COD streams. The low COD effluent after primary, secondary and tertiary treatment and meeting the norms shall be sent to CETP. The high COD effluent shall be evaporated in Multi Effect Evaporator & incinerated in the liquid - cum solid waste incineration system. The incinerator ash shall be disposed of in the TSDF.	Complied. Site has full-fledged ZLD plant. ETP of cap.-150 m ³ /day to treat low COD stream & treated effluent recycle and reused (100%) to utility (using RO System). High COD stream effluent treated in MEE and VTFD facility. Ref: Annexure-V and VI

xi.	The solid waste generated in the form of used /spent oil will be incinerated. Used spent solvent shall be sold to authorized reprocessor. Spent catalyst, expired medicines, spent mother liquor; chemical sludge, oil and ETP residue and sludge from the wet scrubber shall be incinerated. Spent solvents shall be sold to authorized reprocesses. The ash obtained after incineration shall be disposed of at TSDF developed by M/s Maharashtra Enviro Power Ltd. at Ranjangaon.	Complied. Site is complying these conditions and continue to comply in future. We are sending spent solvent to the authorized reprocessor. Photocopy of TSDF membership certificate Refer Annexure – IV
xii.	The company shall develop rainwater harvesting structures to harvest the runoff water for recharge of ground water.	Complied. Site has developed rainwater collection tank of approximate 25 m ³ size. The collected rainwater is being used for cooling tower makeup.
xiii.	Green belt shall be provided in an area of 33 percent of plant area to mitigate the effects of fugitive emissions all around the plant. Development of green belt shall be as per the Central Pollution Control Board guidelines.	Complied. Site has earmarked green belt area as per CPCB guideline and at present to complete the 33% GB of total plot area Cipla Limited has purchased land Gat. No. 27 at Roti Village approx. 3 Km from the existing plot (D-22) will be solely used for green belt development. Annexure-VII
xiv.	Occupational health surveillance of the workers shall be done on a regular basis and records maintained as per the Factories act.	Complied. A procedure has been put in place that all the employees undergo pre-employment medical checkup followed by yearly medical checkup from an approved & qualified doctor & records are maintained as per the factory's act. Ref. Annexure: VIII

B.	General Conditions:	Status
i.	The project authorities shall strictly adhere to the stipulations made by the Maharashtra Pollution Control Board.	Complied. Site complies & will continue to comply in future with the conditions made by the Maharashtra Pollution Control Board. Copy of Consent to operate attached as Ref. Annexure -IX and X.
ii.	At no time the emissions shall exceed the prescribed limits in the event of Failure of any Pollution control system adopted by the unit, the unit shall be immediately put off operation and shall not be restarted until the desired efficiency has been achieved.	Complied. Site maintains emissions as per prescribed limits and continue to follow in future also. The critical spare inventory is maintained to attend the breakdown of system. in the event of Failure of any Pollution control system

		adopted by the unit, the unit will be immediately put off operation and shall not be restarted until the desired efficiency has been achieved.
iii.	No further expansion or modifications in the plant shall be carried out without Prior approval of the Ministry of Environment and Forest. In case of deviations or alterations in the project proposal from those submitted to this Ministry for Clearance, a fresh reference shall be made to the Ministry to assess the Adequacy of conditions imposed and to add additional environmental protection Measures required, if any.	Complied. Site will seek prior approval of MOEF in case we undergo such an activity of Expansion or Modification.
iv.	The project authorities shall strictly comply with the rules and regulations Under Manufacture, storage and import of Hazardous Chemicals Rules, 1989 as amended in October 1994 and January 2000 & 2003 Authorization from the SPCB shall be obtained for collection, treatment, storage, and disposal of hazardous waste.	Complied. Site strictly comply with the rules and regulations and continue to follow them.
v.	The project authorization must strictly comply with the rules and regulations with regard to handling and disposal of hazardous wastes in accordance with the Hazardous Wastes (Management and Handling) Rules, 2003. Authorization from the state pollution Control Board must be obtained for collection /treatment /storage /disposal of hazardous wastes.	Complied. Site has already obtained Authorization from MPCB for collection / treatment / storage / disposal of hazardous wastes. Further, we are fully complying with HW (M&H) Rules, 2003 & 2008. The consent to operate is valid up to 30.04.2027. Refer Annexure IV & X.
vi.	The overall noise levels in and around the plant area shall be kept well within the standards (85 dBA) by providing noise control measures including acoustic hoods, silencers enclosures etc. on all sources of noise generation. The ambient noise levels shall conform to the standards prescribed under the Environment (Protection) Act, Rules, 1989 viz. and 70 dBA (nighttime).	Complied. Site has carried out ambient noise level survey of our plant. Site do not have any such process or equipment that adds to the ambient noise level. We will comply the standards under Environment (Protection) Act, Rules, 1989 in future also. Photocopy of Reports attached as Annexure - XI
vii.	The project proponent shall also comply with all the environmental protection measures and safeguards recommended in the EIA report.	Complied. Site is fully complying with these provisions & continue to comply in future also.
viii.	A separate Environmental Management Cell equipped with full-fledged laboratory facilities shall be set up to carry out the Environmental Management and Monitoring functions.	Complied. Site has already set-up EMC under control of Plant Manager and developed full-fledged ETP laboratory to support environmental monitoring functions. Copy of EMC attached as Annexure - XII

ix.	The project authorities shall earmark separate funds to implement the Conditions stipulated by the Ministry of Environment and Forest as well as the state Government along with the implementation schedule for all the conditions stipulated herein. The funds provided shall not be diverted for any other purpose.	Complied. Site has sufficient provision of funds for Environment protection & will make adequate provision for this. Annexure-XIII.
x.	The implementation of the project vis-à-vis environmental action plans shall be monitored by Ministry Regional Office at Bhopal / SPCB/ CPCB. A six-monthly compliance status report shall be submitted to monitoring agencies.	Complied. Site regularly submits six monthly compliance status reports to monitoring agencies and complies in future also. Annexure-XIV
xi.	The project proponent shall inform the public that the project has been accorded environmental clearance by the Ministry and copies of the clearance letter are available with the SPCB/Committee and may also be seen at website of the Ministry at http://envfor.nic.in . This shall be advertised within seven days from the date of issue of the clearance letter, at least in two local newspapers that are widely circulated in the vernacular language of locality concerned and a copy of the same shall be forwarded to the Ministry's Regional Office at Nagpur	Complied. Site already had given an advertisement on 26 th October 2005 in vernacular Language Newspaper (Loksatta) and in English News Paper (Indian Express). A copy of the same is enclosed herewith as Annexure-XV
xii.	The project authorities shall inform the regional office as well as the Ministry of the date of financial closure and final approval of the project by the concerned authorities and the date of start of the project.	Complied. Manufacturing activity of Completed project started in May 2014.

Monitoring the Implementation of Environmental Safeguards
Ministry of Environment & Forests
Regional Office (w), Bhopal.
Monitoring Report

PART – I

DATA SHEET

1. Project type: River –valley /Mining : Industry
Industry /Thermal /Nuclear/ other (specify)
2. Name of the project : Bulk Drug manufacturing Plant
3. Clearance letter (s) / OM no. and date : No. J -11011/47/2005 - IA II (I)
Dated 13th October, 2005
4. Location :
a) District (s) Pune
b) State (s) Maharashtra
c) Latitude/Longitude 18° 21' N / 74° 31' E
5. Address for correspondence:
a) Address of concerned project : Mr. Laxmikant Khedkar
Chef Engineer (with pin code & telephone : Cipla Limited
/ Fax numbers D -22, MIDC area Kurkumbh
Tal – Daund, Dist.: – Pune
Pin code - 413802
Tel No –02117-**230100**
Tel Fax-02117-**230232**
Email-
laxmikant.khedkar@cipla.com
- b) Address of Executive Project : Mr. Laxmikant Khedkar
Engineer/ Manager (with pin code/ : Cipla Limited
Fax numbers D –22, MIDC area Kurkumbh
Tal – Daund, Dist. – Pune
Pin code - 413802
Email :
laxmikant.khedkar@cipla.com
Tel No –02117-**230515**
Tel Fax-02117-230232
6. Salient features:
a) Of the project : Bulk drugs manufacturing plant
b) Of the environmental management plans : as per MPCB consent to
Operate norms vide letter No.
Format 1.0/CAC/UAN
No.0000200484/CR/2502000433

7. Breakup of the project area : Notified chemical zone by MIDC
a) Submergence area: forest & non-forest
b) Others
8. Breakup of the project affected population
With enumeration of those losing houses/
dwelling units only agricultural land only,
both dwelling unit & agricultural land &
landless laborer's/artisan : Nil
a) SC, ST/ Adivasis : Nil
b) Others
- (Please indicate whether these figures :
are based on any scientific and systematic.
survey is carried out or only provisional.
figures, if a survey is carried out give details.
and years of survey)
9. Financial details :
a) Project cost as originally planned and
subsequent revised estimates and the :
The year of price reference. As per Annexure -XIII
b) Allocation made for environmental.
management plans with item wise and
year wise break-up.
c) Benefit cost ratio/ Internal rate of return
And the year of assessment.
d) Whether (c) includes the cost of
environmental management as shown
in the above.
d) Actual expenditure incurred on the
Project so far :
e) Actual expenditure incurred on the
environmental management plans so far.
10. Forest land requirement : Nil
a) The status of approval for diversion of
forest land for non-forestry use.
b) The status of clearing felling. :
c) The status of compensatory afforestation,
if any. :
d) Comments on the viability & sustainability
of compensatory afforestation programmed
in the light of actual field experience so far. :
11. The status of clear felling in non-forest areas : Nil

(such as submergence area of reservoir, approach roads), if any with quantitative information

12. Status of construction :
 a) Date of commencement (Actual and/or planned) : Project completed in April-2013.
 b) Date of completion (Actual and /of planned): Phase I Manufacturing is Started from March 2008 Project completed. manufacturing started in May 2014.
13. Reasons for the delay if the project is yet to start :
14. Date of site visits : 12/12/ 2007
 a) The dates on which the project was monitored by the Regional office on Previous occasions, if any :
 b) Date of site visit for this monitoring report : -
15. Details of correspondence with project Authorities for obtaining action plans/ Information on status of compliance to Safeguards other than the routine letters for logistic support for site visits) : -
 (The first monitoring report may contain the details of all the letters issued so far, but the later reports may cover only the letters issued subsequently) :

Annexure-I



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS	REPORT NO.	HALPL/LAB/AA/16382
M/s Cipla Ltd.	REPORT DATE	05/03/2026
Plot No. D-22, Unit III MIDC Kurkumbh,	LAB REFERENCE NO.	HALPL/LAB/AA/704
Tal- Daund, Dist- Pune	SAMPLING DATE	26/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14/2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	TIME OF SAMPLING	LOCATION
Scrubber Monitoring	Horizon Services	Plastic Bottles and Bags	11:00 Hrs.	Process Vent 1 (BD-I) S 6

RESULTS

SR. NO	TEST DESCRIPTION	UNIT	RESULTS	MPCB LIMITS	METHOD OF SAMPLING AND ANALYSIS
1	ACID MIST (HCl)	mg/NM ³	5.9	35	HALPL/LAB/STK/01:2017
2	NO _x	ppm	BDL (<2.66)	N.S.	IS 11255 (Part 7)

Equipment Used: -1) Stack Monitoring Kit, Sr. No. 07/2018 (ETCL model)

Date of Calibration: -07/08/2025 Next Calibration due: - 06/08/2026

REMARKS/OBSERVATIONS:

N S -Not Specified



For HORIZON SERVICES

MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS	REPORT NO.
M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	HALPL/LAB/AA/16383
	REPORT DATE
	05/03/2026
	LAB REFERENCE NO.
	HALPL/LAB/AA/704
	SAMPLING DATE
	26/02/2026
	SAMPLE RECEIPT DATE
	27/02/2026
	START DATE OF ANALYSIS
	27/02/2026
	END DATE OF ANALYSIS
	04/03/2026
	SAMPLING REF. / SOP NO.
	HALPL/LAB/NABL/SAM/14-2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	TIME OF SAMPLING	LOCATION
Scrubber Monitoring	Horizon Services	Plastic Bottles and Bags	11 30 Hrs.	Process Vent 2 (BD-I) S 7

RESULTS

SR. NO	TEST DESCRIPTION	UNIT	RESULTS	MPCB LIMITS	METHOD OF SAMPLING AND ANALYSIS
1	ACID MIST (HCl)	mg/NM ³	6.2	35	HALPL/LAB/STK/01:2017
2	NO _x	ppm	BDL (<2.66)	N S	IS 11255 (Part 7)

Equipment Used: -1) Stack Monitoring Kit, Sr. No. 07/2018 (ETCL model)
Date of Calibration: -07/08/2025 Next Calibration due. - 06/08/2026

REMARKS/OBSERVATIONS: -
N.S.-Not Specified



For HORIZON SERVICES

MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

CLIENT'S NAME & ADDRESS M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	REPORT NO.	HALPL/LAB/NABL/F/7.8.2.1
	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/704
	SAMPLING DATE	26/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14:2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	TIME OF SAMPLING	LOCATION
Scrubber Monitoring	Horizon Services	Plastic Bottles and Bags	12.00 Hrs	Process Vent 3 (BD-II) S 8

RESULTS


SR. NO	TEST DESCRIPTION	UNIT	RESULTS	MPCB LIMITS	METHOD OF SAMPLING AND ANALYSIS
1	ACID MIST (HCl)	mg/NM ³	5.2	35	HALPL/LAB/STK/01:2017
2	NO _x	ppm	BDL (<2.66)	N.S.	IS 11255 (Part 7)

Equipment Used: -1) Stack Monitoring Kit, Sr. No. 07/2018 (ETCL model)

Date of Calibration: -07/08/2025 Next Calibration due: -06/08/2026

REMARKS/OBSERVATIONS:-

N.S.-Not Specified



For HORIZON SERVICES

MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email: kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	REPORT NO.	HALPL/LAB/AA/16385
	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/704
	SAMPLING DATE	26/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14.2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	TIME OF SAMPLING	LOCATION
Scrubber Monitoring	Horizon Services	Plastic Bottles and Bags	12:30 Hrs.	Process Vent 4 (BD-It) S 9

RESULTS

SR. NO	TEST DESCRIPTION	UNIT	RESULTS	MPCB LIMITS	METHOD OF SAMPLING AND ANALYSIS
1.	ACID MIST (HCl)	mg/NM ³	6.1	35	HALPL/LAB/STK/01:2017
2.	NO _x	ppm	BDL (<2.66)	N.S.	IS 11255 (Part 7)

Equipment Used: -1) Stack Monitoring Kit, Sr. No. 07/2018 (ETCL model)

Date of Calibration: -07/08/2025 Next Calibration due: - 06/08/2026

REMARKS/OBSERVATIONS: -

N.S.-Not Specified



For HORIZON SERVICES

MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.
• Mob.: 7249067318, 8378018710 • Email: kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7 8 2 1

CLIENT'S NAME & ADDRESS	REPORT NO.	HALPL/LAB/AA/16386
M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	REPORT DATE	05/03/2026
	LAB REFERENCE NO	HALPL/LAB/AA/704
	SAMPLING DATE	26/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14/2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	TIME OF SAMPLING	LOCATION
Scrubber Monitoring	Horizon Services	Plastic Bottles and Bags	13:00 Hrs	Process Vent 5 (BO-III) S 10

RESULTS

SR. NO	TEST DESCRIPTION	UNIT	RESULTS	MPCB LIMITS	METHOD OF SAMPLING AND ANALYSIS
1.	ACID MIST (HCl)	mg/NM ³	4.1	35	HALPL/LAB/STK/01/2017
2.	NO _x	ppm	BDL (<2.66)	N.S	IS 11255 (Part 7)

Equipment Used: -1) Stack Monitoring Kit, Sr. No. 07/2018 (ETCL model)
Date of Calibration: -07/08/2025 Next Calibration due: - 06/08/2026

REMARKS/OBSERVATIONS: -
N.S -Not Specified



For HORIZON SERVICES

MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

Shree, K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7 8.2.1

CLIENT'S NAME & ADDRESS	REPORT NO.	HALPL/LAB/AA/16387
M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/704
	SAMPLING DATE	26/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14.2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	TIME OF SAMPLING	LOCATION
Scrubber Monitoring	Horizon Services	Plastic Bottles and Bags	13:30 Hrs.	Process Vent 6 (BD-IV) S 11

RESULTS

SR. NO	TEST DESCRIPTION	UNIT	RESULTS	MPCB LIMITS	METHOD OF SAMPLING AND ANALYSIS
1	ACID MIST (HCl)	mg/NM ³	4.0	35	HALPL/LAB/STK/01 2017
2.	NO _x	ppm	BDL (<2.65)	N.S.	IS 11255 (Part 7)

Equipment Used: -1) Stack Monitoring Kit, Sr. No. 07/2018 (ETCL model)
Date of Calibration: -07/08/2025 Next Calibration due: - 06/08/2026

REMARKS/OBSERVATIONS. -

N.S -Not Specified



For HORIZON SERVICES

Manisha Nargolkar

MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

'Shree', K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.
• Mob.: 7249867318, 8378018710 • Email : kmr@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

CLIENT'S NAME & ADDRESS M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	REPORT NO.	HALPL/LAB/NABL/F/7 8.2.1
	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/704
	SAMPLING DATE	26/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14.2021


DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	TIME OF SAMPLING	LOCATION
Scrubber Monitoring	Horizon Services	Plastic Bottles and Bags	14:00 Hrs	Process Vent 7 (BD-IV) S 12

RESULTS

SR. NO	TEST DESCRIPTION	UNIT	RESULTS	MPCB LIMITS	METHOD OF SAMPLING AND ANALYSIS
1	ACID MIST (HCl)	mg/NM ³	3.8	35	HALPL/LAB/STK/01:2017
2	NO _x	ppm	BDL (<2.66)	N.S	IS 11255 (Part 7)

Equipment Used: -1) Stack Monitoring Kit, Sr. No. 07/2018 (ETCL model)
Date of Calibration: -07/08/2025 **Next Calibration due:** - 06/08/2026

REMARKS/OBSERVATIONS: -
N.S.-Not Specified



For HORIZON SERVICES

MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****

Annexure-II



Lab NABL Accredited - Chemical Field, (Valid till 16/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email: kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7 8 2.1

CLIENT'S NAME & ADDRESS	ULR NO.	TC1620826000016372
M/s Cipla Ltd.	REPORT DATE	05/03/2026
Plot No. D-22, Unit III MIDC	LAB REFERENCE NO.	HALPL/LAB/AA/704
Kurkumbh,	SAMPLING DATE	25&26/02/2026
Tal- Daund, Dist- Pune	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14/2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Air	Horizon Analytical Laboratory Pvt.Ltd.	Plastic Bottles and Bags	--	Near Main Gate

RESULTS

SR. NO.	DESCRIPTION	UNIT	RESULTS	NAAQS LIMITS	TEST METHOD REFERENCE
01	Date of Sampling	DD/MM/YY	25&26/02/2026		
02	Test Location		Near Main Gate		
03	Time of Sampling	Hrs	12:10		
04	Temperature (Max./Min)	De C	34/23		
05	Relative Humidity	% RH	47		
06	Sampling Duration	Hrs	24		
07	Respirable Suspended Particulate Matter (PM ₁₀)	µg/m ³	59.86	100	IS 5182(part 23)
08	Fine Particulate Matter (PM _{2.5})	µg/m ³	32.16	60	IS 5182(part 24)
09	Sulphur Dioxide as SO ₂	µg/m ³	14.80	80	IS 5182(part 2) : Sec 1
10	Nitrogen Dioxide as NO ₂	µg/m ³	29.05	80	IS 5182(part 6)
11	Ozone as O ₃	µg/m ³	13.60	100	IS 5182(part 9)
12	Ammonia as NH ₃	µg/m ³	BDL (<30)	400	IS 5182(part 25)
13	Lead as Pb	µg/m ³	BDL (<0.05)	1.0	IS 5182 (Part 22)
14	Arsenic as As	ng/m ³	BDL (<3)	06	HALPL/LAB/NABL/AA/22.2021
15	Nickel as Ni	ng/m ³	BDL (<7)	20	IS 5182(part 26)

Equipment Used: - Fine Dust Sampler, Sr No.2218 (Polltech Make)

Date of Calibration: -07/08/2025 Next Calibration due: -06/08/2026

REMARKS/OBSERVATIONS:-

NAAQS - National Ambient Air Quality Standards

Limits as per NAAQS Monitoring & Analysis Guidelines Volume-I (2009)

BDL-Below Detectable Level

For HORIZON ANALYTICAL LABORATORY PVT.LTD.



MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER

- Sample will be retained only for 15 days. • Above results indicate to the parameters mentioned only • Liability limited (in issue of test reports only)
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS	REPORT NO.	HALPL/LAB/AA/16372
M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/704
	SAMPLING DATE	25&26/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14.2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Air	Horizon Services	Plastic Bottles and Bags	—	Near Main Gate

RESULTS

SR. NO.	DESCRIPTION	UNIT	RESULTS	NAAQS LIMITS	TEST METHOD REFERENCE
01	Date of Sampling	DD/MM/YY	25&26/02/2026		
02	Test Location		Near Main Gate		
03	Time of Sampling	Hrs	12:10		
04	Temperature (Max./Min)	Deg C	34/23		
05	Relative Humidity	% RH	47		
06	Sampling Duration	Hrs	24		
07	Carbon monoxide as CO	mg/m ³	0.090	2.0	IS 5182 (Part 10)
08	Benzene as C ₆ H ₆	µg/m ³	BDL (<4)	05	IS 5182 (Part 11)
09	Benzo (a) Pyrene as Ba(a)P	ng/m ³	BDL (<0.5)	01	IS 5182 (Part 12)

REMARKS/OBSERVATIONS :

NAAQS: - National Ambient Air Quality Standards

Limits as per NAAQS Monitoring & Analysis Guidelines Volume-I (2009)

BDL-Below Detectable Level



For HORIZON SERVICES

Manisha Nargolkar

MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmm@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

CLIENT'S NAME & ADDRESS M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	ULR NO.	HALPL/LAB/NABL/F/7 8.2 1
	REPORT DATE	TC1620826000016373
	LAB REFERENCE NO.	05/03/2026
	SAMPLING DATE	HALPL/LAB/AA/704
	SAMPLE RECEIPT DATE	25&26/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	27/02/2026
	SAMPLING REF. / SOP NO.	04/03/2026
		HALPL/LAB/NABL/SAM/14-2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Air	Horizon Analytical Laboratory Pvt Ltd	Plastic Bottles and Bags	--	Near DG Set

RESULTS

SR. NO.	DESCRIPTION	UNIT	RESULTS	NAAQS LIMITS	TEST METHOD REFERENCE
01	Date of Sampling	DD/MM/YY	25&26/02/2026		
02	Test Location		Near DG Set		
03	Time of Sampling	Hrs.	12:40		
04	Temperature (Max./Min)	Deg C	34/23		
05	Relative Humidity	% RH	47		
06	Sampling Duration	Hrs	24		
07	Respirable Suspended Particulate Matter (PM ₁₀)	µg/m ³	59.06	100	IS 5182(part 23)
08	Fine Particulate Matter (PM _{2.5})	µg/m ³	31.51	60	IS 5182(part 24)
09	Sulphur Dioxide as SO ₂	µg/m ³	12.80	80	IS 5182(part 2) : Sec.1
10	Nitrogen Dioxide as NO ₂	µg/m ³	25.10	80	IS 5182(part 8)
11	Ozone as O ₃	µg/m ³	10.62	100	IS 5182(part 9)
12	Ammonia as NH ₃	µg/m ³	BDL (<30)	400	IS 5182(part 25)
13	Lead as Pb	µg/m ³	BDL (<0.05)	1.0	IS 5182 (Part 22)
14	Arsenic as As	ng/m ³	BDL (<3)	06	HALPL/LAB/NABL/AA/22: 2021
15	Nickel as Ni	ng/m ³	BDL (<7)	20	IS 5182(part 26)

Equipment Used: - Fine Dust Sampler, Sr.No.2419 (Politech Make)

Date of Calibration: -07/08/2025 Next Calibration due: -06/08/2026

REMARKS/OBSERVATIONS:-

NAAQS:- National Ambient Air Quality Standards

Limits as per NAAQS Monitoring & Analysis Guidelines Volume-I (2009)

BDL-Below Detectable Level

For HORIZON ANALYTICAL LABORATORY PVT.LTD.



MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER:

- Sample will be retained only for 15 days.
- Above results indicate to the parameters mentioned only.
- Liability limited till issue of test reports only
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.
• Mob : 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	REPORT NO.	HALPL/LAB/AA/16373
	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/704
	SAMPLING DATE	25&26/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14.2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Air	Horizon Services	Plastic Bottles and Bags	--	Near DG Set

RESULTS


SR. NO.	DESCRIPTION	UNIT	RESULTS	NAAQS LIMITS	TEST METHOD REFERENCE
01	Date of Sampling	DD/MM/YY	25&26/02/2026		
02	Test Location		Near DG Set		
03	Time of Sampling	Hrs.	12:40		
04	Temperature (Max./Min)	De C	34/23		
05	Relative Humidity	% RH	47		
06	Sampling Duration	Hrs	24		
07	Carbon monoxide as CO	mg/m ³	0.081	2.0	IS 5182 Part 10
08	Benzene as C ₆ H ₆	µg/m ³	BDL (<4)	05	IS 5182 Part 11
09	Benzo (a) Pyrene as Ba(a)P	ng/m ³	BDL (<0.5)	01	IS 5182 Part 12

REMARKS/OBSERVATIONS:-

NAAQS:- National Ambient Air Quality Standards

Limits as per NAAQS Monitoring & Analysis Guidelines Volume-I (2009)

BDL-Below Detectable Level



For HORIZON SERVICES

MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / rnd@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7 B 2 1

CLIENT'S NAME & ADDRESS	ULR NO.	TC1620826000016374
M/s Cipla Ltd.	REPORT DATE	05/03/2026
Plot No. D-22, Unit III MIDC Kurkumbh,	LAB REFERENCE NO.	HALPL/LAB/AA/704
Tal- Daund, Dist- Pune	SAMPLING DATE	26&27/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14:2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Air	Horizon Analytical Laboratory Pvt.Ltd.	Plastic Bottles and Bags	--	Near BD-III DP Store

RESULTS

SR. NO.	DESCRIPTION	UNIT	RESULTS	NAAQS LIMITS	TEST METHOD REFERENCE
01	Date of Sampling	DD/MM/YY	26&27/02/2026		
02	Test Location		Near BD-III DP Store		
03	Time of Sampling	Hrs	14:15		
04	Temperature (Max./Min)	Deg C	34/21		
05	Relative Humidity	% RH	48		
06	Sampling Duration	Hrs	24		
07	Respirable Suspended Particulate Matter (PM ₁₀)	µg/m ³	61.37	100	IS 5182(part 23)
08	Fine Particulate Matter (PM _{2.5})	µg/m ³	32.56	60	IS 5182(part 24)
09	Sulphur Dioxide as SO ₂	µg/m ³	15.02	80	IS 5182(part 2) : Sec. 1
10	Nitrogen Dioxide as NO ₂	µg/m ³	28.10	80	IS 5182(part 6)
11	Ozone as O ₃	µg/m ³	13.97	100	IS 5182(part 9)
12	Ammonia as NH ₃	µg/m ³	BDL (<30)	400	IS 5182(part 25)
13	Lead as Pb	µg/m ³	BDL (<0.05)	1.0	IS 5182 (Part 22)
14	Arsenic as As	ng/m ³	BDL (<3)	06	HALPL/LAB/NABL/AA/22:2021
15	Nickel as Ni	ng/m ³	BDL (<7)	20	IS 5182(part 26)

Equipment Used: - Fine Dust Sampler, Sr.No.2218 (Politech Make)

Date of Calibration: -07/08/2025 Next Calibration due: -06/08/2026

REMARKS/OBSERVATIONS: -

NAAQS - National Ambient Air Quality Standards

Limits as per NAAQS Monitoring & Analysis Guidelines Volume-I (2009)

BDL-Below Detectable Level

For HORIZON ANALYTICAL LABORATORY PVT.LTD.



MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

End of Test Report

DISCLAIMER.

- Sample will be retained only for 15 days.
- Above results indicate to the parameters mentioned only.
- Liability limited till issue of test reports only
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandwane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7 8.2.1

CLIENT'S NAME & ADDRESS	REPORT NO.	HALPL/LAB/AA/16374
	REPORT DATE	05/03/2026
M/s Cipla Ltd.	LAB REFERENCE NO.	HALPL/LAB/AA/704
Plot No. D-22, Unit III MIDC Kurkumbh,	SAMPLING DATE	26&27/02/2026
Tal- Daund, Dist- Pune	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14.2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Air	Horizon Services	Plastic Bottles and Bags	~	Near BD-III DP Store

RESULTS

SR. NO.	DESCRIPTION	UNIT	RESULTS	NAAQS LIMITS	TEST METHOD REFERENCE
01	Date of Sampling	DD/MM/YY	26&27/02/2026		
02	Test Location		Near BD-III DP Store		
03	Time of Sampling	Hrs.	14:15		
04	Temperature (Max /Min)	De C	34/21		
05	Relative Humidity	% RH	48		
06	Sampling Duration	Hrs	24		
07	Carbon monoxide as CO	mg/m ³	0.097	2.0	IS 5182 (Part 10)
08	Benzene as C ₆ H ₆	mg/m ³	BDL (<4)	05	IS 5182 (Part 11)
09	Benzo [a] Pyrene as Ba[a]P	ng/m ³	BDL (<0.5)	01	IS 5182 (Part 12)

REMARKS/OBSERVATIONS:-

NAAQS - National Ambient Air Quality Standards

Limits as per NAAQS Monitoring & Analysis Guidelines Volume-I (2009)

BDL-Below Detectable Level



For HORIZON SERVICES

Manisha Nargolkar

MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawate Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7 8 2.1

CLIENT'S NAME & ADDRESS	ULR NO.	REPORT DATE
M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	TC162082600016375	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/704
	SAMPLING DATE	26&27/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14.2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Air	Horizon Analytical Laboratory Pvt.Ltd.	Plastic Bottles and Bags	--	Near BD-IV

RESULTS

SR. NO.	DESCRIPTION	UNIT	RESULTS	NAAQS LIMITS	TEST METHOD REFERENCE
01	Date of Sampling	DD/MM/YY	26&27/02/2026		
02	Test Location		Near BD-IV		
03	Time of Sampling	Hrs	14:45		
04	Temperature (Max./Min)	De C	34/21		
05	Relative Humidity	% RH	48		
06	Sampling Duration	Hrs	24		
07	Respirable Suspended Particulate Matter (PM ₁₀)	µg/m ³	61.37	100	IS 5182(part 23)
08	Fine Particulate Matter (PM _{2.5})	µg/m ³	35.29	60	IS 5182 (part 24)
09	Sulphur Dioxide as SO ₂	µg/m ³	15.12	80	IS 5182 (part 2) . Sec. 1
10	Nitrogen Dioxide as NO ₂	µg/m ³	29.09	80	IS 5182(part 6)
11	Ozone as O ₃	µg/m ³	12.10	100	IS 5182 (part 9)
12	Ammonia as NH ₃	µg/m ³	BDL (<30)	400	IS 5182 (part 25)
13	Lead as Pb	µg/m ³	BDL (<0.05)	1.0	IS 5182 (Part 22)
14	Arsenic as As	ng/m ³	BDL (<3)	06	HALPL/LAB/NABL/AA/22.2021
15	Nickel as Ni	ng/m ³	BDL (<7)	20	IS 5182(part 26)

Equipment Used: - Fine Dust Sampler, Sr.No 2419 (Politech Make)

Date of Calibration: -07/08/2025 Next Calibration due: -06/08/2026

REMARKS/OBSERVATIONS:-

NAAQS: - National Ambient Air Quality Standards

Limits as per NAAQS Monitoring & Analysis Guidelines Volume-I (2009)

BDL-Below Detectable Level

For HORIZON ANALYTICAL LABORATORY PVT.LTD.



Manisha Nargolkar
MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER:

- Sample will be retained only for 15 days.
- Above results indicate to the parameters mentioned only
- Liability limited till issue of last reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS	REPORT NO.	HALPL/LAB/AA/16375
M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/704
	SAMPLING DATE	26&27/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14.2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Air	Horizon Services	Plastic Bottles and Bags	---	Near BD-IV

RESULTS

SR. NO.	DESCRIPTION	UNIT	RESULTS	NAAQS LIMITS	TEST METHOD REFERENCE
01	Date of Sampling	DD/MM/YY	26&27/02/2026		
02	Test Location		Near BD-IV		
03	Time of Sampling	Hrs.	14:45		
04	Temperature (Max./Min)	Deg C	34/21		
05	Relative Humidity	% RH	48		
06	Sampling Duration	Hrs	24		
07	Carbon monoxide as CO	mg/m ³	0.091	2.0	IS 5182 (Part 10)
08	Benzene as C ₆ H ₆	µg/m ³	BDL (<4)	05	IS 5182 (Part 11)
09	Benzo (a) Pyrene as Ba(a)P	ng/m ³	BDL (<0.5)	01	IS 5182 (Part 12)

REMARKS/OBSERVATIONS: -

NAAQS: - National Ambient Air Quality Standards

Limits as per NAAQS Monitoring & Analysis Guidelines Volume-I (2009)

BDL-Below Detectable Level

For HORIZON SERVICES



MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****

Annexure-III



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004

• Mob.: 7249867318, 8378018710 • Email: kmm@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 2

HALPL/LAB/NABL/F/7 8.2.1

CLIENT'S NAME & ADDRESS	ULR NO.	TC1620826000016376
M/s Cipla Ltd.	REPORT DATE	05/03/2026
Plot No. D-22, Unit III MIDC	LAB REFERENCE NO.	HALPL/LAB/AA/704
Kurkumbh,	SAMPLING DATE	25/02/2026
Tal- Daund, Dist- Pune	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14 2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Stack Emission	Horizon Analytical Laboratory Pvt Ltd.	Plastic Bottles and Bags	--	DG Set No. 5 750 KVA

RESULTS OF ANALYSIS

SR. NO.	DESCRIPTION	UNIT	RESULT	LIMITS	METHODS USED
01	Date Of Sampling	DD/MM/YY	25/02/2026		
02	Test Location		DG Set No. 5 750 KVA		
03	Time Of Sampling (00.00)	Hrs	13.10		
04	Material Of Stack		MS		
05	Stack Height	Mtr	6		
06	Type Of Fuel Used	--	Diesel		
07	Type Of Stack		Round		
08	Flue Gas Temperature	Deg K	395		
09	Differential Pressure	mm WG	3.0		
10	Velocity	m/Sec	6.71		
11	Diameter Of Stack	m	0.2		
12	Stack Area	m ²	0.0314		
13	Gas Volume	Nm ³ /Hr	572.46		
14	Particulate Matter as PM	mg/Nm ³	28.64	≤150	IS 11255 (Part 1)
		g/kw-hr	0.027	≤0.2*	--
15	Sulphur Dioxide as SO ₂	mg/Nm ³	25.20	--	IS 11255 (Part 2)
		Kg/Day	0.35	--	--
		ppm	18	N.S	IS 11255 (Part 7)
16	Oxides of Nitrogen (NOx)	g/kw-hr	0.032	≤4.0*	--
		mg/Nm ³	25.13	--	--
		ppm	25	N.S.	HALPL/LAB/NABL/STK/26:2017
17	Carbon Monoxide as CO	g/kw-hr	0.027	≤3.5*	--
18	Carbon Dioxide as CO ₂	%	6.3	N.S	HALPL/LAB/NABL/STK/09:2017

DISCLAIMER:

- Sample will be retained only for 15 days.
- Above results indicate to the parameters mentioned only
- Liability limited till issue of last reports only
- The test report shall not be produced for any legal identity or advertised without permission of lab



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

Shree, K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

* Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

Page 2 of 2

Equipment Used: -1) Stack Monitoring Kit, Sr. No. 07/2018 (ETCL model)

Date of Calibration: -07/08/2025 Next Calibration due: - 06/08/2026

**Remarks: - ** Standards are given as per the Gazette of India, G.S.R 771(E)
dated 11th December, 2013**

Monitoring results are well within the norms as specified by standards.

NS – Not Specified

For **HORIZON ANALYTICAL LABORATORY PVT.LTD.**



**MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)**

******End of Test Report******

DISCLAIMER:

- Sample will be retained only for 15 days. • Above results indicate to the parameters mentioned only. • Liability limited till issue of test reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

Shree, K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 2

HALPL/LAB/NABL/F/7 8.2.1

CLIENT'S NAME & ADDRESS M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	ULR NO.	TC1620826000016377
	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/704
	SAMPLING DATE	25/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14:2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Stack Emission	Horizon Analytical Laboratory Pvt Ltd.	Plastic Bottles and Bags	--	DG Set No. 4 750 KVA

RESULTS OF ANALYSIS

SR. NO.	DESCRIPTION	UNIT	RESULT	LIMITS	METHODS USED
01	Date Of Sampling	DD/MM/YY	25/02/2026		
02	Test Location		DG Set No. 4 750 KVA		
03	Time Of Sampling (00 00)	Hrs	13 30		
04	Material Of Stack		MS		
05	Stack Height	Mtr	6		
06	Type Of Fuel Used	--	Diesel		
07	Type Of Stack		Round		
08	Flue Gas Temperature	De ^o K	388		
09	Differential Pressure	mm WG	3.3		
10	Velocity	m/Sec	6.98		
11	Diameter Of Stack	m	0.2		
12	Stack Area	m ²	0.0314		
13	Gas Volume	Nm ³ /Hr	605.79		
14	Particulate Matter as PM	mg/Nm ³	9.06	≤150	IS 11255 (Part 1)
		g/kw-hr	0.009	≤0.2*	--
15	Sulphur Dioxide as SO ₂	mg/Nm ³	BDL (<2)	--	IS 11255 (Part 2)
		Kg/Day	NIL	--	--
		ppm	13.0	N S	IS 11255 (Part 7)
16	Oxides of Nitrogen (NO _x)	g/kw-hr	0.025	≤4.0*	--
		mg/Nm ³	24.46	--	--
17	Carbon Monoxide as CO	ppm	7.8	N S	HALPL/LAB/NABL/STK/26-2017
		g/kw-hr	0.009	≤3.5*	--
18	Carbon Dioxide as CO ₂	%	2.9	N S	HALPL/LAB/NABL/STK/09:2017

DISCLAIMER:

- Sample will be retained only for 15 days.
- Above results indicate to the parameters mentioned only
- Liability limited till issue of test reports only
- The test report shall not be produced for any legal identity or advertised without permission of lab



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

Page 2 of 2

Equipment Used: -1) Stack Monitoring Kit, Sr. No. 07/2018 (ETCL model)
Date of Calibration: -07/08/2025 **Next Calibration due:** - 06/08/2026

Remarks: - ** Standards are given as per the Gazette of India, G.S.R. 771(E)
dated 11th December, 2013

Monitoring results are well within the norms as specified by standards

NS – Not Specified

For HORIZON ANALYTICAL LABORATORY PVT.LTD.



MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER.

- Sample will be retained only for 15 days
- Above results indicate to the parameters mentioned only
- Liability limited till issue of test reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Steep", K 3/4, S. No. 10, Grandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004

• Mob : 7249867318 8378018710 • Email : kmo@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7 8.2.1

CLIENT'S NAME & ADDRESS	ULR NO.	TC1620826000016378
M/s Cipla Ltd.	REPORT DATE	05/03/2026
Plot No. D-22, Unit III MIDC	LAB REFERENCE NO.	HALPL/LAB/AA/704
Kurkumbh,	SAMPLING DATE	27/02/2026
Tal- Daund, Dist- Pune	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14.2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Stack Emission	Horizon Analytical Laboratory Pvt.Ltd.	Plastic Bottles and Bags	--	Thermopack W-1701 A (S-1)

RESULTS OF ANALYSIS

SR. NO.	DESCRIPTION	UNIT	RESULT	LIMITS	METHODS USED
01	Date Of Sampling	DD/MM/YY	27/02/2026		
02	Test Location		Thermopack W-1701 A (S-1)		
03	Time Of Sampling (00.00)	Hrs	11:30		
04	Material Of Stack		MS		
05	Stack Height	Mtr	30		
06	Type Of Fuel Used	--	HSD		
07	Type Of Stack		Round		
08	Flue Gas Temperature	Deg K	409		
09	Differential Pressure	mm WG	2.1		
10	Velocity	m/Sec	5.71		
11	Diameter Of Stack	m	0.3		
12	Stack Area	m ²	0.0707		
13	Gas Volume	Nm ³ /Hr	1059.04		
14	Particulate Matter as PM	mg/Nm ³	31.09	≤150	IS 11255 (Part 1)
15	Sulphur Dioxide as SO ₂	mg/Nm ³	26.12	--	IS 11255 (Part 2)
		Kg/Day	0.66	--	--
16	Oxides of Nitrogen (NOx)	ppm	23.0	N.S	IS 11255 (Part 7)
		mg/Nm ³	43.27	--	--
17	Carbon Monoxide as CO	ppm	25.0	N.S	HALPL/LAB/NABL/STK/26-2017
18	Carbon Dioxide as CO ₂	%	9.2	N.S	HALPL/LAB/NABL/STK/09-2017

Equipment Used: -1) Stack Monitoring Kit, Sr. No. 07/2018 (ETCL model)

Date of Calibration: -07/08/2025 Next Calibration due: - 06/08/2026

REMARKS/OBSERVATIONS:-

N.S.-Not Specified

For HORIZON ANALYTICAL LABORATORY PVT.LTD.



Manisha Nargolkar
MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER:

- Sample will be retained only for 15 days
- Above results indicate to the parameters mentioned only
- Liability limited till issue of test reports only
- The test report shall not be produced for any legal identity or advertised without permission of lab



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob : 7249867318, 8378018710 • Email : knn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS	ULR NO.	TC1620826000016379
M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/704
	SAMPLING DATE	27/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14:2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Stack Emission	Horizon Analytical Laboratory Pvt.Ltd.	Plastic Bottles and Bags	--	Thermopack II W-1701 B

RESULTS OF ANALYSIS

SR. NO.	DESCRIPTION	UNIT	RESULT	LIMITS	METHODS USED
01	Date Of Sampling	DD/MM/YY	27/02/2026		
02	Test Location		Thermopack II W-1701 B		
03	Time Of Sampling (00 00)	Hrs	12:30		
04	Material Of Stack		MS		
05	Stack Height	Mtr	30		
06	Type Of Fuel Used	--	HSD		
07	Type Of Stack		Round		
08	Flue Gas Temperature	Deg K	406		
09	Differential Pressure	mm WG	2.2		
10	Velocity	m/Sec	5.63		
11	Diameter Of Stack	m	0.3		
12	Stack Area	m ²	0.0707		
13	Gas Volume	Nm ³ /Hr	1087.96		
14	Particulate Matter as PM	mg/Nm ³	35.17	≤150	IS 11255 (Part 1)
15	Sulphur Dioxide as SO ₂	mg/Nm ³	40.81	--	IS 11255 (Part 2)
		Kg/Day	1.07	--	--
16	Oxides of Nitrogen (NOx)	ppm	25.0	N.S	IS 11255 (Part 7)
		mg/Nm ³	47.03	--	--
17	Carbon Monoxide as CO	ppm	33.0	N.S	HALPL/LAB/NABL/STK/26:2017
18	Carbon Dioxide as CO ₂	%	8.9	N.S	HALPL/LAB/NABL/STK/09:2017

Equipment Used: -1) Stack Monitoring Kit, Sr. No. 07/2018 (ETCL model)

Date of Calibration: -07/08/2025 Next Calibration due: - 05/08/2026

REMARKS/OBSERVATIONS:-

N.S.-Not Specified

For HORIZON ANALYTICAL LABORATORY PVT.LTD.



MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER:

- Sample will be retained only for 15 days
- Above results indicate to the parameters mentioned only
- Liability limited till issue of test reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249567318, 8378018710 • Email: kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS	ULR NO.	TC1620826000016380
M/s Cipla Ltd.	REPORT DATE	05/03/2026
Plot No. D-22, Unit III MIDC Kurkumbh,	LAB REFERENCE NO.	HALPL/LAB/AA/704
Tal- Daund, Dist- Pune	SAMPLING DATE	27/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14/2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Stack Emission	Horizon Analytical Laboratory Pvt.Ltd.	Plastic Bottles and Bags	--	Boiler No. 01 2 TPH MR 15855 B-01

RESULTS OF ANALYSIS

SR. NO.	DESCRIPTION	UNIT	RESULT	LIMITS	METHODS USED
01	Date Of Sampling	DD/MM/YY	27/02/2026		
02	Test Location		Boiler No. 01 2 TPH MR 15855 B-01		
03	Time Of Sampling (00.00)	Hrs	14:00		
04	Material Of Stack		MS		
05	Stack Height	Mtr	33		
06	Type Of Fuel Used	--	LSHS		
07	Type Of Stack		Round		
08	Flue Gas Temperature	De K	399		
09	Differential Pressure	mm WG	3.0		
10	Velocity	m/Sec	6.75		
11	Diameter Of Stack	m	0.76		
12	Stack Area	m ²	0.4534		
13	Gas Volume	Nm ³ /Hr	8224.78		
14	Particulate Matter as PM	mg/Nm ³	26.34	≤150	IS 11255 (Part 1)
15	Sulphur Dioxide as SO ₂	mg/Nm ³	121.08	--	IS 11255 (Part 2)
		Kg/Day	23.90	--	--
16	Oxides of Nitrogen (NO _x)	ppm	28.0	--	IS 11255 (Part 7)
		mg/Nm ³	52.68	--	--
17	Carbon Monoxide as CO	ppm	51.0	N.S.	HALPL/LAB/NABL/STK/26/2017
18	Carbon Dioxide as CO ₂	%	8.9	N.S.	HALPL/LAB/NABL/STK/09/2017

Equipment Used: -1) Stack Monitoring Kit, Sr. No. 07/2018 (ETCL model)

Date of Calibration: -07/08/2025 Next Calibration due: - 05/08/2026

REMARKS/OBSERVATIONS. -

N.S.-Not Specified

For HORIZON ANALYTICAL LABORATORY PVT.LTD.



MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER

- Sample will be retained only for 15 days
- Above results indicate to the parameters mentioned only
- Liability limited till issue of test reports only
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree" K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.
• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS	REPORT NO.	HALPL/LAB/AA/15380
M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	REPORT DATE	05/03/2025
	LAB REFERENCE NO.	HALPL/LAB/AA/704
	SAMPLING DATE	27/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14 2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Stack Emission	Horizon Services	Plastic Bottles and Bags	---	Boiler No. 01 2 TPH MR 15855 B-01

RESULTS OF ANALYSIS

SR. NO.	DESCRIPTION	UNIT	RESULT	LIMITS	METHODS USED
01	Date Of Sampling	DD/MM/YY	27/02/2026		
02	Test Location		Boiler No. 01 2 TPH MR 15855 B-01		
03	Time Of Sampling (00.00)	Hrs	14:00		
04	Material Of Stack		MS		
05	Stack Height	Mtr	33		
06	Type Of Fuel Used	---	LSHS		
07	Type Of Stack		Round		
08	Flue Gas Temperature	Deg K	399		
09	Differential Pressure	mm WG	3.0		
10	Velocity	M/Sec	6.75		
11	Diameter Of Stack	M	0.76		
12	Stack Area	M ²	0.4534		
13	Gas Volume	Nm ³ /Hr	8224.78		
14	Combustion Efficiency	%	99.94	N.S.	HALPL/LAB/STK/09 :2017

REMARKS/OBSERVATIONS: -
N S -Not Specified



For HORIZON SERVICES

MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob : 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7 8.2.1

CLIENT'S NAME & ADDRESS M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	ULR NO.	TC1620826000016381
	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/704
	SAMPLING DATE	27/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14/2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Stack Emission	Horizon Analytical Laboratory Pvt.Ltd.	Plastic Bottles and Bags	--	Boiler No. 02 2 TPH G-151 B-02

RESULTS OF ANALYSIS

SR. NO.	DESCRIPTION	UNIT	RESULT	LIMITS	METHODS USED
01	Date Of Sampling	DD/MM/YY	27/02/2026		
02	Test Location		Boiler No. 02 2 TPH G-151 B-02		
03	Time Of Sampling (00:00)	Hrs	13.15		
04	Material Of Stack		MS		
05	Stack Height	Mtr	33		
06	Type Of Fuel Used	--	LSHS		
07	Type Of Stack		Round		
08	Flue Gas Temperature	Dej K	371		
09	Differential Pressure	mm WG	2.0		
10	Velocity	m/Sec	5.31		
11	Diameter Of Stack	m	0.76		
12	Stack Area	m ²	0.4534		
13	Gas Volume	Nm ³ /Hr	6964.31		
14	Particulate Matter as PM	mg/Nm ³	32.16	≤150	IS 11255 (Part 1)
		mg/Nm ³	115.64	--	IS 11255 (Part 2)
15	Sulphur Dioxide as SO ₂	Kg/Day	19.33	--	
		ppm	31.0	--	IS 11255 (Part 7)
16	Oxides of Nitrogen (NO _x)	mg/Nm ³	58.32	--	
17	Carbon Monoxide as CO	ppm	49.0	N.S	HALPL/LAB/NABL/STK/26 2017
18	Carbon Dioxide as CO ₂	%	8.8	N.S	HALPL/LAB/NABL/STK/09/2017

Equipment Used: -1) Stack Monitoring Kit, Sr No 07/2018 (ETCL model)

Date of Calibration: -07/08/2025 Next Calibration due: -06/08/2026

REMARKS/OBSERVATIONS:

N.S.-Not Specified

For HORIZON ANALYTICAL LABORATORY PVT.LTD.



MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

End of Test Report

DISCLAIMER:

- Sample will be retained only for 15 days. • Above results indicate to the parameters mentioned only. • Liability limited till issue of test reports only
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	REPORT NO.	HALPL/LAB/AA/16381
	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/704
	SAMPLING DATE	27/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14/2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Stack Emission	Horizon Services	Plastic Bottles and Bags	--	Boiler No. 02 2 TPH G-151 B-02

RESULTS OF ANALYSIS

SR. NO.	DESCRIPTION	UNIT	RESULT	LIMITS	METHODS USED
01	Date Of Sampling	DD/MM/YY	27/02/2026		
02	Test Location		Boiler No 02 2 TPH G-151 B-02		
03	Time Of Sampling (00.00)	Hrs	13.15		
04	Material Of Stack		MS		
05	Stack Height	Mtr	33		
06	Type Of Fuel Used	--	LSHS		
07	Type Of Stack		Round		
08	Flue Gas Temperature	Deg K	371		
09	Differential Pressure	mm WG	2.0		
10	Velocity	M/Sec	5.31		
11	Diameter Of Stack	M	0.76		
12	Stack Area	M ²	0.4534		
13	Gas Volume	Nm ³ /Hr	6964.31		
14	Combustion Efficiency	%	99.94	N.S	HALPL/LAB/STK/09 .2017

REMARKS/OBSERVATIONS:-

N.S -Not Specified



For HORIZON SERVICES

Manisha Nargolkar

MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****

Annexure-IV

MAHARASHTRA
ENVIRO POWER LTD
ISO 9001:2015 / EMS 14001:2004 / OHSAS 18001:2007 Certified Company
(Common Hazardous Waste Treatment, Storage and Disposal Facility)
The Corporate Identity Number (CIN) : UAC105MH2205PLC150783



Doc No.: SMS/MEPL/IMS/MKT/PMC
Issue/Rev. No.: 04/00
Rev. Date: 01.02.2020

MAHARASHTRA
ENVIRO POWER LTD

This is to certify that: M/S. CIPLA LTD.
Address: UNIT III, D - 22, MIDC Kurkumbh, Tal.- Daund, Dist. - Pune
413802 a Valid member of CHWTSDF (As per MOU with MIDC & MPCB),
at Plot No. P-56, Ranjangaon MIDC, Taluka - Shirur, Pune - 412 220.

Membership No. : MEPL/33002825

Membership Period: 21 September 2022 to 20 September 2027

For Maharashtra Enviro Power Ltd.


Authorized signatory


Marketing Coordinator



CHWTSDF : Plot No. P-56, Ranjangaon, Tal. Shirur, Dist. Pune. Pin - 412220 Ph : +91 - 92046421100

Pune Office : 301, Pentagon, P-3, Magarpatta Township, Hadapsar
Pune 411 028. Email : India Ph : +91-020-65421100
Email : info@mahenviro.com Web : www.mahenviro.com / www.mepco.in


Regd. Office : 207, Ganesh Prashasti, Bhandari, New Bhandari, Pune
Dharampeth, Nagpur. Ph : +91-0712-265192/55 Telefax : +91-0712-265192/55

Marketing Office (Atty): Bhandari Bazar Commercial Complex, 1st/2nd Floor, Near API Corner,
MIDC Area, Chhatrapati, Aurangabad - 431210 Ph : +91 206 2473047

Corporate Office : 20, 11 Park, Pashadi, Nagpur - 460022
Ph : +91-0712-6665000 Telefax : +91-0712-6665100 Web : www.smt.co.in

"An Environmental Laboratory Accredited by NABL, ISO/IEC 17025:2005 TC-5139 & Recognized by MoEF&CC"

Annexure-V

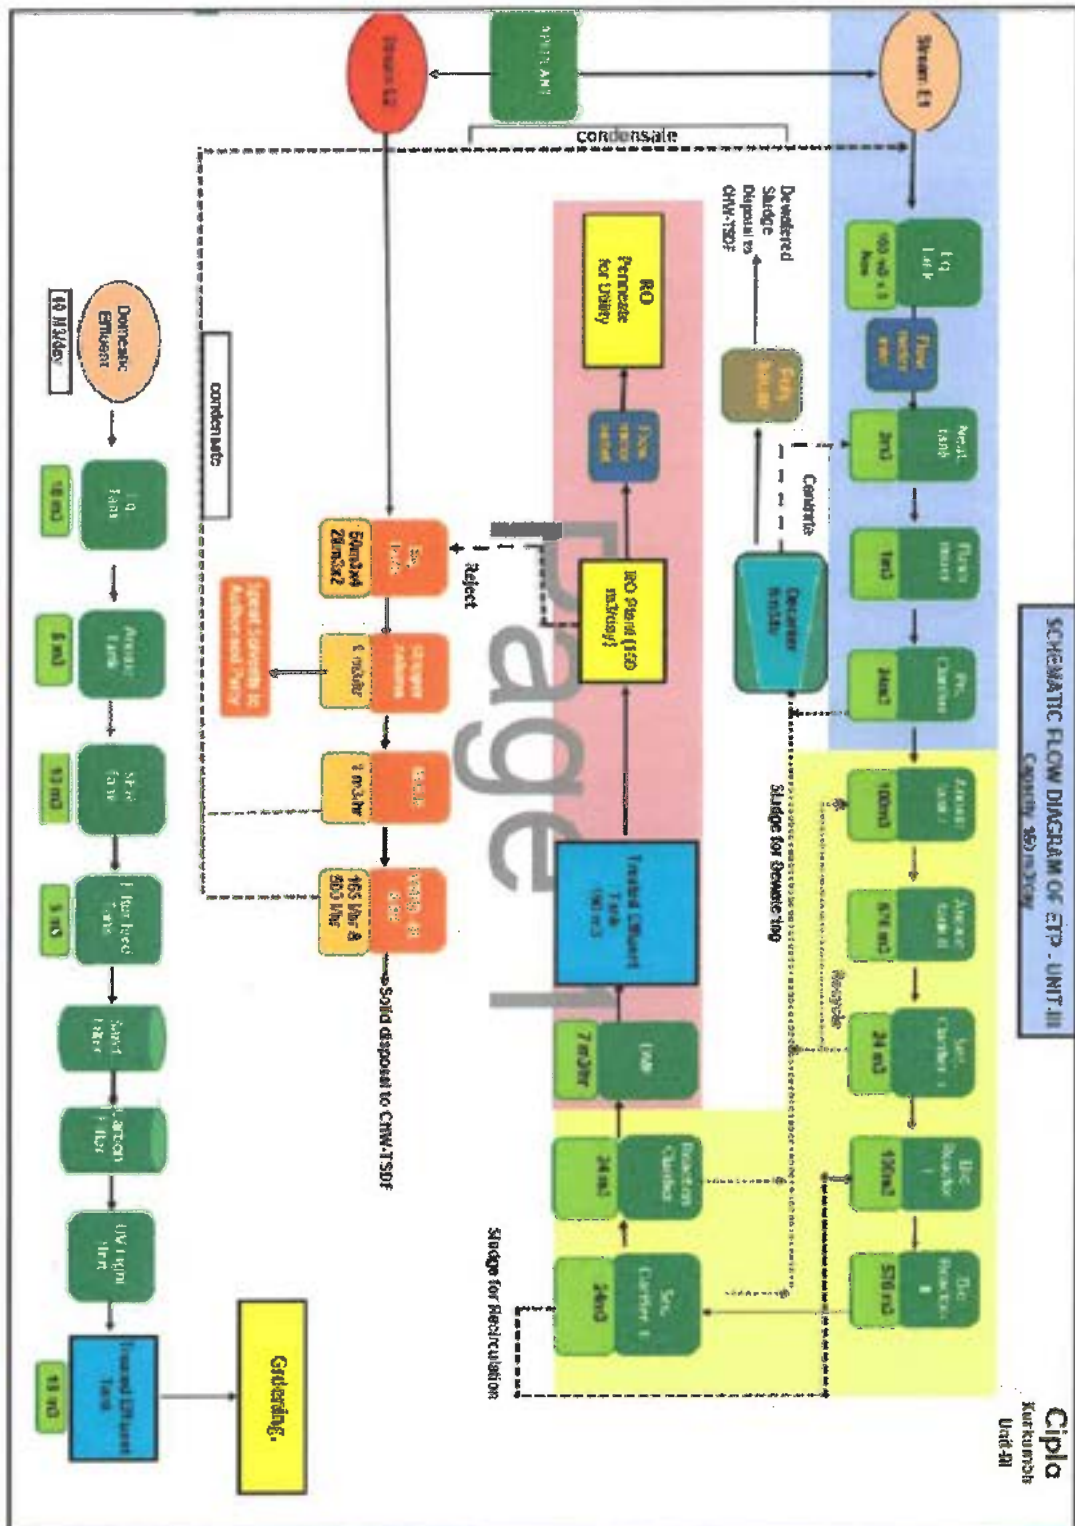


Annexure-VI

Effluent generation record			
Month	Weak COD/TDS stream (M3/d)	Domestic Effluent Quantity (M3/d)	Strong COD/TDS stream (M3/d)
Dec.25	42.55	4.15	14.66
Jan.26	40.19	4.19	11.72
Feb.26	39.71	4.27	12.47
Mar.26	38.26	4.20	11.60
Apr.26	37.63	4.25	12.47
May.26	38.16	4.28	11.02

Annexure-VII



 महाराष्ट्र साकार गोवंद नमुना सारित (अधिकार अभिलेख पत्रक) [महाराष्ट्र जमीन महसूल अधिकार अभिलेख आणि नोंदवहा (तयार करणे व सुविधायी ठेवणे) नियम १९७१ यातील नियम ३,५,६ आणि ७] नाम :- रोटी (५१६३९५) तालुका :- दोळ तालुका :- पुणे PJ ID : 20001418036 दस्त अर्जांक व उपविभाग २७ 20001418036						
भूधारका पद्धती		भोववटास्थानी नाव :				
क्षेत्र, एकक व आकारपत्री	खाली क्र.	भोववटास्थानी नाव	क्षेत्र	आकार	फु. ख.	फेरवार क्र.
क्षेत्राचे एकक व आकार पत्री	२५१	[<u>संभाजी साकार</u>]	३.८२.००	६.६३	२.६६.००	(२५७३)
अ) लागवड योग्य क्षेत्र		[<u>संभाजी साकार</u>]				(२५७३)
निरावत ७.८२.००		[<u>संभाजी साकार</u>]				(२५७३)
योगावत -		[<u>संभाजी साकार</u>]				(२५७३)
एकूण		[<u>संभाजी साकार</u>]				(२५७३)
सा. बी. क्षेत्र ७.८२.००		[<u>संभाजी साकार</u>]				(२५७३)
ब) मोटाखा क्षेत्र		[<u>संभाजी साकार</u>]				(२५७३)
(लागवड अयोग्य)		[<u>संभाजी साकार</u>]				(२५७३)
ग) ०.९६.००		[<u>संभाजी साकार</u>]				(२५७३)
ग) -		[<u>संभाजी साकार</u>]				(२५७३)
एकूण		[<u>संभाजी साकार</u>]				(२५७३)
घ) ०.९६.००		[<u>संभाजी साकार</u>]				(२५७३)
एकूण क्षेत्र ८.७८.००		[<u>संभाजी साकार</u>]				(२५७३)
(अ+ब)		[<u>संभाजी साकार</u>]				(२५७३)
आकारपत्री ६.६३		[<u>संभाजी साकार</u>]				(२५७३)
कुडी किंवा विभाग	२०७३	संभाजी साकार	१.४०.००	१.११		(२५७३)
आकारपत्री	२०७४	संभाजी साकार	१.४०.००	१.११		(२५७३)
	२०७५	संभाजी साकार	१.४०.००	१.११		(२५७३)
	२०७६	संभाजी साकार	१.४०.००	१.११		(२५७३)
	२०७७	संभाजी साकार	१.४०.००	१.११		(२५७३)
	२०७८	संभाजी साकार	१.४०.००	१.११		(२५७३)
	२०७९	संभाजी साकार	१.४०.००	१.११		(२५७३)
	२३१६	संभाजी साकार	२.२८.००	१.१३	०.९६.००	(२५७३)



पृष्ठ नं. १/३

Flag tail



यह प्रस्ताव नमूने के तहत है। यदि आप इसे अपडेट करना चाहते हैं, तो आप इसे अपडेट कर सकते हैं। यदि आप इसे अपडेट नहीं करना चाहते हैं, तो आप इसे अपडेट नहीं कर सकते हैं।

पृष्ठ क्र. २/३



गाय नमुना बारा { विकारी नंदवारी }										
{ महाराष्ट्र जमीन महसूल अधिकार अभिलेख आणि नॉटिफिकेशन (न्याय करणे व सुविधासहित ठेकने) नियम १९७५ धातील नियम २१ }										
गाय :- पोली (५५६३९५)			वास्तुका :- पोली					जिल्हा :- पुणे		
मह. करणक व उपविभाग			२७							
			विकारवादी/विकारवा संपत्तीस					स्वागतवादी संपत्ती उपलब्ध गणवतीस जमीन		धोरत
वर्ष	हंगाम	आले क्रमांक	विकारवा प्रकार	विकारवा नाव	वस्तु स्थिति	अवतल विविधता	वस्तु स्थिति/वस्तु	स्वागत	क्षेत्र	
(१)	(२)	(३)	(४)	(५)	(६)	(७)	(८)	(९)	(१०)	(११)
					हे.आर.बी.सी	हे.आर.बी.सी			हे.आर.बी.सी	
२०१७-१८	एकी							गवत घट	७.८२००	
२०१८-१९	एकी							गवत घट	७.८२००	
२०१९-२०	एकी							गवत घट	७.८२००	


टीप :- " सरकारी नोट गोदावरी और हारें घेतल आलेली आहे



Annexure-VIII

EHS SCANNER		Dr. Vaibhav Chakurkar MBBS AFH, ADIS DISH Authorized Certifying Surgeon PUNE District																			
MAHARASHTRA FACTORIES RULES FORM 6 (see rule 18)																					
CERTIFICATE OF MEDICAL EXAMINATION : JAN - FEB - 2026																					
Name : SAKASHI SHASHIKANT KADAM		KKB - 3																			
Sr. No : 202 Reg No. K 3207 EMP ID : 158180		Age : 24 Yrs/ Female																			
Job Profile : API		Weight : 47 Kg																			
Company : CIPLA LIMITED		Height : 143 Cms																			
Address : Unit - III, Plot No. D 22, MIDC kurkumbh, Tal. Daund, Pune 413802		BMI : 22.9 Kg/m ²																			
Medical And Occupational History	Present c/o : Nil Past h/o : Not significant Family h/o : Not significant																				
General Examination	Pulse : 96 / min Blood Pressure : 108 / 71 mmHg in sitting position. No : Pallor/Edema/LN-pathy/Icterus/Cyanosis/Clubbing																				
Clinical Examination	RS : AEBE, clear, no any adventitious sound heard. CVS : S ₁ , S ₂ - heard, no murmur.																				
Systemic Examination	CNS: Conscious, well oriented, no abnormality detected P/A : Soft, no organomegaly Skin : Healthy, no abnormality detected.																				
		<table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <th colspan="3">Vision Test : Eye Examination</th> </tr> <tr> <td>Spects :</td> <td colspan="2">No</td> </tr> <tr> <td>Test done</td> <td>Right Eye</td> <td>Left Eye</td> </tr> <tr> <td>Distant vision</td> <td>6/6</td> <td>6/6</td> </tr> <tr> <td>Near vision</td> <td>N6</td> <td>N6</td> </tr> <tr> <td>Colour vision</td> <td colspan="2">Normal</td> </tr> </table>		Vision Test : Eye Examination			Spects :	No		Test done	Right Eye	Left Eye	Distant vision	6/6	6/6	Near vision	N6	N6	Colour vision	Normal	
Vision Test : Eye Examination																					
Spects :	No																				
Test done	Right Eye	Left Eye																			
Distant vision	6/6	6/6																			
Near vision	N6	N6																			
Colour vision	Normal																				
Blood & Urine Reports : as per the attached laboratory reports																					
X Ray Chest PA view : normal study																					
PFT : within normal limits																					
Advice																					
Physical Fitness : I heereby certify that, I have personally examined , SAKASHI SHASHIKANT KADAM , Residing at Kurkumbh, Pune, who is desirous of being employed in factory, and that his age as nearly as can be ascertained from my examination is 24 years and that he is FIT for Employment as an Adult.																					
Free from Skin & Infectious Diseases.																					
Date : 02/02/2026		 डॉ. वैभव चाकुरकर MBBS, AFH, ADIS, DISH Reg No. 202604/2026 कारखाने अधीनस्थ एच.एस. एम्.आर. (सी) प्रमाणित पुणे जिल्हाकाय सेवा विभाग १५/०२/२०२६ १५/०२/२०२६ परी प्राधिकृत प्रमाणित सत्य विकसितक डॉ. १५-२६-२०२६																			
C-104, Akshay Park, Thergaon, Pune 411 033		64847 health@ehsscanner.com																			

Annexure-IX

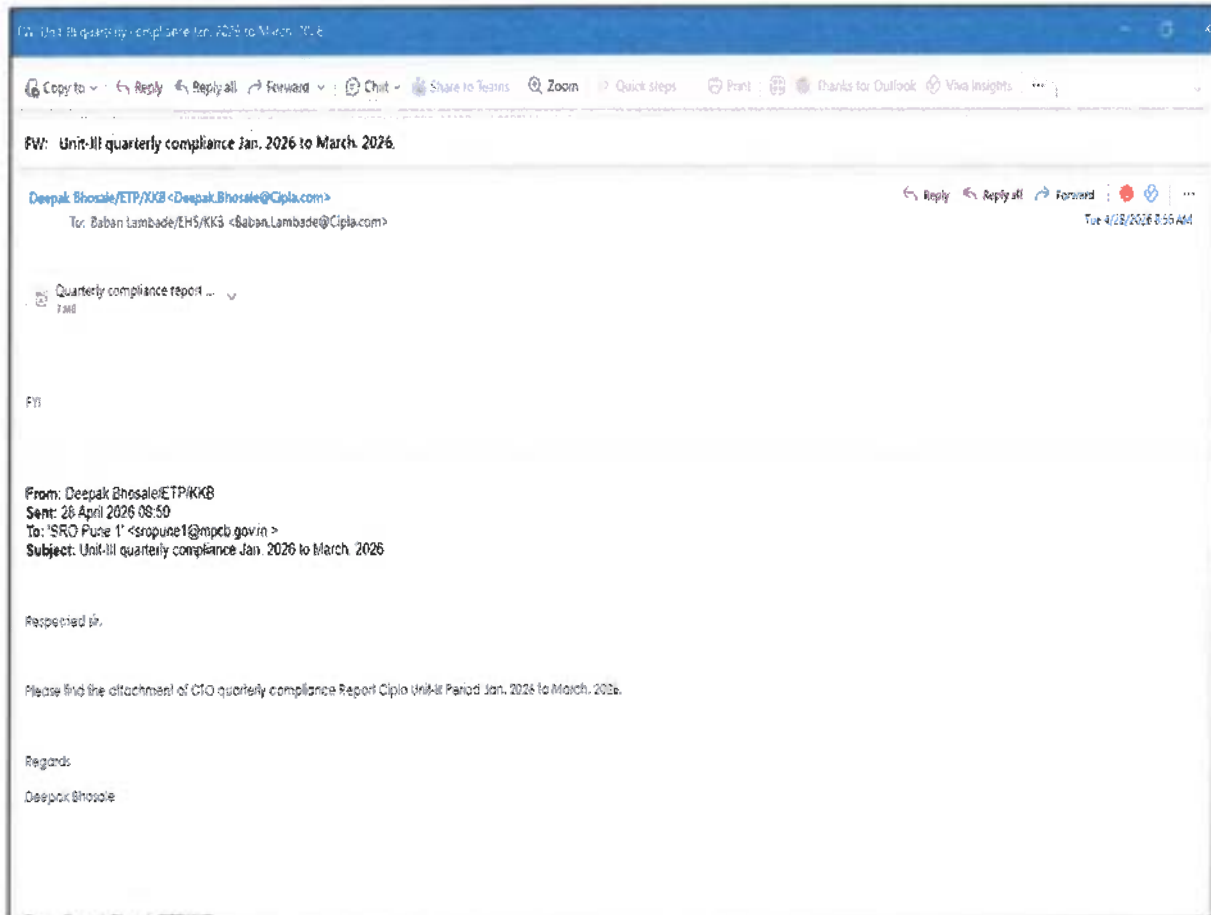

Annexure-X

MAHARASHTRA POLLUTION CONTROL BOARD

Tel: 24010706/24010437
Fax: 24023516
Website: <http://mpcb.gov.in>
Email: cac-cell@mpcb.gov.in



Kalpataru Point, 2nd, 3rd
and 4th floor, Opp. Cine
Planet Cinema, Near Sion
Circle, Sion (E),
Mumbai-400022

RED/L.S.I (R58)
No:- Format1.0/CAC/UAN
No.0000200484/CR/2502000433

Date: 05/02/2025

To,
Cipla Ltd.,
Plot No. D-22, Unit.-3, MIDC Kurkumbh,
Tal- Daund, Dist- Pune.



Sub: Grant amendment in consent to operate based on change in product mix, under RED category.

- Ref:**
1. Earlier Amendment in Consent to Operate under Product mix granted by the Board vide No:- Format1.0/CAC/UAN No.0000159754/CO/2309002291 dated 28.09.2023.
 2. Environmental Clearance granted vide No. F. No. J-11011/47/205-IA II (I) dated 13/10/2005.
 3. Minutes of Technical Committee meeting held on 16.08.2024.
 4. Minutes of 12th CAC meeting held on 13.12.2024.

Your application No.MPCB-CONSENT-0000200484 Dated 26.02.2024

For: grant of Consent to Operate under Section 26 of the Water (Prevention & Control of Pollution) Act, 1974 & under Section 21 of the Air (Prevention & Control of Pollution) Act, 1981 and Authorization under Rule 6 and Rule 18(7) of the Hazardous & Other Wastes (Management & Transboundary Movement) Rules 2016 is considered and the consent is hereby granted subject to the following terms and conditions and as detailed in the schedule I, II, III & IV annexed to this order:

1. The consent to renewal is granted for a period up to 30/04/2027
2. The capital investment of the project is Rs.193.66 Crs. (As per C.A Certificate submitted by industry Existing CI is-Rs. 168.56 Crs + Expansion/Increase in C.I. - Rs. 25.1 Crs)
3. Consent is valid for the manufacture of:

Sr No	Product	Existing Quantity	Proposed Quantity	Total	UOM
Products					
1	Anti-Retroviral/Anti-Viral : Abacavir Sulphate	9	11	20	MT/A
2	Anti-Retroviral/Anti-Viral : Tenofovir Disoproxil Fumarate	8	0	8	MT/A
3	Anti-Retroviral/Anti-Viral : Tenofovir Alafenamide Fumarate	0.2	0	0.2	MT/A
4	Anti-Bacterial/Fungal :Terbinafine Hydrochloride	22	-7	15	MT/A
5	Cheiating Agent: Deferasirox	1.7	0	1.7	MT/A



Sr No	Product	Existing Quantity	Proposed Quantity	Total	UOM
6	Anti-Neoplastic: Ondansetron Base / HCL	2	0	2	MT/A
7	R&D	0.5	1.5	2	MT/A
8	Anti-Retroviral/Anti-Viral: Dolutegravir Sodium	23.5	1.5	25	MT/A
9	Anti-Retroviral/Anti-Viral: Lamivudine	10	-5	5	MT/A
10	Nirmatrelvir	4	-3	1	MT/A
11	Anti-inflammatory: Tafamidis	0.1	0	0.1	MT/A
12	Omeprazole Sodium	10	-5	5	MT/A
13	Anti-Retroviral/Anti-Viral: Emtricitabine	8.8	0	8.8	MT/A
14	Anti-Retroviral/Anti-Viral: Remdesivir	0.5	0	0.5	MT/A
15	Anti-Retroviral/Anti-Viral: Oseltamivir Phosphate	20	0	20	MT/A
16	Anti-Retroviral/Anti-Viral: Valacyclovir Hydrochloride	0.2	0	0.2	MT/A
17	Anti-Retroviral/Anti-Viral: Molnupiravir	1	-0.7	0.3	MT/A
18	Anti-Retroviral/Anti-Viral: Cabotegravir Sodium	5	0	5	MT/A
19	Tenofovir Pivafem Fumarate	0.5	0	0.5	MT/A
20	Chelating Agent: Edaravone	0.1	0	0.1	MT/A
21	Anti-Androgen: Danazol	0.05	0	0.05	MT/A
22	Anti-Androgen: Cyproterone Acetate	0.7	0	0.7	MT/A
23	Anti-inflammatory: Eluxadoline	0.1	0	0.1	MT/A
24	Anti-inflammatory / Histamine: Fexofenadine Hydrochloride	0.1	0	0.1	MT/A
25	Chelating Agent: Sodium thiosulfate pentahydrate	0.5	0	0.5	MT/A
26	Chelating Agent: Deferiprone	0.1	0	0.1	MT/A
27	Anti-Depressant: Escitalopram Oxalate	0.1	0	0.1	MT/A
28	Anti-Depressant: Citalopram Hydrobromide	0.1	0	0.1	MT/A
29	Anti-Neoplastic: Exemestane	0.5	1	1.5	MT/A
30	Anti-Dibetic: Dapagliflozin	0.05	0	0.05	MT/A
31	Anti-Dibetic: Empagliflozin	0.05	0	0.05	MT/A
32	Estrogenic: Levonorgestrel	0.01	0	0.01	MT/A
33	Bronchodilator: Formoterol Fumarate / FC-V	0.5	0	0.5	MT/A
34	Anti-Parkinson: Pramipexole Dihydrochloride / PX-IV	0.25	0	0.25	MT/A
35	Cardiac: Trimetazidine Dihydrochloride	1	0	1	MT/A
36	Pantoprazole Sodium	10	-1	9	MT/A
37	Apixaban	0.3	1.7	2	MT/A

Sr No	Product	Existing Quantity	Proposed Quantity	Total	UOM
38	Ivacaftor	0.1	0	0.1	MT/A
39	Leflunomide	5	-2	3	MT/A
40	Isavuconazonium Sulphate	0.2	0.3	0.5	MT/A
41	Lenacapavir	0.5	0	0.5	MT/A
42	Levermeloxifene Fumarate	0.5	0	0.5	MT/A
43	Edoxaban Tosylate	0.1	0	0.1	MT/A
44	Anti-Retroviral/Anti-Viral: Nevirapine/ Nevirapine hemihydrate	2	0	2	MT/A
45	Zidovudine	1	0	1	MT/A
46	Anti-Retroviral/Anti-Viral: Baioxavir Marboxil	2	0	2	MT/A
47	Anti-Neoplastic: Estramustine sodium Phosphate	0.08	0	0.08	MT/A
48	Anti-Diabetic: Rosiglitazone Maleate	0.1	0	0.1	MT/A
49	Cardiac: Carvedilol	2	0	2	MT/A
50	Anti-Retroviral/Anti-Viral: Bictegravir	0.2	0	0.2	MT/A
51	Lansoprazole	0	3	3	MT/A
52	Linagliptin	0	2	2	MT/A
53	Nintedanib	0	1.5	1.5	MT/A

4. **Conditions under Water (P&CP), 1974 Act for discharge of effluent:**

Sr No	Description	Permitted in CMD	Standards to	Disposal Path
1.	Trade effluent	103	As per Schedule-I	Recycle 100% to achieve ZLD
2.	Domestic effluent	38	As per Schedule-I	Recycle 100% to achieve ZLD

5. **Conditions under Air (P& CP) Act, 1981 for air emissions:**

Sr No.	Stack No.	Description of stack / source	Number of Stack	Standards to be achieved
1	S-1	Thermopack (1W + 1S)	1	As per Schedule -II
2	S-2	Boiler (1W + 1S)	1	As per Schedule -II
3	S-4	D.G. Set (750 kVA)	1	As per Schedule -II
4	S-5	D.G. Set (750 kVA)	1	As per Schedule -II
5	S-6	Process Vent-1 (BD I)	1	As per Schedule -II
6	S-7	Process Vent-2 (BD I)	1	As per Schedule -II
7	S-8	Process Vent-3 (BD II)	1	As per Schedule -II
8	S-9	Process Vent-4 (BD II)	1	As per Schedule -II
9	S-10	Process Vent-5 (BD III)	1	As per Schedule -II

Sr No.	Stack No.	Description of stack / source	Number of Stack	Standards to be achieved
10	S-11	Process Vent-6 (BD IV)	1	As per Schedule -II
11	S-12	Process Vent-7 (BD IV)	1	As per Schedule -II

6. **Non-Hazardous Wastes:**

Sr No.	Type of Waste	Quantity	UoM	Treatment	Disposal
1	Corrugated Boxes/ Paper, Aluminium, GI scrap, rubber Scrap & Miscellaneous Scrap (Metal waste, Glass waste, wooden scrap)	132	MT/A	NIL	Sale to Authorised Party

7. **Conditions under Hazardous & Other Wastes (M & T M) Rules 2016 for Collection, Segregation, Storage, Transportation, Treatment and Disposal of hazardous waste:**

Sr No.	Category No. / Type	Quantity	UoM	Treatment	Disposal
1	37.3 Concentration or evaporation residues	284.11	MT/A	Recycle/Incineration/coprocessing	Sale to authorized part/Coprocessor through MPCB/CPCB Authorized Preprocessor/CHWTSDf
2	5.1 Used or spent oil	2.020	KL/A	Incineration/ Recycle	Sale to authorised party / CHWTSDf
3	37.1 Sludge from wet scrubbers	0.1	MT/A	Landfill/ Recycle	Sale to authorised party / CHWTSDf
4	28.5 Date-expired products	0.21	MT/A	Incineration	CHWTSDf
5	28.6 Spent organic solvents	259.2	MT/A	Incineration/ Recycle	Sale to authorised party / CHWTSDf
6	35.3 Chemical sludge from waste water treatment	42.1	MT/M	Recycle/Incineration/coprocessing	Sale to authorized part/Coprocessor through MPCB/CPCB Authorized Preprocessor/CHWTSDf
7	28.3 Spent carbon	10.6	MT/A	Incineration /Coproprocessing	Coprocessor through MPCB/CPCB Authorized Preprocessor/CHWTSDf
8	20.2 Spent solvents	3651.4	KL/A	Recycle/Incineration/coprocessing	Sale to authorized part/Coprocessor through MPCB/CPCB Authorized Preprocessor/CHWTSDf
9	28.2 Spent catalyst	90	MT/A	Recycle/Incineration/coprocessing	Sale to authorized part/Coprocessor through MPCB/CPCB Authorized Preprocessor/CHWTSDf
10	35.4 Oil and grease skimming	63	MT/A	Recycle/Incineration/coprocessing	Sale to authorized part/Coprocessor through MPCB/CPCB Authorized Preprocessor/CHWTSDf

Sr No	Category No./ Type	Quantity	UoM	Treatment	Disposal
11	33.1 Empty barrels /containers /liners contaminated with hazardous chemicals /wastes	1200	No/M	Recycle/incineration/coprocessing	Safe to authorized part/Coprocessor through MPCB/CPCB Authorized Preprocessor/CHWTSDF

8. **Conditions under E-Waste Management:**

Sr No	Type of Waste	Quantity	UoM	Disposal Path
1	E-Waste	4.00	MT/A	Safe to authorized recycler.

9. **Treatment and Disposal of Biomedical Waste generated to CBMWTSDF:**

Sr.No	Category	Type of Waste	Quantity not to exceed (Kg./M)	Segregation Color coding	Treatment & Disposal
1	Yellow	a) Soiled Waste	5.00	Yellow colored non-chlorinated plastic bags or containers	CBMWTSDF
2	Red	Contaminated waste (Recyclable)	1.50	Red colored non chlorinated plastic bags or containers	CBMWTSDF
3	White (Translucent)	Waste sharps including Metals	1.00	Puncture proof, Leak proof, tamper proof container	CBMWTSDF
4	Blue	a) Glassware	1.00	Puncture proof & leak proof boxes or containers with blue colored marking.	CBMWTSDF

- The Board reserves the right to review, amend, suspend, revoke this consent and the same shall be binding on the industry.
- This consent should not be construed as exemption from obtaining necessary NOC/ permission from any other Government authorities.
- This consent is issued with overriding effect on earlier Earlier Amendment in Consent to Operate under Product mix granted by the Board vide No:- Format1.0/CAC/UAN No.0000159754/CO/2309002291 dated 28.09.2023 valid up to 30.04.2024.
- This consent is issued pursuant to the decision of the 12th Consent Appraisal Committee Meeting held on 13/12/2024.
- Industry shall comply with all the conditions stipulated in Environmental Clearance granted vide No. F. No. J-11011/47/205-IA II (I) dated 13/10/2005 and ensure display/upload of six-monthly compliance monitoring report on their official website.
- Industry shall install online continuous monitoring system as per CPCB guidelines & data to be transmitted directly from Data Logger to Board server .
- The applicant shall make an application for renewal of consent 60 days prior to date of expiry of the consent. (Operate/Renewal)

17. Industry shall cover the collection and equalization tanks of Effluent Treatment Plant and shall provide scrubber to control the emissions.
18. The condition shall be imposed as "If any submission of misleading information including NIPL certificate is noticed, then the consent issued under MoEF & CC Product Mix Circular dtd. 02.03.2021 and amendments thereto will stand automatically cancelled."
19. The industry shall create an Environment Cell by appointing an Environmental Engineer OR Expert for looking after day-to-day activities related to Environment OR Pollution control.

This consent is issued on the basis of information/documents submitted by the Applicant/Project Proponent, if it has been observed that the information submitted by the Applicant/Project Proponent is false, misleading or fraudulent, the Board reserves its right to revoke the consent & further legal action will be initiated against the Applicant/Project Proponent.



Disnazy

2b9a099b
7a9c4cd8
8ae9bd46
09a84bc4
cf226031
1dd59e6e
bd4cbccf
b89e14d4

Signed by: Dr. Arinash Dholake
Member Secretary
For and on behalf of
Maharashtra Pollution Control Board
ms@mpcb.gov.in
2025-02-05 11:15:35 IST

Received Consent fee of -

Sr.No	Amount(Rs.)	Transaction DR.No.	Date	Transaction Type
1	1161960.00	MPCB-DR-25884	15/04/2024	NEFT

Copy to:

1. Regional Officer, MPCB, Pune and Sub-Regional Officer, MPCB, Pune
- They are directed to ensure the compliance of the consent conditions.
2. Chief Accounts Officer, MPCB, Sion, Mumbai
3. CC-CAC updating.

SCHEDULE-I

Terms & conditions for compliance of Water Pollution Control:

1. A) As per your application, you have segregated trade effluent into weak stream & strong stream and provided Effluent Treatment Plant (ETP) comprising of:
 - i) **Strong COD/TDS stream of 14 CMD** - Treatment system comprising of Primary (Collection tank, Neutralization tank, Equalization tank, Flash mixer, Primary after stmt) , Stripper followed by Multi effect evaporator (3 stage). The MEE condensate is treated in weak stream ETP.
 - ii) **Weak COD/TDS stream of 89 CMD** - Treatment system comprising of Primary (Collection tank, Neutralization tank, Equalization tank), Secondary (Activated sludge process), Tertiary (Pressure sand filter), Advance treatment (Reverse osmosis, Multi Effective Evaporator (stage)) .
- B) The Applicant shall operate the effluent treatment plant (ETP) to treat the trade effluent and recycle the entire treated effluent into the process for various purposes such as for cooling, process & Scrubbing with metering system so as to achieve Zero Liquid Discharge. There shall be no discharge on land or outside factory premises.
- C) The Industry shall ensure connectivity online monitoring system to the MPCB server including separate energy meter for pollution control system.
- D) The treated effluent shall be recycled for secondary purposes. In no case, effluent shall find its way for gardening / outside factory premises.
2. A) As per your application, you have provided Sewage Treatment Plant of designed capacity 40 CMD for the treatment of 38 CMD of sewage.
- B) The Applicant shall operate the sewage treatment system to treat the sewage so as to achieve the following standards.

Sr.No	Parameters	Standards (mg/l)	
1	Suspended Solids	Not to exceed	50
2	BOD 3 days 27°C	Not to exceed	30
3	COD	Not to exceed	100

- C) The treated sewage shall be recycled for secondary purposes to the maximum extent and remaining shall be discharged on land for gardening within premise after confirming above standards. In no case, sewage shall find its way for gardening / outside factory premises.
3. The Board reserves its rights to review plans, specifications or other data relating to plant setup for the treatment of waterworks for the purification there of & the system for the disposal of sewage or trade effluent or in connection with the grant of any consent conditions. The Applicant shall obtain prior consent of the Board to take steps to establish the unit or establish any treatment and disposal system or an extension or addition thereto.
4. The industry shall ensure replacement of pollution control system or its parts after expiry of its expected life as defined by manufacturer so as to ensure the compliance of standards and safety of the operation thereof.

5. The Applicant shall comply with the provisions of the Water (Prevention & Control of Pollution) Act, 1974 and as amended, by installing water meters and other provisions as contained in the said act:

Sr. No.	Purpose for water consumed	Water consumption quantity (CMD)
1.	Industrial Cooling, spraying in mine pits or boiler feed	223.00
2.	Domestic purpose	40.00
3.	Processing whereby water gets polluted & pollutants are easily biodegradable	53.00
4.	Processing whereby water gets polluted & pollutants are not easily biodegradable and are toxic	0.00
5.	Gardening	30

6. The Applicant shall provide Specific Water Pollution control system as per the conditions of EP Act, 1986 and rule made there under from time to time/ Environmental Clearance/ CREP guidelines.

SCHEDULE-II

Terms & conditions for compliance of Air Pollution Control:

1. As per your application, you have provided the Air pollution control (APC) system and erected following stack (s) to observe the following fuel pattern:

Stack No.	Source	APC System provided proposed	Stack Height(in mtr)	Type of Fuel	Sulphur Content(in %)	Pollutant	Standard
S-1	Thermopack (1W + 1S)	Stack	30.00	HSD 48 Ltr/Hr	-	Other	-
S-2	Boiler (1W + 1S)	Stack	33.00	LSHS 135 Kg/Hr	-	Other	-
				PNG SCM/hr	-		
				162.68 SCM/Hr	-		
				LDO 3.8 KL/D	-		
				HSD 3.44 KL/D	-		
S-4	D.G. Set (750 kVA))	Acoustic Enclosure Stack	5.00	HSD 100 Kg/Hr	-	TPM	-
						SO2	-
S-5	D.G. Set (750 kVA))	Acoustic Enclosure Stack	6.00	HSD 150 Kg/Hr	-	TPM	-
						SO2	-
S-6	Process Vent-1 (BD I)	Scrubber	3.00	- 0 --NA--	-	HCL	35 Mg/Nm ³
S-7	Process Vent-2 (BD I)	Scrubber	6.00	- 0 --NA--	-	HCL	35 Mg/Nm ³

Stack No.	Source	APC System provided, proposed	Stack Height(in mtr)	Type of Fuel	Sulphur Content(in %)	Pollutant	Standard
S-8	Process Vent-3 (BD II)	Scrubber	6.00	- 0 -- NA--	-	HCL	35 Mg/Nm ³
S-9	Process Vent-4 (BD II)	Scrubber	4.00	- 0 -- NA--	-	HCL	35 Mg/Nm ³
S-10	Process Vent-5 (BD III)	Scrubber	6.00	- 0 -- NA--	-	HCL	35 Mg/Nm ³
S-11	Process Vent-6 (BD IV)	Scrubber	4.00	- 0 -- NA--	-	HCL	35 Mg/Nm ³
S-12	Process Vent-7 (BD IV)	Scrubber	9.00	- 0 -- NA--	-	Acid Mist	35 Mg/Nm ³

- The Applicant shall provide Specific Air Pollution control equipments as per the conditions of EP Act, 1986 and rule made there under from time to time/ Environmental Clearance / CREP guidelines.
- The applicant shall operate and maintain above mentioned air pollution control system, so as to achieve the level of pollutants to the following standards:

Parameters	Standards (unit)	
Total Particulate Matter	Not to exceed	30 mg/ Nm ³

- The Applicant shall obtain necessary prior permission for providing additional control equipment with necessary specifications and operation thereof or alteration or replacement/alteration well before its life come to an end or erection of new pollution control equipment.
- The Board reserves its rights to vary all or any of the condition in the consent, if due to any technological improvement or otherwise such variation (including the change of any control equipment, other in whole or in part is necessary).

SCHEDULE-III

Details of Bank Guarantees:

Sr. No	Consent (C2E/ C2O/ C2R)	Amt of BG Imposed	Submission Period	Purpose of BG	Compliance Period	Validity Date
1	C to 1st O	2500000	15 days/extend	Towards O & M of pollution control systems and compliance of consent conditions.	30.04.2027	30.04.2028

If the above Bank Guarantee is not submitted within stipulated period, then 12% Interest will be levied as a penalty as per circular dtd 29/02/2024 No. BO/MPCB/AS(T)/Circular/B-240229FTS0122

BG Forfeiture History

Srno.	Consent (C2E/C2O/C2R)	Amount of BG imposed	Submission Period	Purpose of BG	Amount of BG Forfeiture	Reason of BG Forfeiture
NA						

BG Return details

Srno.	Consent (C2E/C2O/C2R)	BG imposed	Purpose of BG	Amount of BG Returned
NA				

SCHEDULE-IV

General Conditions:

1. Consumers or bulk consumers of electrical and electronic equipment listed in Schedule I shall ensure that e-waste generated by them is channelised through collection centre or dealer of authorised producer or dismantler or recycler or through the designated take back service provider of the producer to authorised dismantler or recycler
2. Bulk consumers of electrical and electronic equipment listed in Schedule I shall maintain records of e-waste generated by them in Form-2 and make such records available for scrutiny by the concerned State Pollution Control Board
3. Consumers or bulk consumers of electrical and electronic equipment listed in Schedule I shall ensure that such end-of-life electrical and electronic equipment are not admixed with e-waste containing radioactive material as covered under the provisions of the Atomic Energy Act, 1962 (33 of 1962) and rules made there under;
4. Bulk consumers of electrical and electronic equipment listed in Schedule I shall file annual returns in Form-3, to the concerned State Pollution Control Board on or before the 30th day of June following the financial year to which that return relates. In case of the bulk consumer with multiple offices in a State, one annual return combining information from all the offices shall be filed to the concerned State Pollution Control Board on or before the 30th day of June following the financial year to which that return relates.
5. Specific Conditions for storage, Handling and Disposal of Waste from Electrical & Electronic equipment (WEEE):

1. **Collection of WEEE** - The applicant must provide appropriate and dedicated vehicles duly identified as per the norms for transportation of Hazardous Waste. The applicant shall obtain all the required permits for transportation of WEEE from competent authority. The applicant shall ensure the safe transport of the WEEE without any spillage during transportation.

Storage for disassembled parts: The applicant must provide appropriate storage for disassembled spare parts from WEEE. Some spare parts (e.g. motors and compressors) will contain oil and/or other fluids. Such part must be appropriately segregated and stored in containers that are secured such that oil and other fluids cannot escape from them. These containers must be stored on an area with an area with an impermeable surface and a sealed drainage system.

2. **Storage for other components and residues:** Other components and residues arising from the treatment of WEEE will need to be contained following their removal for disposal or recovery. Where they contain hazardous substances they should be stored on impermeable surface and in appropriate containers or bays with weatherproof covering. Containers should be clearly labelled to identify their contents and must be secured so that liquids, including rain water cannot enter them. Components should be segregated having regard to their eventual destinations and the compatibility of the component types. All batteries should be handled and stored having regard to the potential fire risk associated with them.
3. **Balances :** WEEE Guidelines also requires that sites for handling of WEEE have "balances to measure the weight of the segregated waste". The objective is to ensure that a record of weights can be maintained of WEEE entering a facility and components and materials leaving each site (together with their destinations). The nature of the weighing equipment should be appropriate for the type and quantity of WEEE being processed.
4. Plastic, which cannot be recycled and is hazardous in nature, is recommended to be land filled in nearby CHWTSDf.
5. Ferrous and nonferrous metal recycling facilities fall under the purview of existing environmental regulations for air, water, noise, land and soil pollution and generation of hazardous waste and the same should be followed.
6. CFCs should be either reused or incinerated in common hazardous waste incineration facilities at CHWTSDf.
7. Waste Oil should be either reused or incinerated in common hazardous waste incineration facilities.
8. PCB's containing capacitors shall be incinerated in common hazardous waste incineration facilities at CHWTSDf.
9. Mercury recovery and lead recycling facilities from batteries fall under the Hazardous & Other Wastes (M & TM) Rules, 2016.
10. Existing environmental regulations for air, water, noise, land and soil pollution and generation of hazardous waste and the same should be followed. In case Mercury or lead recovery is very low, they can be temporarily stored at e-waste recycling facility and later disposed in TSDF.
11. The industry shall maintain records of the e-waste purchased, processed in Form-2 and shall file annual returns of its activities of previous year in Form-3 as per Rules 11(9) & 13(3)(vii) of the E-Waste(M) Rules, 2016; on or before 30th day of June of every year.
6. The Energy source for lighting purpose shall preferably be LED based
7. The PP shall harvest rainwater from roof tops of the buildings and storm water drains to recharge the ground water and utilize the same for different industrial applications within the plant
8. Conditions for D.G. Set
 - a) Noise from the D.G. Set should be controlled by providing an acoustic enclosure or by treating the room acoustically.
 - b) Industry should provide acoustic enclosure for control of noise. The acoustic enclosure/ acoustic treatment of the room should be designed for minimum 25 dB (A) insertion loss or for meeting the ambient noise standards, whichever is on higher side. A suitable exhaust muffler with insertion loss of 25 dB (A) shall also be provided. The measurement of insertion loss will be done at different points at 0.5 meters from acoustic enclosure/room and then average.
 - c) Industry should make efforts to bring down noise level due to DG set, outside industrial premises, within ambient noise requirements by proper siting and control measures.

- d) Installation of DG Set must be strictly in compliance with recommendations of DG Set manufacturer.
 - e) A proper routine and preventive maintenance procedure for DG set should be set and followed in consultation with the DG manufacturer which would help to prevent noise levels of DG set from deteriorating with use.
 - f) D.G. Set shall be operated only in case of power failure.
 - g) The applicant should not cause any nuisance in the surrounding area due to operation of D.G. Set.
 - h) The applicant shall comply with the notification of MoEFCC, India on Environment (Protection) second Amendment Rules vide GSR 371(E) dated 17.05.2002 and its amendments regarding noise limit for generator sets run with diesel.
9. The applicant shall maintain good housekeeping.
 10. The non-hazardous solid waste arising in the factory premises, sweepings, etc. be disposed of scientifically so as not to cause any nuisance / pollution. The applicant shall take necessary permissions from civic authorities for disposal of solid waste.
 11. The applicant shall not change or alter the quantity, quality, the rate of discharge, temperature or the mode of the effluent/emissions or hazardous wastes or control equipments provided for without previous written permission of the Board. The industry will not carry out any activity, for which this consent has not been granted/without prior consent of the Board.
 12. The Board reserves the right to review, amend, suspend, revoke this consent and the same shall be binding upon you.
 13. The industry shall submit quarterly statement in respect of industries obligation towards consent and pollution control compliance's duly supported with documentary evidences (format can be downloaded from MPCB official site).
 14. The industry shall submit official e-mail address and any change will be duly informed to the MPCB.
 15. The industry shall achieve the National Ambient Air Quality standards prescribed vide Government of India, Notification No. B-29016/20/90/PCI-I dated. 18.11.2009 as amended.
 16. This consent should not be construed as exemption from obtaining necessary NOC/permission from any other Government authorities.
 17. The industry shall ensure replacement of pollution control system or its parts after expiry of its expected life as defined by manufacturer so as to ensure the compliance of standards and safety of the operation thereof.
 18. You shall operate OCEMS installed for source emission round 'O' clock and transmit data online to CPCB and MPCB server. You shall also monitor effluent quality, stack emissions and ambient air quality monthly/quarterly. You shall conduct Dioxin Furan monitoring by third party NABL Accredited agency once in year and submit report to Sub Regional Officer.
 19. You shall ensure collection, and segregation of BMW regularly to treat and dispose Off within 48 hrs from generation.
 20. Whenever due to any accident or other unforeseen act or even, such emissions occur or is apprehended to occur in excess of standards laid down, such information shall be forthwith Reported to Board, concerned Police Station, office of Directorate of Health Services, Department of Explosives, Inspectorate of Factories and Local Body. In case of failure of pollution control equipments, the production process connected to it shall be stopped.
 21. The applicant shall provide an alternate electric power source sufficient to operate all pollution control facilities installed to maintain compliance with the terms and conditions of the consent. In the absence, the applicant shall stop, reduce or otherwise, control production to abide by terms and conditions of this consent.

22. The industry shall recycle/reprocess/reuse/recover Hazardous Waste as per the provision contain in the Hazardous and Other Wastes (M & TM) Rules 2016, which can be recycled /processed /reused /recovered and only waste which has to be incinerated shall go to incineration and waste which can be used for land filling and cannot be recycled/reprocessed etc. should go for that purpose, in order to reduce load on incineration and landfill site/environment.
23. An inspection book shall be opened and made available to the Board's officers during their visit to the applicant.
24. You shall not Rent, Lend, Sell, Transfer or Close Down the facility or otherwise transport the Bio Medical waste for any other purpose without obtaining prior written permission of the MPC Board.
25. Separate drainage system shall be provided for collection of trade and sewage effluents. Terminal manholes shall be provided at the end of the collection system with arrangement for measuring the flow. No effluent shall be admitted in the pipes/sewers downstream of the terminal manholes. No effluent shall find its way other than in designed and provided collection system.
26. Neither storm water nor discharge from other premises shall be allowed to mix with the effluents from the factory.
27. The industry should not cause any nuisance in surrounding area.
28. The industry shall take adequate measures for control of noise levels from its own sources within the premises so as to maintain ambient air quality standard in respect of noise to less than 75 dB (A) during day time and 70 dB (A) during night time. Day time is reckoned in between 6 a.m. and 10 p.m. and night time is reckoned between 10 p.m. and 6 a.m.
29. You shall ensure that fugitive emissions from the activity are controlled so as to maintain clean and safe environment in and around the facility premises.
30. The applicant shall provide ports in the chimney/(s) and facilities such as ladder, platform etc. for monitoring the air emissions and the same shall be open for inspection to/and for use of the Board's Staff. The chimney(s) vents attached to various sources of emission shall be designated by numbers such as S-1, S-2, etc. and these shall be painted/ displayed to facilitate identification.
31. The Board reserves its rights to review plans, specifications or other data relating to plant setup for the treatment of waterworks for the purification thereof & the system for the disposal of sewage or trade effluent or in connection with the grant of any consent conditions. The Applicant shall obtain prior consent of the Board to take steps to establish the unit or establish any treatment and disposal system or an extension or addition thereto
32. The applicant shall install a separate meter showing the consumption of energy for operation of domestic and industrial effluent treatment plants and air pollution control system. A register showing consumption of chemicals used for treatment shall be maintained.
33. The applicant shall bring minimum 33% of the available open land under green coverage/ plantation. The applicant shall submit a yearly statement by 30th September every year on available open plot area, number of trees surviving as on 31st March of the year and number of trees planted by September end.
34. The Board reserves its rights to review plans, specifications or other data relating to plant setup for the treatment of waterworks for the purification thereof & the system for the disposal of sewage or trade effluent or in connection with the grant of any consent conditions.

35. The firm shall submit to this office, the 30th day of September every year, the Environment Statement Report for the financial year ending 31st March in the prescribed FORM-V as per the provisions of Rule 14 of the Environment (Protection) (second Amendment) Rules, 1992.
36. You should monitor effluent quality, stack emissions and ambient air quality monthly/quarterly. You shall conduct Dioxin Furan monitoring by third party NABL Accredited agency once in every year and submit report to Sub Regional Officer.
37. The Board reserves its rights to vary all or any of the condition in the consent, if due to any technological improvement or otherwise such variation (including the change of any control equipment, other in whole or in part is necessary).
38. The applicant shall provide facility for collection of environmental samples and samples of trade and sewage effluents, air emissions and hazardous waste to the Board staff at the terminal or designated points and shall pay to the Board for the services rendered in this behalf.
39. You shall obtain necessary prior permission for providing additional control equipment with necessary specifications and operation thereof or alteration or shall ensure replacement of pollution control system or its parts after expiry of its expected life as defined by manufacturer so as to ensure the compliance of standards and safety of the operation thereof.
40. You shall strictly comply with the Water (P&CP) Act, 1974, Air (P&CP) Act, 1981 and Environmental Protection Act, 1986 and industry specific standard under EP Rules 1986 which are available on MPCB website (www.mpcb.gov.in).
41. You shall create the Environmental Cell by appointing an Environmental Engineer and Chemist for looking after day-to-day activities related to compliance of CCA.
42. You should comply with the Hazardous and Other Wastes (M & TM) Rules, 2016 , Bio Medical Waste Management Rules,2016 and submit the Annual Returns as per Rule 6(5) & 20(2) of Hazardous and Other Wastes (M & TM) Rules, 2016 for the preceding year in Form-IV by 30th June of every year

This certificate is digitally & electronically signed.

Annexure-XI



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004

* Mob.: 7249867318, 6378018710 * Email : kran@hespl.co.in / md@hespl.co.in * www.hespl.co.in

AMBIENT NOISE MONITORING REPORT

CLIENT'S NAME & ADDRESS	ULR NO.	TC 1620826000016389
M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	DATED	05/03/2026

Description of Location:		Date: 25&26/02/2026	
Near Main Gate			
Noise Level Meter			
Make	:	Lutron	
Model	:	SL 4023SD	
Serial No.	:	Q697685	
Calibration Details:		Calibration Date: 27/10/2025 Next Calibration Due: 26/10/2026	
Calibration Result of Noise Level Meter			
Calibration		94 dB at 1000 Hz	114 dB at 1000 Hz
Initial		93.3	113.1
Final		93.8	113.8
Sampling Rate		1 sec.	

SR.NO.	DATE	TIME	NOISE LEVEL UNIT dB(A)
	Day Time		
1	26/02/2026	06:25	65.7
2	26/02/2026	07:25	66.1
3	26/02/2026	08:25	65.9
4	26/02/2026	09:25	64.9
5	26/02/2026	10:25	64.4
6	26/02/2026	11:25	63.5
7	25/02/2026	12:25	64.8
8	25/02/2026	13:25	62.5
9	25/02/2026	14:25	63.4
10	25/02/2026	15:25	64.9
11	25/02/2026	16:25	61.2
12	25/02/2026	17:25	66.8
13	25/02/2026	18:25	67.3
14	25/02/2026	19:25	65.7
15	25/02/2026	20:25	64.8
16	25/02/2026	21:25	63.7
	Day Time Leq		64.98

DISCLAIMER:

- Sample will be retained only for 15 days
- Above results indicate to the parameters mentioned only
- Liability limited till issue of test reports only
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004

• Mob.: 7249067318, 8378010710 • Email: kmp@hespi.co.in / md@hespi.co.in • www.hespi.co.in

	Night Time		
17	25/02/2026	22:25	59.2
18	25/02/2026	23:25	60.3
19	26/02/2026	24:25	58.7
20	26/02/2026	01:25	55.3
21	26/02/2026	02:25	54.3
22	26/02/2026	03:25	59.5
23	26/02/2026	04:25	56.2
24	26/02/2026	05:25	57.3
		Night Time Leq	58.04

Instrument Used: DIGITAL Sound Level Meter (data logging) Q697685

Make: Lutron Make

Calibration Date: 27/10/2025 **Next Calibration Due:** 26/10/2026

Test Method: HALPL/LAB/NABL/Amb-Noise/01:2017, SOP Based on IS 9989-1981 / CPCB

Protocol for Ambient Noise Level Monitoring

July 2015, CPCB Regulation on Ambient Noise and Manufacturers Manual

REMARK/OBSERVATIONS:

Note:

Day time shall mean from 6:00 Hrs. to 22:00 Hrs.

Night time shall mean from 22:00 Hrs. to 6:00 Hrs.

Limits: Leq dB (A)

≤75 dB (A) For Day Time

≤70 dB (A) For Night Time

For HORIZON ANALYTICAL LABORATORY PVT.LTD.



MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER:

- Sample will be retained only for 15 days
- Above results indicate to the parameters mentioned only
- Liability limited till issue of test reports only
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.. 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

AMBIENT NOISE MONITORING REPORT

CLIENT'S NAME & ADDRESS	ULR NO.	TC1620826000016390
M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	DATED	05/03/2026

Description of Location: Near DG Set Area		Date: 258.26/02/2026	
Noise Level Meter			
Make	:	Lutron	
Model	:	SL 4023SD	
Serial No.	:	Q697688	
Calibration Details:	Calibration Date: 27/10/2025 Next Calibration Due: 26/10/2026		
Calibration Result of Noise Level Meter			
Calibration	94 dB at 1000 Hz		114 dB at 1000 Hz
Initial	93.1		113.2
Final	93.7		113.4
Sampling Rate	1 sec.		

SR.NO.	DATE	TIME	NOISE LEVEL UNIT dB(A)
	Day Time		
1	26/02/2026	06:55	64.5
2	26/02/2026	07:55	66.2
3	26/02/2026	08:55	65.9
4	26/02/2026	09:55	71.9
5	26/02/2026	10:55	68.1
6	26/02/2026	11:55	67.2
7	25/02/2026	12:55	65.3
8	25/02/2026	13:55	64.1
9	25/02/2026	14:55	65.9
10	25/02/2026	15:55	63.4
11	25/02/2026	16:55	65.4
12	25/02/2026	17:55	65.7
13	25/02/2026	18:55	68.9
14	25/02/2026	19:55	63.4
15	25/02/2026	20:55	70.5
16	25/02/2026	21:55	68.8
		Day Time Leq	67.31

DISCLAIMER :

- Sample will be retained only for 15 days
- Above results indicate to the parameters mentioned only
- Liability limited till issue of test reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Daananath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : krm@hespl.co.in / md@hespl.co.in • www.hespl.co.in

	Night Time		
17	25/02/2026	22:55	60.9
18	25/02/2026	23:55	53.7
19	26/02/2026	24:55	57.8
20	26/02/2026	01:55	58.1
21	26/02/2026	02:55	58.9
22	26/02/2026	03:55	60.6
23	26/02/2026	04:55	60.7
24	26/02/2026	05:55	63.3
		Night Time Leq	59.97

Instrument Used: DIGITAL, Sound Level Meter (data logging) Q697688

Make: Lutron Make

Calibration Date: 27/10/2025 Next Calibration Due: 26/10/2026

Test Method- HALPL/LAB/NABL/Amb-Noise/01:2017, SOP Based on IS 9989-1981 / CPCB

Protocol for Ambient Noise Level Monitoring

July 2015, CPCB Regulation on Ambient Noise and Manufacturers Manual

REMARK/OBSERVATIONS:

Note:

Day time shall mean from 6.00 Hrs. to 22.00 Hrs

Night time shall mean from 22.00 Hrs. to 6.00 Hrs

Limits: Leq dB (A)

≤75 dB (A) For Day Time

≤70 dB (A) For Night Time

For HORIZON ANALYTICAL LABORATORY PVT.LTD.



Manisha Nargolkar
MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER:

- Sample will be retained only for 15 days.
- Above results indicate to the parameters mentioned only.
- Liability limited till issue of test reports only
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob : 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

AMBIENT NOISE MONITORING REPORT

CLIENT'S NAME & ADDRESS	ULR NO.	TC1620826000015391
M/s Cipla Ltd.	DATED	05/03/2026
Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune		

Description of Location:		Date: 26&27/02/2026	
Near BD III DP Store			
Noise Level Meter			
Make	:	Lutron	
Model	:	SL 4023SD	
Serial No.	:	Q697686	
Calibration Details:		Calibration Date: 27/10/2025 Next Calibration Due 26/10/2026	
Calibration Result of Noise Level Meter			
Calibration		94 dB at 1000 Hz	114 dB at 1000 Hz
Initial		93.1	113.2
Final		93.7	113.4
Sampling Rate		1 sec.	

SR.NO.	DATE	TIME	NOISE LEVEL UNIT dB(A)
	Day Time		
1	27/02/2026	06:30	62.1
2	27/02/2026	07:30	63.4
3	27/02/2026	08:30	60.5
4	27/02/2026	09:30	64.9
5	27/02/2026	10:30	64.4
6	27/02/2026	11:30	63.5
7	27/02/2026	12:30	64.8
8	27/02/2026	13:30	62.5
9	26/02/2026	14:30	63.4
10	26/02/2026	15:30	63.1
11	26/02/2026	16:30	60.5
12	26/02/2026	17:30	66.2
13	26/02/2026	18:30	64.5
14	26/02/2026	19:30	63.4
15	26/02/2026	20:30	61.2
16	26/02/2026	21:30	60.5
		Day Time Leq	63.37

DISCLAIMER:

- Sample will be retained only for 15 days.
- Above results indicate to the parameters mentioned only.
- Liability limited till issue of test reports only
- The test report shall not be produced for any legal identity or advertised without permission of lab



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

	Night Time		
17	26/02/2026	22:30	50.5
18	26/02/2026	23:30	49.5
19	27/02/2026	24:30	52.4
20	27/02/2026	01:30	53.8
21	27/02/2026	02:30	54.5
22	27/02/2026	03:30	55.6
23	27/02/2026	04:30	58.4
24	27/02/2026	05:30	59.2
		Night Time Leq	55.42

Instrument Used: DIGITAL Sound Level Meter (data logging) Q697686

Make: Lutron Make

Calibration Date: 27/10/2025 **Next Calibration Due:** 26/10/2026

Test Method- HALPL/LAB/NABL/Amb-Noise/01'2017, SOP Based on IS 9989-1981 / CPCB

Protocol for Ambient Noise Level Monitoring

July 2015, CPCB Regulation on Ambient Noise and Manufacturers Manual

REMARK/OBSERVATIONS:

Note:

Day time shall mean from 6.00 Hrs. to 22.00 Hrs.

Night time shall mean from 22.00 Hrs. to 6.00 Hrs

Limits: Leq dB (A)

≤75 dB (A) For Day Time

≤70 dB (A) For Night Time

For HORIZON ANALYTICAL LABORATORY PVT.LTD.



Manisha Nargolkar
MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER:

- Sample will be retained only for 15 days.
- Above results indicate to the parameters mentioned only
- Liability limited till issue of test reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004

• Mob.: 7249867318, 8378018710 • Email: kmm@hespl.co.in / md@hespl.co.in • www.hespl.co.in

AMBIENT NOISE MONITORING REPORT

CLIENT'S NAME & ADDRESS	ULR NO.	TC1620826000016392
M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	DATED	05/03/2026

Description of Location:		Date: 26&27/02/2026
Near BD IV		
Noise Level Meter		
Make	:	Lutron
Model	:	SL 4023SD
Serial No.	:	Q697687
Calibration Details:	Calibration Date: 27/10/2025 Next Calibration Due: 26/10/2026	
Calibration Result of Noise Level Meter		
Calibration	94 dB at 1000 Hz	114 dB at 1000 Hz
Initial	93.3	113.1
Final	93.8	113.9
Sampling Rate	1 sec.	

SR.NO.	DATE	TIME	NOISE LEVEL UNIT dB(A)
	Day Time		
1	27/02/2026	06:00	68.1
2	27/02/2026	07:00	70.2
3	27/02/2026	08:00	69.2
4	27/02/2026	09:00	63.5
5	27/02/2026	10:00	65.2
6	27/02/2026	11:00	63.1
7	27/02/2026	12:00	67.3
8	27/02/2026	13:00	66.6
9	27/02/2026	14:00	65.4
10	26/02/2026	15:00	61.5
11	26/02/2026	16:00	60.4
12	26/02/2026	17:00	63.9
13	26/02/2026	18:00	60.5
14	26/02/2026	19:00	63.1
15	26/02/2026	20:00	64.5
16	26/02/2026	21:00	66.4
	Day Time Leq		65.85

DISCLAIMER

- Sample will be retained only for 15 days.
- Above results indicate to the parameters mentioned only.
- Liability limited till issue of test reports only
- The test report shall not be produced for any legal identity or advertised without permission of lab



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004

• Mob: 7249867315, 5378018710 • Email: kmg@hespl.co.in / mdg@hespl.co.in • www.hespl.co.in

	Night Time		
17	26/02/2026	22:00	57.6
18	26/02/2026	23:00	55.9
19	27/02/2026	24:00	56.2
20	27/02/2026	01:00	55.6
21	27/02/2026	02:00	56.1
22	27/02/2026	03:00	55.6
23	27/02/2026	04:00	58.4
24	27/02/2026	05:00	61.3
		Night Time Leq	57.55

Instrument Used: DIGITAL Sound Level Meter (data logging) Q697687

Make: Lutron Make

Calibration Date: 27/10/2025 **Next Calibration Due:** 26/10/2026

Test Method- HALPL/LAB/NABL/Amb-Noise/01/2017, SOP Based on IS 9989-1981 / CPCB Protocol for Ambient Noise Level Monitoring
July 2015, CPCB Regulation on Ambient Noise and Manufacturers Manual

REMARK/OBSERVATIONS:

Note:

Day time shall mean from 6.00 Hrs. to 22.00 Hrs.
Night time shall mean from 22.00 Hrs. to 6.00 Hrs.

Limits: Leq dB (A)

≤75 dB (A) For Day Time

≤70 dB (A) For Night Time

For HORIZON ANALYTICAL LABORATORY PVT.LTD.



MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER:

- Sample will be retained only for 15 days
- Above results indicate to the parameters mentioned only.
- Liability limited till issue of test reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F7/8.2.1

CLIENT'S NAME & ADDRESS M/s Cipla Ltd. Plot No. D-22, Unit III MIDC Kurkumbh, Tal- Daund, Dist- Pune	ULR NO.	TC1620826000016393
	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/704
	SAMPLING DATE	25/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	--
	END DATE OF ANALYSIS	--
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/DG-Noise/01A/2017

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
DG-Noise	Horizon Analytical Laboratory Pvt.Ltd.	--	--	--

RESULTS

SR. NO.	DESCRIPTION	UNIT	READING	STANDARDS
	TEST LOCATION (13:00 Hrs.)			
	DG Set No. 5 750 KVA			
01	D.G. SET (INSIDE ACOUSTIC)	dB(A)	102.8	
02	D.G. SET (0.5 MTR AWAY)	dB(A)	72.5	
03	INSESION LOSS AT 0.5 MTR AWAY FROM ACOUSTIC COVER	dB(A)	30.3	More than 25
	DG Set No. 4 750 KVA			
01	D.G. SET (INSIDE ACOUSTIC)	dB(A)	97.0	
02	D.G. SET (0.5 MTR AWAY)	dB(A)	71.1	
03	INSESION LOSS AT 0.5 MTR AWAY FROM ACOUSTIC COVER	dB(A)	25.9	More than 25

Instrument Used: Digital Sound Level Meter (070845)

Make: HTC Instruments

Calibration Date: 12/06/2025 **Next Calibration Due:** 11/06/2026

REMARK/OBSERVATIONS:

*Standards are given as per CPCB notification no. G.S.R. 371(E) dated 17 may 2002.

For HORIZON ANALYTICAL LABORATORY PVT.LTD.




Manisha Nargolkar
MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER :

- Sample will be retained only for 15 days
- Above results indicate to the parameters mentioned only
- Liability limited till issue of test reports only
- The test report shall not be produced for any legal identity or advertised without permission of lab.

ANNEXURE-XII Environment Management Cell

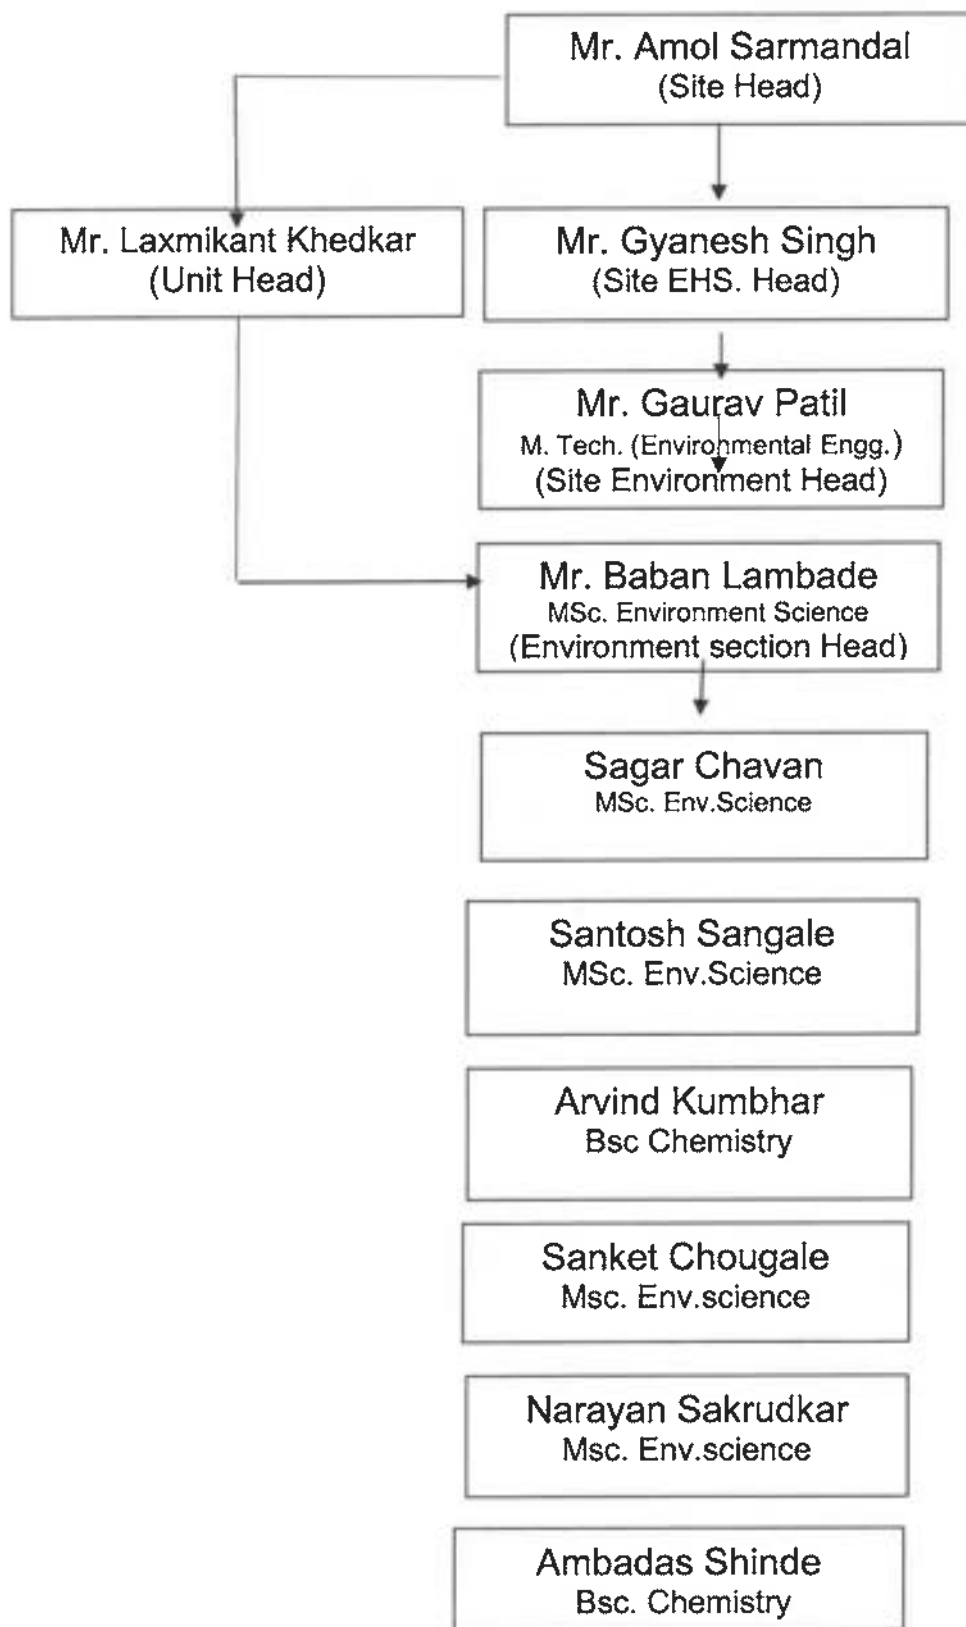

Annexure-XIII

Financial details:

a) Capital cost of the project : Rs. 168.56 Crores

b) Cost for Environmental protection measures (Lakhs)

Sr. No.	Environmental protection measures	Recurring Cost per annum	Capital cost
1	Air pollution control	Rs. 10 Lakhs	Rs. 43 Lakhs
2	Water pollution control	Rs. 41 Lakhs	Rs. 460 Lakhs
3	Noise pollution control	Rs. 01 Lakhs	Rs. 16 Lakhs
4	Environmental Monitoring and Management	Rs. 05 Lakhs	Rs. 27 Lakhs
5	Reclamation borrow / mined area	-	-
6	Occupational Health	Rs. 04 Lakhs	Rs. 20 Lakhs
7	Green belt	Rs. 01 Lakhs	Rs. 02 Lakhs
8	MEE+VTFD	Rs. 130 Lakhs	Rs. 186 Lakhs
Total		Rs. 192 Lakhs	Rs. 754 Lakhs

Annexure-XIV

FW: Half yearly EC compliance report for Cipla D-22 from June-25 to Nov-2025.



Deepak Bhosale/ETP/KKB

To: Arvind Kumbhar1/EHS/KKB-III; Sagar Chavan5/EHS/KKB; Baban Lambade/EHS/KKB



Six monthly EC compliance Cipla D22 from June-25 to Nov-2025.pdf
.pdf File

FYI

From: Deepak Bhosale/ETP/KKB

Sent: 01 December 2025 16:45

To: 'ecompliance-mh@gov.in' <ecompliance-mh@gov.in>

Subject: Half yearly EC compliance report for Cipla D-22 from June-25 to Nov-2025.

Respected Sir,

Please find the attached EC compliance report for Cipla D-22 from June-25 to Nov-25.

Regards,
Deepak Bhosale

Annexure-XV

