

CIPLA/EHS-ENV/KKB-II/03/2026

Date:01.06.2026

**Deputy Director General of Forests (Central),
West Central Zone,
Regional Office,
New Secretariate Building,**

**Opp. VCA Ground,
Civil Lines,
Nagpur-440 001.**

Subject: Half Yearly Environment Clearance Compliance Report

Ref. No: Environment clearance No. SIA/MH/IND3/70271/2018 dated 18th May 2023.

Respected Sir,

With reference to the above subject, we are hereby submitting the six-monthly Environment clearance compliance report for the period of Dec-2025 to May-2026.

1.Point wise compliance to Environment clearance No.SIA/MH/IND3/70271/2018 dated 18th May 2023 as Annexure -1.

This is for your information.

Kindly acknowledge receipt of the same.

Thanking You,

Your's faithfully,

For Cipla Ltd.

Rohan Parmar
BParmar
01.06.2026

Authorized Signatory

Encl: As Above.

Cipla Ltd.

(Export Oriented Unit), D-27, MIDC Industrial Area, Kurkumbh, Dist. Pune - 413 802.
P +91 2117 230600 F +91 2117 235232

Regd. Office - Cipla House, Peninsula Business Park, Ganpatrao Kadam Marg, Lower Parel, Mumbai 400013, India.
P +91 22 24826000 F +91 22 24826120 W www.cipla.com E-Mail contactus@cipla.com Corporate Identity Number L24239MH1935PLC002380

2

2

2

2

2

Annexure Summary

SR. NO.	ANNEXURE NO	ANNEXURE NAME	Page No.
1	Annexure-A	EC compliance Report	1-9
2	Annexure-I	Monitoring Reports	10-39
3	Annexure-II	CER Expenditure Plan	40-40
4	Annexure-III	Existing CER activities & Photographs	41-48
5	Annexure-IV	ETP flow diagram	49-49
6	Annexure-V	MVRE PO details	50-51
7	Annexure-VI	RWH System	52-53
8	Annexure-VII	Photographs of Sliding Gate & Turning Radius	54-54
9	Annexure-VIII	Photographs of Green Belt & GB Plan	55-55
10	Annexure-IX	CHWTSDF Letter	56-56
11	Annexure-X	Peso license	57-57
12	Annexure-XI	DIHS Certificate	58-58
13	Annexure-XII	Mock drill report & Safety Audit report	59-66
14	Annexure-XIII	Newspaper Advertisement	67-67
15	Annexure-XIV	Acknowledgement Copy of Six-Monthly Compliance	68-68
16	Annexure-XV	Screenshot of website	69-69
17	Annexure-XVI	Environment Management cell	70-70
18	Annexure-XVII	Health checkup record	71-80
19	Annexure-XVIII	Env. Statement.	81-87

ANNEXURE A

A report on compliance of various conditions stipulated in EC granted by State Environment Impact Assessment Authority (SEIAA), Department of Environment, Maharashtra vide its EC Identification No. EC23B021MH194305 dated 18th May 2023; for Expansion of Bulk Drugs & Intermediates Manufacturing Unit by Cipla Ltd. (Unit-II) located at Plot No. D-27, MIDC Kurkumbh, Tal.: Daund, Dist.: Pune, Maharashtra. The activity under the said EC of 18.05.2023 is yet to be implemented on site However the 18.05.2023 order is the latest EC, compliance of same is presented in following table-

No.	Conditions	Compliance Status
A.	Specific Conditions	
	SEAC Conditions -	
1	Condition No.1 PP to achieve the standard parameters stipulated for Bulk Drugs & Formulation (Pharmaceuticals) sectors in the Environment (Protection) Second Amendment Rule, 2021 dated 6 th August 2021 published by MoEFCC.	Completed Acknowledged. In the existing activity, the effluent, Ambient Air Quality Monitoring (AAQM), Stack Emissions, Workplace Emissions for VOC monitoring is being monitored through MoEFCC recognized laboratory – Horizon services analytical laboratory Pune. All parameters are well within the limits at all locations, as per the Environment (Protection) Second Amendment Rule, 2021. Monitoring reports are enclosed at Annexure- I
2	Condition No.2 PP to spend the entire CER funds before commissioning proposed activity in calculation with the District Collector.	Completed CER fund is allocated as per District collector approved order. District Collector Order & Photographs of the activities as per District Collector Order are enclosed. Annexure- II.
3	Condition No.3 PP to provide an Online Continuous Monitoring System connected to the servers of CPCB & MPCB	Completed As the unit implemented 'Zero Liquid Discharge' (ZLD), PTZ camera along with Flow meter have been provided as per CPCB guidelines, 2018
4	Condition No.4 PP to provide Zero Liquid Discharge Effluent Treatment Plant.	Completed Effluent generated from existing activity is segregated in two streams viz. Stream-I (Low COD & Low TDS) & Stream-II (High COD & High TDS). Stream -I effluent is treated in Pri-primary followed by secondary and tertiary treatment with capacity 150 CMD & treated effluent is recycled back for cooling tower make-up. Thereby, achieving 'Zero Liquid Discharge' (ZLD). The stream-II effluent is treated in MEE followed by ATFD. The MEE condensate is going to mix with stream-I. MEE Reject is forwarded to ATFD Plant. ATFD salt is forwarded to

No.	Conditions	Compliance Status
		CHWTSDF. Same practice will be followed under expansion as well. ETP flow diagram Annexure III
5	Condition No.5 PP to explore the possibility to assess techno-economic feasibility of using technology for MEE such as low temperature/ mechanical vapor compressor etc. to reduce operation cost and use of natural resources.	Completed Industry has explored technology as a substitute for MEE. Therein, industry is going to install Mechanical Vapor Recompression Evaporator (MVRE) replacing MEE for treatment of strong stream effluent and achieving ZLD. Further, Industry is issued work order to install MVRE on buyback basis from Lombardyne industries, Pune. MVRE work order issued is enclosed herewith at Annexure -IV .
6	Condition No. 6 PP to complete the rainwater harvesting facility before the commissioning of the manufacturing activity.	Completed The industry has implemented a Rainwater Harvesting system. Being a chemical based industry Roof top Rainwater is collected from administration, Utility, engineering buildings. The harvested rainwater is used for cooling tower make-up purposes. A photograph of the same is enclosed in Annexure-V .
7	Condition No. 7 PP to provide a sliding gate at entry and exit to achieve a maximum turning radius of vehicles entering the site.	Industry has provided sliding gates at entry and exit. Also, 9 M turning radius is provided in the industry premises for smooth transportation of vehicles. Photographs of entry gate is attached at Annexure – VI .
	SEIAA Conditions -	
1	Condition No. 1	Completed
2	PP to submit the plan approved by MIDC dated 28.06.2022. As per the said plan, the plot area is 160000 M ² , green belt area of 37150.05 is provided i.e. 23.2% of the total plot area. To provide balanced green belt PP has purchased land at Gat. No. 182 of Roti Village in Daund and provided a green belt of 15,800 M ² making the total green belt 33% of the plot area. Condition No. 2 PP to undertake Miyawaki plantation of native and indigenous trees such as Banyan, Peepal, Neem, Jamun, and other suitable trees as per the Forest Department, Govt. of Maharashtra circular no. SaVaVi-2019/C.R.3/F-11, dated 25 th June 2019. The said plantation to be completed in the first year of operation of Environmental Clearance under expert guidance of Miyawaki experts/ arborist.	The total plot area of Cipla Ltd. (Unit - II) is 16 Ha. Industry has developed a green belt to the tune of 3.71 Ha (23.2%) where under 4,970 Nos. of trees are planted in industrial premises. As per the DoE & MoEFCC guidelines, GB to the tune of 33% of TPA is required to be developed. However, no open area is available on the existing industry plot. As such, the PP decided to implement the additional GB on a new land parcel preferably in the vicinity of the industrial plot. Therefore M/s. Cipla Ltd. has purchased a new land parcel at Gat No. 182 and at 3.7 Km from its existing plot the Roti village of Daund Taluka. This land has been solely acquired for GB development. Therefore, the total green belt area will be 5.29 Ha which is 33 % of the total plot area (16 Ha). Under the new land, Miyawaki plantation of native and indigenous trees is completed. Photographs of existing green belt in the industry premises, and Miyawaki plantation are enclosed in Annexure – VII .

No.	Conditions	Compliance Status																																															
3	Condition No. 3 PP to strictly observe the Solid Waste Management Rules, 2016 as amended from time to time.	Noted Solid Waste generated in industrial premises is in the form of Plastic, Glass, Ferrous, Wooden, Metal Scrap, Discarded containers, drums, carboys, etc., Battery Waste & E-Waste. The same is sold to the re-processors. - M/s green recycling. The same practice will be followed under expansion as well.																																															
4	Condition No. 4 PP to strictly observe the Hazardous and Other Waste (Management & Transboundary Movement) Rules, 2016 as amended from time to time.	Noted Details of hazardous waste generated in premises are as below: a. Hazardous Waste: <table><tr><th>No.</th><th>Description</th><th>Cat.</th><th>QTY.</th><th>Disposal</th></tr><tr><td>1</td><td>Used / Spent Oil</td><td>5.1</td><td>0.3KL/M</td><td rowspan="2">Sale to authorized party/CHWTSDF</td></tr><tr><td>2</td><td>Spent organic Solvents</td><td>28.6</td><td>377.7KL/M</td></tr><tr><td>3</td><td>Spent catalyst</td><td>28.2</td><td>0.03MT/M</td><td rowspan="2">Sale to authorized party/CHWTSDF/Co-processing</td></tr><tr><td>4</td><td>Spent Carbon</td><td>28.3</td><td>0.095MT/M</td></tr><tr><td>5</td><td>Date expired, Products</td><td>28.5</td><td>1 MT/M</td><td>CHWTSDF</td></tr><tr><td>6</td><td>Off-specification products</td><td>28.4</td><td>0.5MT/M</td><td>CHWTSDF</td></tr><tr><td>7</td><td>Empty Barrels /container/ liners contaminated with hazardous waste / chemicals</td><td>33.1</td><td>200 No/M</td><td>Sale to authorized party</td></tr><tr><td>8</td><td>Chemical sludge from wastewater treatment</td><td>35.3</td><td>15 MT/M</td><td rowspan="2"></td></tr><tr><td>9</td><td>Concentration or</td><td>37.3</td><td>48 MT/M</td></tr></table>	No.	Description	Cat.	QTY.	Disposal	1	Used / Spent Oil	5.1	0.3KL/M	Sale to authorized party/CHWTSDF	2	Spent organic Solvents	28.6	377.7KL/M	3	Spent catalyst	28.2	0.03MT/M	Sale to authorized party/CHWTSDF/Co-processing	4	Spent Carbon	28.3	0.095MT/M	5	Date expired, Products	28.5	1 MT/M	CHWTSDF	6	Off-specification products	28.4	0.5MT/M	CHWTSDF	7	Empty Barrels /container/ liners contaminated with hazardous waste / chemicals	33.1	200 No/M	Sale to authorized party	8	Chemical sludge from wastewater treatment	35.3	15 MT/M		9	Concentration or	37.3	48 MT/M
No.	Description	Cat.	QTY.	Disposal																																													
1	Used / Spent Oil	5.1	0.3KL/M	Sale to authorized party/CHWTSDF																																													
2	Spent organic Solvents	28.6	377.7KL/M																																														
3	Spent catalyst	28.2	0.03MT/M	Sale to authorized party/CHWTSDF/Co-processing																																													
4	Spent Carbon	28.3	0.095MT/M																																														
5	Date expired, Products	28.5	1 MT/M	CHWTSDF																																													
6	Off-specification products	28.4	0.5MT/M	CHWTSDF																																													
7	Empty Barrels /container/ liners contaminated with hazardous waste / chemicals	33.1	200 No/M	Sale to authorized party																																													
8	Chemical sludge from wastewater treatment	35.3	15 MT/M																																														
9	Concentration or	37.3	48 MT/M																																														

No.	Conditions	Compliance Status																
		<table><tr><td></td><td>evaporation residue</td><td></td><td></td><td rowspan="3">CHWTSDf</td></tr><tr><td>10</td><td>Sludge from wet scrubber</td><td>37.1</td><td>0.025 MT/M</td></tr><tr><td>11</td><td>Process residue and waste</td><td>28.1</td><td>30MT/M</td></tr></table>				evaporation residue			CHWTSDf	10	Sludge from wet scrubber	37.1	0.025 MT/M	11	Process residue and waste	28.1	30MT/M	
	evaporation residue			CHWTSDf														
10	Sludge from wet scrubber	37.1	0.025 MT/M															
11	Process residue and waste	28.1	30MT/M															
		Generated hazardous waste is forwarded to CHWTSDf, Ranjangoan. Membership of CHWTSDf for disposal of hazardous Waste is already procured. Membership number is MEPL/33003270 dated 02.05.2023 valid up to 01.05.2028. Copy of membership is enclosed at Annexure - VIII . The same practice will be followed under expansion as well.																
5	Condition No. 5 PP to identify all sources of fugitive air pollution on site and provide pollution control measures to mitigate pollution and meet the standard parameters stipulated in the Environment (Protection)Rule 1986 amended- timer to time & Air (Prevention and Control of Pollution) Act, 1981 amended time to time.	completed To control process emissions released during the manufacturing process scrubbers are installed. The loading and unloading section of products and raw materials have also been provided with an ID Fan followed by Scrubbers for controlling the emissions released during the loading and unloading of the finished product and raw materials. The industry has constructed well-paved roads for the prevention of dust emissions. Further, the industry has regularly conducted monitoring of various Environmental Attributes viz. Ambient Air Quality, Scrubber area emissions, Stack Emission, through a MoEFCC & NABL-approved laboratory. Monitoring reports are enclosed in Refer Annexure - I .																
6	Condition No. 6 PP to ensure storage of chemicals as per the Manufacture, Storage, and Import of Hazardous Chemicals Rules,) 1989 amended time to time to ensure no release of any chemical to the atmosphere and leakage to the soil	Noted Adequate provisions are made for the storage and handling of hazardous chemicals. The hazardous chemicals are stored in tanks, drums, and cylinders as per the MSIHC rules. Also, the industry has prepared an On-site emergency management plan.																
7	Condition No. 7 PP to ensure transport, storage, handling, and use of the flammable/toxic chemicals as per conditions stipulated in the license/approval- of the Petroleum & Explosive Safety Organization (PESO).	completed Flammable/toxic chemicals are stored in drums & carboys. Dedicated storage area is provided to store such chemicals. Solvents are stored in barrels. This reduces the risk of fire or any explosion due to bulk storage tanks. The barrels are then stored in a defined area with all safety measures like firefighting, alarms, waterproof electric fitting etc. Proper earthing has been provided to all electrical equipment. Also, flame arresters & lightning arrestors are provided for the tank farm.																

No.	Conditions	Compliance Status
		Petroleum Explosive Safety Organization (PESO) license for storage of chemicals is granted. PESO license is Procured vide letter no. P/HQ/MH/15/5768 (P182874) dated 05.12.2017 (Valid up to 31.12.2027) is enclosed at Annexure- IX
8	Condition No. 8 PP to obtain approval and License from the Directorate of Industrial Health & Safety (DIHS) for proposed project and implement all conditions stipulated therein. PP to carry out Safety Audit as stipulated in the Maharashtra Factories Rules, 1963 and ensure compliance of recommendation of the Audit.	completed The industry has obtained the Directorate of Industrial Health & Safety (DIHS) license vide no. 10005797 dated 05.10.2022. Valid up to 31.12.2026. The license copy is attached to Annexure -X Industry is following the safety measures during manufacturing process as well as in materials' handling. Furthermore, training and mock drills are conducted for employees working in the industry twice in year on safety and health aspects of chemical handling. Latest mock drill was conducted on 31.10.2025. A safety audit was conducted on 28.12.2024. Details of mock drill & Safety audit report is attached at Annexure – XI.
9	Condition No. 9 PP to provide solar energy for illumination of Administrative Building, Street Lights and parking Area	Noted In industrial areas, LED lighting is provided also solar energy is used for lighting purposes.
10	Condition No. 10 PP to ensure use of briquette /bio coal/pellets/ or any such suitable product derived from scientific processing of the appropriate stream of dry waste/agricultural waste, not less than 50% of the total fuel requirement to the boiler	Noted Under existing unit, two boilers of capacity 2 TPH each are installed on site, which operate on LSHS and common stack of 30 M is provided. HSD is used as fuel for the same & a stack of 30 M is provided. No new boiler will be provided for this expansion activity.
11	Condition No. 11 PP to provide roof top Rainwater Harvesting facility	Completed The industry has Implemented a Rainwater Harvesting system. Being a chemical based industry Roof top Rainwater is collected from administration, Utility, engineering buildings. The harvested rainwater is used for cooling tower purposes. The photograph of the same is enclosed Ref. Annexure V.
12	Condition No. 12 PP to ensure that the proposed project is a ZLD	Completed, Effluent generated from existing activity is segregated into two streams viz. Stream-I (Low COD & Low TDS) & Stream-II (High COD & High TDS). Stream -I effluent is treated in ETP of capacity 150 CMD & treated effluent is recycled back for cooling tower make-up. Thereby, achieving 'Zero Liquid Discharge' (ZLD). The stream-II effluent is treated in MEE followed by ATFD. The MEE condensate is going to mix with stream-I.MEE Reject is

No.	Conditions	Compliance Status																
		forwarded to ATFD Plant , ATFD salt is forwarded to CHWTSDf. Same practice will follow under expansion as well.																
B	General Conditions																	
1	Condition No. 1 The project proponent shall advertise at least in two local newspapers widely circulated in the region around the project, one of which shall be in the Marathi language of the local concerned within seven days of issue of this letter, informing that the project has been accorded Environmental Clearance and copies of Environmental Clearance letter are available with the Maharashtra Pollution Control Board, website of the company and may also be seen at Website at http://parivesh.nic.in	Completed Industry published newspaper advertisements regarding the grant of EC in two local newspapers (Punya Nagari & Financial Express, Pune Ed.) on 17.07.2023. Copies of Newspaper advertisements are enclosed in Annexure – XII .																
2	Condition No. 2 The Proponent shall upload the status of compliance (soft copies) of the Environmental Clearance conditions including monitoring data of air, water, soil, noise, etc., on their website and shall update the same periodically. The half-yearly compliance report shall simultaneously be submitted to the Maharashtra Pollution Controls Board, SEIAA and the Regional Office of MoEFCC at Nagpur, on 1 st June & 1 st December of each calendar year	The industry regularly submits a six-monthly compliance report. Acknowledgment of the six-monthly report for the period Dec 2024 to May.2025 was submitted on 01.06.2025. Acknowledgment of the same is attached in Annexure – XIII . Environment statement compliances etc. on the industrial website. A screen shot of the website is attached in Annexure -XIV . http://www.cipla.com/about-us/manufacturing																
3	Condition No. 3 Separate funds shall be allocated for the implementation of the Environmental Management Plan along with item-wise break-up and a specific timeline for its completion. The cost shall be included as part of the project cost. The funds earmarked for the environmental protection measures shall not be diverted for other purposes and year-wise expenditure should be reported to the MPCB and the SEIAA	Completed The industry has earmarked a capital cost of Rs. 840 Lakhs & the recurring cost (O & M) is 160 Lakhs. Details are given in the following table – <table><tr><th>No</th><th>Description</th><th>Capital (Rs. Lakhs)</th><th>O & M/A (Rs. Lakhs)</th></tr><tr><td>1</td><td>Air Pollution Control: Stack & Scrubbers</td><td>300</td><td>10</td></tr><tr><td>2</td><td>Water Pollution: ETP, MEE, ATFD & OCMS to ETP</td><td>400</td><td>120</td></tr><tr><td>3</td><td>Noise Pollution: Insulation, Isolation, Attenuation Infrastructure, PPEs</td><td>20</td><td>5</td></tr></table>	No	Description	Capital (Rs. Lakhs)	O & M/A (Rs. Lakhs)	1	Air Pollution Control: Stack & Scrubbers	300	10	2	Water Pollution: ETP, MEE, ATFD & OCMS to ETP	400	120	3	Noise Pollution: Insulation, Isolation, Attenuation Infrastructure, PPEs	20	5
No	Description	Capital (Rs. Lakhs)	O & M/A (Rs. Lakhs)															
1	Air Pollution Control: Stack & Scrubbers	300	10															
2	Water Pollution: ETP, MEE, ATFD & OCMS to ETP	400	120															
3	Noise Pollution: Insulation, Isolation, Attenuation Infrastructure, PPEs	20	5															

No.	Conditions	Compliance Status			
		4	Occupational Health and Safety	50	10
		5	Green Development & Rainwater Harvesting	55	10
		6	Environmental Monitoring and Management	15	5
		Total		Rs. 840	Rs. 160
4	Condition No. 4 A separate Environmental Management Cell with qualified personnel shall be set up for the implementation of the stipulated environmental safeguards	Completed A separate Environmental Management cell of 10 well-qualified personnel has been established. Annexure -XV			
5	Condition No. 5 In the event of failure of any pollution control equipment, the manufacturing activity shall be immediately stopped safely till the effective functioning of pollution control equipment is regained	Noted In case of failure, the entire manufacturing process will get shutdown with immediate effect and shall not be restarted until the desired efficiency has been achieved.			
6	Condition No. 6 PP to strictly follow conditions stipulated in the Consent to Establish/Operate issued by the Maharashtra Pollution Control Board	Noted Industry is strictly following the stipulations made by Central Pollution Control Board (CPCB), State Pollution Control Board (SPCB) and any other statutory authority			
7	Condition No. 7 PP is to provide separate drains for storm water and effluent and ensure that the storm water drains are dry all the time and in no case, the effluent shall mix with the storm water drain.	Noted The compliance is already followed by the industry. The Effluent generated at various locations is being transferred through a closed pipeline up to ETP Storm water collection and conveyance arrangement through separate gutters has been provided in the premises. The storm water is discharged at the lowest point in the premises of industry and through percolation and infiltration it enriches the groundwater table. Therefore, mixing of water doesn't take place on site. Requisite arrangements are provided by the industry as designed.			
8	Condition No. 8 Periodic Monitoring of groundwater in the study area as marked in the Environmental Impact Assessment Report shall be undertaken and results analyzed to ascertain any	Noted, Periodic Monitoring of groundwater in the study area will be conducted at 9 locations as marked in the EIA report. Same shall be undertaken after the commencement of expansion project. Industry hereby assures that the reports will be submitted regularly to MPCB & MoEFCC			

No.	Conditions	Compliance Status
	change in the quality of water. Results shall be regularly submitted to the Maharashtra Pollution Control Board	through half-yearly compliance report. Due to stipulated norms of MIDC, industries are not allowed to withdraw or recharge the groundwater within the premises. Hence, the source of groundwater (bore well/other source) is not present in industry premises.
9	Condition No. 9 The overall noise levels in and around the factory premises shall be kept within the prescribed standard under the Environment (Protection) Act, 1986 and Rule, 1989 as amended from time to time by providing adequate noise control measures and protective equipment like earmuff and ear plug, etc.	Completed Major noise-generating sources at the integrated project complex are boilers, reactors, compressors, MEE treatment Plant D.G. Set, etc. All preventive measures such as regular operation & maintenance of pumps, motors, and compressors are carried out and enclosures are provided to abate noise levels at the source. The overall noise levels in and around the plant area are maintained within the standards prescribed under the Environment (Protection) Act, 1986, 1989 Rules. Workers working in noisy areas are provided with personal protective equipment such as ear plugs, earmuffs, etc. Ambient and Work-zone noise monitoring is periodically carried out to check noise levels in and around industrial premises and noise control is done through acoustic enclosures. Noise levels are being monitored at 5 locations each for ambient and work zones. The noise levels are conformed as per prescribed standards, i.e. 75 dB (A) during daytime and 70 dB (A) during nighttime. Monitoring reports of noise monitoring are enclosed in Refer Annexure- I.
10	Condition No. 10 Adequate safety measures should be ensured to limit the risk zone within the factory premises. A leak detection system shall be installed for early detection and mitigation purposes	Completed Safety procedures for High-risk zones are defined and implemented, and close monitoring of the same is being followed. The entire plant operations are through DCS, hence continuously monitored and controlled for all aspects. Also, a Leak detection system (continuous monitoring of formaldehyde) is installed at two locations (Drum Storage Area & Solvent Dispensing Area). Periodical calibration and testing are being carried out through a third party to ensure the operability. Dedicated staff is hired to carry out daily checks on the leak detection system & DCS system.
11	Condition No. 11 PP to scrupulously follow the requirements of the Maharashtra Factories Act, 1948 & Rules 1963 as amended from time to time.	Completed Firefighting arrangements have been provided on site as per Factories Act. Industry has installed & provided fire-fighting system infrastructure comprising of fire water lines, fire hydrants, fire extinguishers etc. at all strategic & fire prone areas in the industry. Moreover, Mock drills are being carried out once in six months. The latest mock drill was conducted on 13.05.2025. Safety audit was

No.	Conditions	Compliance Status
		conducted in 28.12.2024. Industry has an OHC and it conducts health checkup camps for all workers once 6 months and the records of the same are kept on site. PPEs are provided to all workers during working hours. The first aid facilities in the occupational health center are strengthened and regular medical test record of each employee is maintained separately. Latest health checkup camp was carried out during 02.07.2025. Reports are enclosed at Annexure - XVI.
12	Condition No. 12 The Environmental Statement for each financial year ending on 31st March in Form• V is mandated to be submitted by the Project Proponent to the concerned Pollution Control Board as prescribed under the Environment (Protection) Rule, 1989 as amended from time to time, it shall also be put on the website of the company along with the status of the compliance of the conditions stipulated in the Environmental Clearance letter	Completed The Environmental Statement (ES) for each financial year ending 31st March in Form-V is submitted w.r.t. existing unit to Maharashtra Pollution Control Board. The latest Environmental statement for FY 2024-2025 submitted on 29.09.2025 is enclosed in Annexure-XVII.

ANNEXURE-I



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 2

CLIENT'S NAME & ADDRESS M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	ULR NO	HALPL/LAB/NABL/F/7.8.2.1
	REPORT DATE	TC1620826000016354
	LAB REFERENCE NO.	05/03/2026
	SAMPLING DATE	HALPL/LAB/AA/703
	SAMPLE RECEIPT DATE	23&24/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	--
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/Amb-Noise/01:2017

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Noise	Horizon Analytical Laboratory Pvt.Ltd.	--	--	Near Main Gate

SR. NO.	TIME	UNIT	RESULTS	
			RESULT (DAY TIME)	RESULT (NIGHT TIME)
1	11:25	dB(A)	65.3	
2	12:25	dB(A)	69.6	
3	13:25	dB(A)	70.1	
4	14:25	dB(A)	72.3	
5	15:25	dB(A)	69.7	
6	16:25	dB(A)	68.9	
7	17:25	dB(A)	64.5	
8	18:25	dB(A)	68.9	
9	19:25	dB(A)	64.2	
10	20:25	dB(A)	62.3	
11	21:25	dB(A)	64.5	
12	22:25	dB(A)		61.2
13	23:25	dB(A)		60.3
14	24:25	dB(A)		58.5
15	01:25	dB(A)		56.7
16	02:25	dB(A)		55.5
17	03:25	dB(A)		57.8
18	04:25	dB(A)		59.6
19	05:25	dB(A)		60.5
20	06:25	dB(A)	62.8	

DISCLAIMER:

- Sample will be retained only for 15 days.
- Above results indicate to the parameters mentioned only.
- Liability limited till 5 days of 9 reports only.
- The test report shall not be produced for any legal identity or otherwise without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

Page 2 of 2

21	07:25	dB(A)	60.7	
22	08:25	dB(A)	62.3	
23	09:25	dB(A)	63.3	
24	10:25	dB(A)	67.5	
		Day Time Leq	67.36	--
		Night Time Leq	--	59.14

Instrument Used: DIGITAL Sound Level Meter (data logging) Q697688

Make: Lutron Make

Calibration Date: 27/10/2025 **Next Calibration Due:** 26/10/2026

REMARK/OBSERVATIONS:

Limits:

≤75 dB(A) For Day Time

≤70 dB(A) For Night Time

Note: Day time shall mean from 6:00 Hrs. to 22:00 Hrs.


Night time shall mean from 22:00 Hrs. to 6:00 Hrs.

All Noise levels are within limit given as per Noise Pollution (Regulation & Control) Rules 2000

verified
G. S. S. S.

For HORIZON ANALYTICAL LABORATORY PVT.LTD.




MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER:

- Sample will be retained only for 15 days.
- Above results indicate to the parameters mentioned only.
- Liability limited till issue of 10 reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 2

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	ULR NO	TC1620826000016355
	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/703
	SAMPLING DATE	23&24/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	—
	END DATE OF ANALYSIS	—
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/Amb-Noise/01:2017

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Noise	Horizon Analytical Laboratory Pvt.Ltd.	—	—	Near ETP

RESULTS

SR. NO.	TIME	UNIT	RESULT (DAY TIME)	RESULT (NIGHT TIME)
1	11:55	dB(A)	63.2	
2	12:55	dB(A)	66.5	
3	13:55	dB(A)	63.4	
4	14:55	dB(A)	62.1	
5	15:55	dB(A)	65.2	
6	16:55	dB(A)	63.5	
7	17:55	dB(A)	65.7	
8	18:55	dB(A)	64.8	
9	19:55	dB(A)	61.3	
10	20:55	dB(A)	60.9	
11	21:55	dB(A)	58.8	
12	22:55	dB(A)		57.6
13	23:55	dB(A)		57.0
14	24:55	dB(A)		55.1
15	01:55	dB(A)		56.4
16	02:55	dB(A)		57.9
17	03:55	dB(A)		56.3
18	04:55	dB(A)		57.5
19	05:55	dB(A)		58.4
20	06:55	dB(A)	59.6	

DISCLAIMER:

- Sample will be retained only for 15 days.
- Above results indicate to the parameters mentioned only.
- Liability limited till issue of 11 reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

Page 2 of 2

21	07:55	dB(A)	60.7	
22	08:55	dB(A)	62.4	
23	09:55	dB(A)	63.8	
24	10:55	dB(A)	67.5	
		Day Time Leq	63.74	--
		Night Time Leq	--	57.13

Instrument Used: DIGITAL Sound Level Meter (data logging) Q697685

Make: Lutron Make

Calibration Date: 27/10/2025 **Next Calibration Due:** 26/10/2026

REMARK/OBSERVATIONS:

Limits:

≤75 dB(A) For Day Time

≤70 dB(A) For Night Time


Note: Day time shall mean from 6:00 Hrs. to 22:00 Hrs.

Night time shall mean from 22:00 Hrs. to 6:00 Hrs.

All Noise levels are within limit given as per Noise Pollution (Regulation & Control) Rules 2000

verified,
23.11.2026

For HORIZON ANALYTICAL LABORATORY PVT.LTD.



Manisha Nargolkar
F MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER:

- Sample will be retained only for 15 days
- Above results indicate to the parameters mentioned only
- Liability limited till issue of 12 reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 2

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	ULR NO	TC1620826000016356
	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/703
	SAMPLING DATE	24&25/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	—
	END DATE OF ANALYSIS	—
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/Amb-Noise/01:2017

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Noise	Horizon Analytical Laboratory Pvt Ltd.	—	—	Near Boiler

RESULTS

SR. NO.	TIME	UNIT	RESULT (DAY TIME)	RESULT (NIGHT TIME)
1	11:00	dB(A)	65.3	
2	12:00	dB(A)	66.4	
3	13:00	dB(A)	65.9	
4	14:00	dB(A)	62.3	
5	15:00	dB(A)	61.3	
6	16:00	dB(A)	63.7	
7	17:00	dB(A)	68.1	
8	18:00	dB(A)	66.4	
9	19:00	dB(A)	64.2	
10	20:00	dB(A)	63.8	
11	21:00	dB(A)	59.7	
12	22:00	dB(A)		55.9
13	23:00	dB(A)		52.3
14	24:00	dB(A)		51.6
15	01:00	dB(A)		47.9
16	02:00	dB(A)		49.6
17	03:00	dB(A)		48.6
18	04:00	dB(A)		50.4
19	05:00	dB(A)		56.7
20	06:00	dB(A)	60.3	

DISCLAIMER

- Sample will be retained only for 15 days
- Above results indicate to the parameters mentioned only
- Liability limited till issue of 13 reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

Page 2 of 2

21	07:00	dB(A)	63.4	
22	08:00	dB(A)	64.8	
23	09:00	dB(A)	65.9	
24	10:00	dB(A)	66.4	
		Day Time Leq	64.80	--
		Night Time Leq	--	52.74

Instrument Used: DIGITAL Sound Level Meter (data logging) Q697686

Make. Lutron Make

Calibration Date: 27/10/2025 Next Calibration Due: 26/10/2026

REMARK/OBSERVATIONS:

Limits:

≤75 dB(A) For Day Time

≤70 dB(A) For Night Time

Note: Day time shall mean from 6:00 Hrs. to 22:00 Hrs.

Night time shall mean from 22:00 Hrs. to 6:00 Hrs.

All Noise levels are within limit given as per Noise Pollution (Regulation & Control) Rules 2000

Very Good
23.03.2026

For HORIZON ANALYTICAL LABORATORY PVT.LTD.



F MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER

- Sample will be retained only for 15 days. • Above results indicate to the parameter is mentioned only. • Liability limited till issue of 14 reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 2

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS	ULR NO	TC1620826000016357
M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/703
	SAMPLING DATE	24&25/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	--
	END DATE OF ANALYSIS	--
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/Amb- Noise/01:2017

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Noise	Horizon Analytical Laboratory Pvt.Ltd.	--	--	Near Pump House

RESULTS

SR. NO.	TIME	UNIT	RESULT (DAY TIME)	RESULT (NIGHT TIME)
1	11:30	dB(A)	68.5	
2	12:30	dB(A)	70.1	
3	13:30	dB(A)	67.5	
4	14:30	dB(A)	62.3	
5	15:30	dB(A)	66.4	
6	16:30	dB(A)	65.9	
7	17:30	dB(A)	64.3	
8	18:30	dB(A)	65.2	
9	19:30	dB(A)	62.6	
10	20:30	dB(A)	65.9	
11	21:30	dB(A)	66.8	
12	22:30	dB(A)		54.7
13	23:30	dB(A)		53.8
14	24:30	dB(A)		52.0
15	01:30	dB(A)		51.7
16	02:30	dB(A)		50.9
17	03:30	dB(A)		52.1
18	04:30	dB(A)		53.4
19	05:30	dB(A)		55.3
20	06:30	dB(A)	64.6	

DISCLAIMER

- Sample will be retained only for 15 days. • Above results indicate to the parameters mentioned only. • Liability limited to issue of 15 reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

Page 2 of 2

21	07:30	dB(A)	65.3	
22	08:30	dB(A)	66.4	
23	09:30	dB(A)	68.7	
24	10:30	dB(A)	69.9	
		Day Time Leq	66.84	
		Night Time Leq	—	53.23

Instrument Used: DIGITAL Sound Level Meter (data logging) Q697687

Make. Lutron Make

Calibration Date: 27/10/2025 **Next Calibration Due:** 26/10/2026

REMARK/OBSERVATIONS:

Limits:

≤75 dB(A) For Day Time

≤70 dB(A) For Night Time

Note: Day time shall mean from 6:00 Hrs. to 22:00 Hrs.

Night time shall mean from 22:00 Hrs. to 6:00 Hrs.

All Noise levels are within limit given as per Noise Pollution (Regulation & Control) Rules 2000

Very Good.

25.03.2026

For **HORIZON ANALYTICAL LABORATORY PVT.LTD.**



MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER

• Sample will be returned only for 15 days. • Above results indicate to the parameters mentioned only. • Liability limited till issue of 16 reports only.
• The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS	ULR NO.	TC1620826000016350
M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/703
	SAMPLING DATE	23&24/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14:2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Air	Horizon Analytical Laboratory Pvt.Ltd.	Plastic Bottles and Bags	--	Near Main Gate

RESULTS

SR. NO.	DESCRIPTION	UNIT	RESULTS	NAAQS LIMITS	TEST METHOD REFERENCE
01	Date of Sampling	DD/MM/YY	23&24/02/2026		
02	Test Location		Near Main Gate		
03	Time of Sampling	Hrs.	11:10		
04	Temperature (Max./Min)	Deg C	34/20		
05	Relative Humidity	% RH	46		
06	Sampling Duration	Hrs	24		
07	Respirable Suspended Particulate Matter (PM ₁₀)	µg/m ³	68.29	100	IS 5182(part 23)
08	Fine Particulate Matter (PM _{2.5})	µg/m ³	35.16	60	IS 5182(part 24)
09	Sulphur Dioxide as SO ₂	µg/m ³	13.41	80	IS 5182(part 2): Sec.1
10	Nitrogen Dioxide as NO ₂	µg/m ³	32.80	80	IS 5182(part 6)
11	Ozone as O ₃	µg/m ³	10.12	100	IS 5182(part 9)
12	Ammonia as NH ₃	µg/m ³	BDL (<30)	400	IS 5182(part 25)
13	Lead as Pb	µg/m ³	BDL (<0.05)	1.0	IS 5182 (Part 22)
14	Arsenic as As	ng/m ³	BDL (<3)	06	HALPL/LAB/NABL/AA/22:2021
15	Nickel as Ni	ng/m ³	BDL (<7)	20	IS 5182(part 26)

Equipment Used: - Fine Dust Sampler, Sr.No.2218 (Polltech Make)

Date of Calibration: -07/08/2025 Next Calibration due: -06/08/2026

REMARKS/OBSERVATIONS: -


NAAQS: - National Ambient Air Quality Standards

Limits as per NAAQS Monitoring & Analysis Guidelines Volume-I (2009)

BDL-Below Detectable Level

Verified.
09-03-2026

For **HORIZON ANALYTICAL LABORATORY PVT.LTD.**



MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER

- Sample will be retained only for 15 days.
- Above results indicate to the parameters mentioned only.
- Liability limited till issue of test reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	REPORT NO.	HALPL/LAB/AA/16350
	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/703
	SAMPLING DATE	23&24/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14:2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Air	Horizon Services	Plastic Bottles and Bags	-	Near Main Gate

RESULTS

SR. NO.	DESCRIPTION	UNIT	RESULTS	NAAQS LIMITS	TEST METHOD REFERENCE
01	Date of Sampling	DD/MM/YY	23&24/02/2026		
02	Test Location		Near Main Gate		
03	Time of Sampling	Hrs.	11:10		
04	Temperature (Max./Min)	Deg C	34/20		
05	Relative Humidity	% RH	46		
06	Sampling Duration	Hrs	24		
07	Carbon monoxide as CO	mg/m ³	0.099	2.0	IS 5182 (Part 10)
08	Benzene as C ₆ H ₆	µg/m ³	BDL (<4)	05	IS 5182 (Part 11)
09	Benzo (a) Pyrene as Ba(a)P	ng/m ³	BDL (<0.5)	01	IS 5182 (Part 12)
10	Hydrogen Bromide (HBr)	mg/m ³	BDL (<1.32)	N.S.	HALPL/LAB/AA/04:2021


REMARKS/OBSERVATIONS: -

NAAQS: - National Ambient Air Quality Standards

Limits as per NAAQS Monitoring & Analysis Guidelines Volume-I (2009)

BDL-Below Detectable Level

Verified by
CQ 23.02.2026



For HORIZON SERVICES

MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	ULR NO.	TC1620826000016351
	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/703
	SAMPLING DATE	23&24/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14:2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Air	Horizon Analytical Laboratory Pvt.Ltd.	Plastic Bottles and Bags	--	Near ETP

RESULTS

SR. NO.	DESCRIPTION	UNIT	RESULTS	NAAQS LIMITS	TEST METHOD REFERENCE
01	Date of Sampling	DD/MM/YY	23&24/02/2026		
02	Test Location		Near ETP		
03	Time of Sampling	Hrs.	11:40		
04	Temperature (Max./Min)	Deg C	34/20		
05	Relative Humidity	% RH	46		
06	Sampling Duration	Hrs	24		
07	Respirable Suspended Particulate Matter (PM ₁₀)	µg/m ³	63.19	100	IS 5182(part 23)
08	Fine Particulate Matter (PM _{2.5})	µg/m ³	33.56	60	IS 5182(part 24)
09	Sulphur Dioxide as SO ₂	µg/m ³	12.14	80	IS 5182(part 2): Sec. 1
10	Nitrogen Dioxide as NO ₂	µg/m ³	28.70	80	IS 5182(part 6)
11	Ozone as O ₃	µg/m ³	14.09	100	IS 5182(part 9)
12	Ammonia as NH ₃	µg/m ³	BDL (<30)	400	IS 5182(part 25)
13	Lead as Pb	µg/m ³	BDL (<0.05)	1.0	IS 5182 (Part 22)
14	Arsenic as As	ng/m ³	BDL (<3)	06	HALPL/LAB/NABL/AA/22:2021
15	Nickel as Ni	ng/m ³	BDL (<7)	20	IS 5182(part 26)

Equipment Used: - Fine Dust Sampler, Sr.No.2419 (Polltech Make)

Date of Calibration: -07/08/2025 Next Calibration due: -06/08/2026

REMARKS/OBSERVATIONS: -


NAAQS: - National Ambient Air Quality Standards

Limits as per NAAQS Monitoring & Analysis Guidelines Volume-I (2009)

BDL-Below Detectable Level

Verified,
02/03/2026

For HORIZON ANALYTICAL LABORATORY PVT.LTD.



MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER

• Sample will be retained only for 15 days. • Above results indicate to the parameter mentioned only. • Liability limited to the issue of test reports only. • The test report shall not be produced for any legal certainty or advertised without permission of lab.



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS	REPORT NO.	HALPL/LAB/AA/16351
M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/703
	SAMPLING DATE	23&24/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14:2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Air	Horizon Services	Plastic Bottles and Bags	--	Near ETP

RESULTS

SR. NO.	DESCRIPTION	UNIT	RESULTS	NAAQS LIMITS	TEST METHOD REFERENCE
01	Date of Sampling	DD/MM/YY	23&24/02/2026		
02	Test Location		Near ETP		
03	Time of Sampling	Hrs.	11:40		
04	Temperature (Max./Min)	Deg C	34/20		
05	Relative Humidity	% RH	46		
06	Sampling Duration	Hrs	24		
07	Carbon monoxide as CO	mg/m ³	0.097	2.0	IS 5182 (Part 10)
08	Benzene as C ₆ H ₆	µg/m ³	BDL (<4)	05	IS 5182 (Part 11)
09	Benzo (a) Pyrene as Ba(a)P	ng/m ³	BDL (<0.5)	01	IS 5182 (Part 12)
10	Hydrogen Bromide (HBr)	mg/m ³	BDL (<1.32)	N.S.	HALPL/LAB/AA/04:2021

REMARKS/OBSERVATIONS: -

NAAQS: - National Ambient Air Quality Standards

Limits as per NAAQS Monitoring & Analysis Guidelines Volume-I (2009)

BDL-Below Detectable Level

N.S.- Not Specified

Verified
25-03-2026



For HORIZON SERVICES

Manisha Nargolkar
MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	ULR NO.	TC1620826000016352
	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/703
	SAMPLING DATE	24&25/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14:2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Air	Horizon Analytical Laboratory Pvt.Ltd.	Plastic Bottles and Bags	-	Near Boiler

RESULTS

SR. NO.	DESCRIPTION	UNIT	RESULTS	NAAQS LIMITS	TEST METHOD REFERENCE
01	Date of Sampling	DD/MM/YY	24&25/02/2026		
02	Test Location		Near Boiler		
03	Time of Sampling	Hrs.	10:45		
04	Temperature (Max./Min)	Deg C	33/22		
05	Relative Humidity	% RH	50		
06	Sampling Duration	Hrs	24		
07	Respirable Suspended Particulate Matter (PM ₁₀)	µg/m ³	60.83	100	IS 5182(part 23)
08	Fine Particulate Matter (PM _{2.5})	µg/m ³	31.25	60	IS 5182 part 24)
09	Sulphur Dioxide as SO ₂	µg/m ³	15.91	80	IS 5182(part 2): Sec.1
10	Nitrogen Dioxide as NO ₂	µg/m ³	35.01	80	IS 5182(part 6)
11	Ozone as O ₃	µg/m ³	17.09	100	IS 5182(part 9)
12	Ammonia as NH ₃	µg/m ³	BDL (<30)	400	IS 5182(part 25)
13	Lead as Pb	µg/m ³	BDL (<0.05)	1.0	IS 5182 (Part 22)
14	Arsenic as As	ng/m ³	BDL (<3)	06	HALPL/LAB/NABL/AA/22:2021
15	Nickel as Ni	ng/m ³	BDL (<7)	20	IS 5182(part 26)

Equipment Used: - Fine Dust Sampler, Sr.No.2519 (Polltech Make)

Date of Calibration: -07/08/2025 **Next Calibration due:** -06/08/2026

REMARKS/OBSERVATIONS:-

NAAQS: - National Ambient Air Quality Standards

Limits as per NAAQS Monitoring & Analysis Guidelines Volume-I (2009)

BDL-Below Detectable Level

Verified
G23

For HORIZON ANALYTICAL LABORATORY PVT.LTD.



MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER:

- Sample will be retained only for 15 days.
- Above results indicate to the parameters mentioned only.
- Liability limited till issue of test reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.
• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1
HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS	REPORT NO.	HALPL/LAB/AA/16352
M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/703
	SAMPLING DATE	24&25/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14:2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Air	Horizon Services	Plastic Bottles and Bags	--	Near Boiler

RESULTS

SR. NO.	DESCRIPTION	UNIT	RESULTS	NAAQS LIMITS	TEST METHOD REFERENCE
01	Date of Sampling	DD/MM/YY	24&25/02/2026		
02	Test Location		Near Boiler		
03	Time of Sampling	Hrs.	10:45		
04	Temperature (Max./Min)	Deg C	33/22		
05	Relative Humidity	% RH	50		
06	Sampling Duration	Hrs	24		
07	Carbon monoxide as CO	mg/m ³	0.086	2.0	IS 5182 (Part 10)
08	Benzene as C ₆ H ₆	µg/m ³	BDL (<4)	05	IS 5182 (Part 11)
09	Benzo (a) Pyrene as Ba(a)P	ng/m ³	BDL (<0.5)	01	IS 5182 (Part 12)
10	Hydrogen Bromide (HBr)	mg/m ³	BDL (<1.32)	N.S.	HALPL/LAB/AA/04:2021

REMARKS/OBSERVATIONS: -

NAAQS: - National Ambient Air Quality Standards
Limits as per NAAQS Monitoring & Analysis Guidelines Volume-I (2009)
BDL-Below Detectable Level
N.S.- Not Specified

VEER FROTH
22.02.2026



For HORIZON SERVICES

MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	ULR NO.	TC1620826000016353
	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/703
	SAMPLING DATE	24&25/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14:2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Air	Horizon Analytical Laboratory Pvt.Ltd.	Plastic Bottles and Bags	-	Near Pump House

RESULTS

SR. NO.	DESCRIPTION	UNIT	RESULTS	NAAQS LIMITS	TEST METHOD REFERENCE
01	Date of Sampling	DD/MM/YY	24&25/02/2026		
02	Test Location		Near Pump House		
03	Time of Sampling	Hrs.	11:15		
04	Temperature (Max./Min)	De ^o C	33/22		
05	Relative Humidity	% RH	50		
06	Sampling Duration	Hrs	24		
07	Respirable Suspended Particulate Matter (PM ₁₀)	µg/m ³	53.19	100	IS 5182(part 23)
08	Fine Particulate Matter (PM _{2.5})	µg/m ³	26.34	60	IS 5182(part 24)
09	Sulphur Dioxide as SO ₂	µg/m ³	12.10	80	IS 5182(part 2): Sec.1
10	Nitrogen Dioxide as NO ₂	µg/m ³	30.80	80	IS 5182(part 6)
11	Ozone as O ₃	µg/m ³	11.67	100	IS 5182(part 9)
12	Ammonia as NH ₃	µg/m ³	BDL (<30)	400	IS 5182(part 25)
13	Lead as Pb	µg/m ³	BDL (<0.05)	1.0	IS 5182 (Part 22)
14	Arsenic as As	ng/m ³	BDL (<3)	06	HALPL/LAB/NABL/AA/22:2021
15	Nickel as Ni	ng/m ³	BDL (<7)	20	IS 5182(part 26)

Equipment Used: - Fine Dust Sampler, Sr.No.2319 (Politech Make)

Date of Calibration: -07/08/2025 Next Calibration due: -06/08/2026

REMARKS/OBSERVATIONS: -


NAAQS: - National Ambient Air Quality Standards

Limits as per NAAQS Monitoring & Analysis Guidelines Volume-I (2009)

BDL-Below Detectable Level

Verified
B. S. S. S.

For **HORIZON ANALYTICAL LABORATORY PVT.LTD.**



F. MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER:

- Sample will be retained only for 15 days.
- Above results indicate to the parameters mentioned only.
- Liability limited till issue of 7 reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS	REPORT NO.	HALPL/LAB/AA/16353
M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/703
	SAMPLING DATE	24&25/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14:2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Ambient Air	Horizon Services	Plastic Bottles and Bags	--	Near Pump House

RESULTS

SR. NO.	DESCRIPTION	UNIT	RESULTS	NAAQS LIMITS	TEST METHOD REFERENCE
01	Date of Sampling	DD/MM/YY	24&25/02/2026		
02	Test Location		Near Pump House		
03	Time of Sampling	Hrs.	11:15		
04	Temperature (Max./Min)	Deg C	33/22		
05	Relative Humidity	% RH	50		
06	Sampling Duration	Hrs	24		
07	Carbon monoxide as CO	mg/m ³	0.097	2.0	IS 5182 (Part 10)
08	Benzene as C ₆ H ₆	µg/m ³	BDL (<4)	05	IS 5182 (Part 11)
09	Benzo (a) Pyrene as Ba(a)P	ng/m ³	BDL (<0.5)	01	IS 5182 (Part 12)
10	Hydrogen Bromide (HBr)	mg/m ³	BDL (<1.32)	N.S.	HALPL/LAB/AA/04: 2021

REMARKS/OBSERVATIONS: -

NAAQS: - National Ambient Air Quality Standards

Limits as per NAAQS Monitoring & Analysis Guidelines Volume-I (2009)

BDL-Below Detectable Level

N.S.- Not Specified

Verified
025-02-2026

For HORIZON SERVICES



MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS	ULR NO.	TC1620826000016358
M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/703
	SAMPLING DATE	24/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14:2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Stack Emission	Horizon Analytical Laboratory Pvt.Ltd.	Plastic Bottles and Bags	--	DG Set No. 1 1250 KVA S6

RESULTS OF ANALYSIS

SR. NO.	DESCRIPTION	UNIT	RESULT	LIMITS	METHODS USED
01	Date Of Sampling	DD/MM/YY	24/02/2026		
02	Test Location		DG Set No. 1 1250 KVA S6		
03	Time Of Sampling (00.00)	Hrs	15:00		
04	Material Of Stack		MS		
05	Stack Height	Mtr	30		
06	Type Of Fuel Used	--	HSD		
07	Type Of Stack		Round		
08	Flue Gas Temperature	Deg K	398		
09	Differential Pressure	mm WG	4.3		
10	Velocity	m/Sec	8.07		
11	Diameter Of Stack	m	0.4		
12	Stack Area	m ²	0.1256		
13	Gas Volume	Nm ³ /Hr	2731.09		
14	Particulate Matter as PM	mg/Nm ³	23.16	≤30	IS 11255 (Part 1)
15	Sulphur Dioxide as SO ₂	mg/Nm ³	41.58	--	IS 11255 (Part 2)
		Kg/Day	2.73	≤30	--
16	Oxides of Nitrogen (NO _x)	ppm	29.0	N.S.	IS 11255 (Part 7)
17	Carbon Monoxide as CO	ppm	35.0	N.S.	HALPL/LAB/NABL/STK/26:2017
18	Carbon Dioxide as CO ₂	%	5.3	N.S.	HALPL/LAB/NABL/STK/09:2017

Equipment Used: -1) Stack Monitoring Kit, Sr. No. 07/2018 (ETCL model)

Date of Calibration: -07/08/2025 Next Calibration due: - 06/08/2026

REMARKS/OBSERVATIONS: -

N.S.-Not Specified

Verified
C23

For HORIZON ANALYTICAL LABORATORY PVT.LTD.



F. MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER

* Sample will be retained only for 15 days. * Above results indicate to the parameters mentioned only. * Liability limited to issue of 17 reports only.
* The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	ULR NO.	TC1620826000016360
	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/703
	SAMPLING DATE	24/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14:2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Stack Emission	Horizon Analytical Laboratory Pvt.Ltd.	Plastic Bottles and Bags	—	Boiler No. 14643 (B-202)

RESULTS OF ANALYSIS

SR. NO.	DESCRIPTION	UNIT	RESULT	LIMITS	METHODS USED
01	Date Of Sampling	DD/MM/YY	24/02/2026		
02	Test Location		Boiler No. 14643 (B-202)		
03	Time Of Sampling (00.00)	Hrs	14:15		
04	Material Of Stack		MS		
05	Stack Height	Mtr	30		
06	Type Of Fuel Used	—	LSHS		
07	Type Of Stack		Round		
08	Flue Gas Temperature	Deg K	430		
09	Differential Pressure	mm WG	3.1		
10	Velocity	m/Sec	7.12		
11	Diameter Of Stack	m	0.8		
12	Stack Area	m ²	0.5024		
13	Gas Volume	Nm ³ /Hr	8923.80		
14	Particulate Matter as PM	mg/Nm ³	23.19	≤30	IS 11255 (Part 1)
15	Sulphur Dioxide as SO ₂	mg/Nm ³	40.64	—	IS 11255 (Part 2)
		Kg/Day	8.70	10.24	—
16	Oxides of Nitrogen (NO _x)	ppm	93	N.S.	IS 11255 (Part 7)
17	Carbon Monoxide as CO	ppm	90	N.S.	HALPL/LAB/NABL/STK/26:2017
18	Carbon Dioxide as CO ₂	%	7.6	N.S.	HALPL/LAB/NABL/STK/09:2017

Equipment Used: -1) Stack Monitoring Kit, Sr. No. 07/2018 (ETCL model)

Date of Calibration: -07/08/2025 Next Calibration due: - 06/08/2026

REMARKS/OBSERVATIONS: -

N.S.- Not Specified

For HORIZON ANALYTICAL LABORATORY PVT.LTD.

F. MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER

- Sample will be retained only for 15 days.
- Above results indicate to the parameters mentioned only.
- Liability limited till issue of 20 reports only.
- This test report shall not be produced for any legal identity or advertised without permission of lab.



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	REPORT NO.	HALPL/LAB/AA/16360
	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/703
	SAMPLING DATE	24/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14:2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Stack Emission	Horizon Services	Plastic Bottles and Bags	--	Boiler No. 14643 (B-202)

RESULTS OF ANALYSIS

SR. NO.	DESCRIPTION	UNIT	RESULT	LIMITS	METHODS USED
01	Date Of Sampling	DD/MM/YY	24/02/2026		
02	Test Location		Boiler No. 14643 (B-202)		
03	Time Of Sampling (00.00)	Hrs	14:15		
04	Material Of Stack		MS		
05	Stack Height	Mtr	30		
06	Type Of Fuel Used	--	LSHS		
07	Type Of Stack		Round		
08	Flue Gas Temperature	Deg K	430		
09	Differential Pressure	mm WG	3.1		
10	Velocity	M/Sec	7.12		
11	Diameter Of Stack	M	0.8		
12	Stack Area	M ²	0.5024		
13	Gas Volume	Nm ³ /Hr	8923.80		
14	Combustion Efficiency	%	99.88	N.S.	HALPL/LAB/STK/09:2017

REMARKS/OBSERVATIONS: -

N.S.-Not Specified

Verified
8/25/26



For HORIZON SERVICES

F MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	REPORT NO.	HALPL/LAB/AA/16359
	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/703
	SAMPLING DATE	24/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14:2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Stack Emission	Horizon Services	Plastic Bottles and Bags	--	Boiler No. 15715 (B-203)


RESULTS OF ANALYSIS

SR. NO.	DESCRIPTION	UNIT	RESULT	LIMITS	METHODS USED
01	Date Of Sampling	DD/MM/YY	24/02/2026		
02	Test Location		Boiler No. 15715 (B-203)		
03	Time Of Sampling (00.00)	Hrs	15:30		
04	Material Of Stack		MS		
05	Stack Height	Mtr	30		
06	Type Of Fuel Used	--	LSHS		
07	Type Of Stack		Round		
08	Flue Gas Temperature	Deg K	445		
09	Differential Pressure	mm WG	3.0		
10	Velocity	M/Sec	7.12		
11	Diameter Of Stack	M	0.8		
12	Stack Area	M ²	0.5024		
13	Gas Volume	Nm ³ /Hr	8629.46		
14	Combustion Efficiency	%	99.88	N.S.	HALPL/LAB/STK/09:2021

REMARKS/OBSERVATIONS: -

N.S.-Not Specified

Verified
CS 23.03.2026



For HORIZON SERVICES

F MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	ULR NO.	TC1620826000016359
	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/703
	SAMPLING DATE	24/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14:2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
Stack Emission	Horizon Services	Plastic Bottles and Bags	--	Boiler No. 15715 (B-203)

RESULTS OF ANALYSIS

SR. NO.	DESCRIPTION	UNIT	RESULT	LIMITS	METHODS USED
01	Date Of Sampling	DD/MM/YY	24/02/2026		
02	Test Location		Boiler No. 15715 (B-203)		
03	Time Of Sampling (00.00)	Hrs	15:30		
04	Material Of Stack		MS		
05	Stack Height	Mtr	30		
06	Type Of Fuel Used	--	LSHS		
07	Type Of Stack		Round		
08	Flue Gas Temperature	Deg K	445		
09	Differential Pressure	mm WG	3.0		
10	Velocity	m/Sec	7.12		
11	Diameter Of Stack	m	0.8		
12	Stack Area	m ²	0.5024		
13	Gas Volume	Nm ³ /Hr	8629.46		
14	Particulate Matter as PM	mg/Nm ³	24.16	≤30	IS 11255 (Part 1)
15	Sulphur Dioxide as SO ₂	mg/Nm ³	31.82	--	IS 11255 (Part 2)
		Kg/Da	6.59	10.24	--
16	Oxides of Nitrogen (NOx)	ppm	81.0	N.S.	IS 11255 (Part 7)
17	Carbon Monoxide as CO	ppm	88.0	N.S.	HALPL/LAB/NABL/STK/26:2017
18	Carbon Dioxide as CO ₂	%	7.5	N.S.	HALPL/LAB/NABL/STK/09:2017

Equipment Used: -1) Stack Monitoring Kit, Sr. No. 07/2018 (ETCL model)

Date of Calibration: -07/08/2025 **Next Calibration due:** - 06/08/2026

REMARKS/OBSERVATIONS: -

N.S.-Not Specified

For HORIZON ANALYTICAL LABORATORY PVT.LTD.

F. MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER

- Sample will be retained only for 15 days.
- Above results indicate to the parameters mentioned only.
- Liability limited for issue of 18 reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email: kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS	ULR NO.	
M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	REPORT DATE	TC1620826000016366
	LAB REFERENCE NO.	05/03/2026
	SAMPLING DATE	HALPL/LAB/AA/703
	SAMPLE RECEIPT DATE	24/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	--
	SAMPLING REF. / SOP NO.	--
		HALPL/LAB/NABL/DG Noise/01 A:2017

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	NATURE	LOCATION
DG-Noise	Horizon Analytical Laboratory Pvt.Ltd.	--	--	--

RESULTS

SR. NO.	DESCRIPTION	UNIT	READING	STANDARDS
	TEST LOCATION (15:15 Hrs.)			
	DG Set No. 1 1250 KVA S6			
01	D.G. SET (INSIDE ACOUSTIC)	dB(A)	102.1	
02	D.G. SET (0.5 MTR AWAY)	dB(A)	73.0	
03	INSERION LOSS AT 0.5 MTR AWAY FROM ACOUSTIC COVER	dB(A)	29.1	More than 25

Instrument Used: Digital Sound Level Meter (070845)

Make: HTC Instruments

Calibration Date: 12/06/2025 **Next Calibration Due:** 11/06/2026

REMARK/OBSERVATIONS:

*Standards are given as per CPCB notification no. G.S.R. 371(E) dated 17 may 2002.

Verified
18/02/2026

For HORIZON ANALYTICAL LABORATORY PVT.LTD.



MANISHA NARGOLKAR
(AUTHORIZED SIGNATORY)

****End of Test Report****

DISCLAIMER

* Sample will be retained only for 15 days. * Above results indicate to the parameters mentioned only. * Liability limited till result 27 at reports only.
* The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

ANALYSIS REPORT

CLIENT'S NAME & ADDRESS		REPORT NO		
M/s. Cipla Ltd. (Unit -II- D27) MIDC Industrial Area, Kurkumbh, Tal- Daund, Pune, 413802		HALPL/LAB/NABL/F/7.8.2.1		
		REPORT DATE	HALPL/LAB/WA/11917	
		LAB REFERENCE NO	27/11/2025	
		SAMPLING DATE	HALPL/LAB/WA/1053	
		SAMPLE RECIEPT DATE	19/11/2025	
		START DATE OF ANALYSIS	20/11/2025	
		END DATE OF ANALYSIS	20/11/2025	
		SAMPLING REF./SOP NO	26/11/2025	
			HALPL/NABL/QC/03	
DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER & QUANTITY	NATURE	LOCATION
Soil Sample	The Client	Plastic Bag-500 gm	---	---

RESULT OF ANALYSIS

SR. NO	DESCRIPTION	UNIT	RESULT	TEST METHOD REFERENCE
01	pH @ 25 °C	---	7.20	IS 2720 (Part 26)
02	Electric Conductance	µS/cm	730.00	IS 14767
03	Chlorides as Cl	mg/kg	152.40	SOP NO: HALPL / NABL / SOIL/10
04	Total Soluble Sulphates as SO ₄	mg/kg	70.50	IS 2720 (Part 27)
05	Water Content	%	40.00	IS 2720 (Part -2)
06	Water Holding Capacity	%	36.00	SOP NO: HALPL / NABL / SOIL/25
07	Total Organic Matter	%	1.50	IS 2720 (Part 22)
08	Total Nitrogen as N	%	0.189	IS 14684
09	Potassium as K	%	0.00282	IS 9497
10	Sodium as Na	%	0.00256	IS 9497
11	Calcium as Ca	mg/kg	40.50	SOP NO: HALPL / NABL / SOIL/07
12	Exchangeable Magnesium as Mg	mg/kg	56.20	SOP NO: HALPL NABL / SOIL/13
13	Available Phosphorus as P	mg/kg	70.00	SOP NO: HALPL / NABL / SOIL/04
14	Cation Exchange Capacity	meq/100g	25.00	SOP NO: HALPL / NABL / SOIL/09
15	Total Arsenic as As	mg/kg	BDL (<1.0)	SOP NO: HALPL / NABL / SOIL/20
16	Total Copper as Cu	mg/kg	BDL (<10.0)	SOP NO: HALPL / NABL / SOIL/20
17	Total Cobalt as Co	mg/kg	NIL	SOP NO: HALPL / NABL / SOIL/20
18	Total Zinc as Zn	mg/kg	1.60	SOP NO: HALPL / NABL / SOIL/20
19	Total Iron as Fe	mg/kg	2.00	SOP NO: HALPL / NABL / SOIL/20
20	Total Lead as Pb	mg/kg	BDL (<10.0)	SOP NO: HALPL / NABL / SOIL/20
21	Total Manganese as Mn	mg/kg	1.80	SOP NO: HALPL / NABL / SOIL/20
22	Total Chromium as Cr	mg/kg	BDL (<20.0)	SOP NO: HALPL / NABL / SOIL/20



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

23	Hexavalent Chromium as Cr ⁶⁺	mg/kg	NIL	SOP NO: HALPL / NABL/ SOIL/20
24	Total Nickel as Ni	mg/kg	BDL (<10.0)	SOP NO: HALPL / NABL/ SOIL/20
25	Total Molybdenum as Mo	mg/kg	BDL (<10.0)	SOP NO: HALPL / NABL/ SOIL/20
26	Total Mercury as Hg	mg/kg	NIL	SOP NO: HALPL / NABL/ SOIL/20
27	Total Cadmium as Cd	mg/kg	BDL (<20.0)	SOP NO: HALPL / NABL/ SOIL/20
28	Antimony as Sb	mg/kg	NIL	SOP NO: HALPL / NABL/ SOIL/20
29	Available Boron as B	mg/kg	0.74	SOP NO: HALPL/ NABL/ SOIL/01

Very fresh.
23/12/2024



For HORIZON SERVICES


(LAB INCHARGE)

****End of Test Report****



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS	REPORT NO.	HALPL/LAB/AA/16362
M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/703
	SAMPLING DATE	24/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14.2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	TIME OF SAMPLING	LOCATION
Scrubber Monitoring	Horizon Services	Plastic Bottles and Bags	12:50 Hrs.	Scrubber No. 201 (API - 1) S-3

RESULTS

SR. NO	TEST DESCRIPTION	UNIT	RESULTS	MPCB LIMITS	METHOD OF SAMPLING AND ANALYSIS
1.	ACID MIST (HCl)	mg/NM ³	3.98	35	HALPL/LAB/STK/01:2017
2.	DIMETHYL SULPHATE	mg/NM ³	BDL (<5)	—	HALPL/LAB/STK/10:2017
3.	TOTAL VOC	ppm	BDL (<0.26)	—	HALPL/LAB/STK/06:2017
4.	HC	ppm	BDL (<0.26)	—	HALPL/LAB/STK/03:2017
5.	HBr	ppm	BDL (<0.4)	—	HALPL/LAB/STK/03:2017

Equipment Used: -1) Stack Monitoring Kit; Sr. No. 07/2018 (ETCL model)

Date of Calibration: -07/08/2025 **Next Calibration due:** - 06/08/2026

REMARKS/OBSERVATIONS: -

BDL-Below Detectable Level

*Verified,
23.02.26*



For HORIZON SERVICES

MANISHA NARGOLKAR
F MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS	REPORT NO.	HALPL/LAB/AA/16361
M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	REPORT DATE	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/703
	SAMPLING DATE	24/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14:2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	TIME OF SAMPLING	LOCATION
Scrubber Monitoring	Horizon Services	Plastic Bottles and Bags	12:30 Hrs.	Scrubber No. 202 (API - 1) S-4

RESULTS

SR. NO	TEST DESCRIPTION	UNIT	RESULTS	MPCB LIMITS	METHOD OF SAMPLING AND ANALYSIS
1.	ACID MIST (HCl)	mg/NM ³	3.59	35	HALPL/LAB/STK/01:2017
2.	DIMETHYL SULPHATE	mg/NM ³	BDL (<5)	--	HALPL/LAB/STK/10:2017
3.	TOTAL VOC	ppm	BDL (<0.26)	--	HALPL/LAB/STK/06:2017
4.	HC	ppm	BDL (<0.26)	--	
5.	HBr	ppm	BDL (<0.4)	--	

Equipment Used: -1) Stack Monitoring Kit, Sr. No. 07/2018 (ETCL model)

Date of Calibration: -07/08/2025 Next Calibration due: - 06/08/2026

REMARKS/OBSERVATIONS: -

BDL-Below Detectable Level

Verified
24-03-2026



For HORIZON SERVICES

F MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

Page 1 of 1

HALPL/LAB/NABL/F/7.8.2.1

CLIENT'S NAME & ADDRESS	REPORT NO.	REPORT DATE
M/s. Cipla Limited (Unit - II) Plot No. D - 27, MIDC Kurkumbh Tal- Daund, Dist- Pune	HALPL/LAB/AA/16363	05/03/2026
	LAB REFERENCE NO.	HALPL/LAB/AA/703
	SAMPLING DATE	25/02/2026
	SAMPLE RECEIPT DATE	27/02/2026
	START DATE OF ANALYSIS	27/02/2026
	END DATE OF ANALYSIS	04/03/2026
	SAMPLING REF. / SOP NO.	HALPL/LAB/NABL/SAM/14:2021

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER	TIME OF SAMPLING	LOCATION
Scrubber Monitoring	Horizon Services	Plastic Bottles and Bags	10:00 Hrs.	Scrubber No. 401 (API - 2) S-5

RESULTS

SR. NO	TEST DESCRIPTION	UNIT	RESULTS	MPCB LIMITS	METHOD OF SAMPLING AND ANALYSIS
1.	ACID MIST (HCl)	mg/NM ³	4.98	35	HALPL/LAB/STK/01:2017
2.	DIMETHYL SULPHATE	mg/NM ³	BDL (<5)	--	HALPL/LAB/STK/10:2017
3.	TOTAL VOC	ppm	BDL (<0.26)	--	HALPL/LAB/STK/06:2017
4.	HC	ppm	BDL (<0.26)	--	HALPL/LAB/STK/03:2017
5.	HBr	ppm	BDL (<0.4)	--	

Equipment Used: -1) Stack Monitoring Kit, Sr. No. 07/2018 (ETCL model)

Date of Calibration: -07/08/2025 Next Calibration due: - 06/08/2026

REMARKS/OBSERVATIONS: -

BDL-Below Detectable Level

*10841 Recd.
09/03/2026*



For HORIZON SERVICES

[Signature]
F. MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.
 • Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

CLIENT'S NAME & ADDRESS	ULR NO	HALPL/LAB/NABL/F/7.8.2.1
M/s. Cipla Ltd. (Unit -II- D27) MIDC Industrial Area, Kurkumbh, Tal- Daund, Pune, 413802	REPORT DATE	TC1620826000016346
	LAB REFERENCE NO.	04/03/2026
	SAMPLING DATE	HALPL/LAB/WA/1500
	SAMPLING TIME	---
	CUSTOMER REF. DOCUMENT	---
	SAMPLE RECEIPT DATE	Yearly Contract
	DATE OF SAMPLE ANALYSIS	26/02/2026
	SAMPLING REF. / SOP NO.	26/02/2026 to 03/03/2026
	ENVIRONMENTAL CONDITION WHILE TESTING	---
		Ambient Temp.27.9 °C & Humidity 31 %

DETAILS OF SAMPLE	SAMPLING & TRANSPORTATION DONE BY	SAMPLE CONTAINER QUANTITY & CONDITION	NATURE	LOCATION/ IDENTIFICATION
Wastewater Sample	The Client	Plastic Bottle-1000ml- Sealed	Treated	RO Permeate

RESULTS OF ANALYSIS

SR. NO.	DESCRIPTION	UNIT	RESULT	TEST METHOD REFERENCE
01	pH	---	7.48	APHA 24 th Ed 2023, 4500-H ⁺ B
02	Total Suspended Solids	mg/L	BDL (<4.0)	APHA 24 th Ed. 2023, 2540-D
03	Total Dissolved Solids	mg/L	118.00	APHA 24 th Ed. 2023, 2540 C
04	Chemical Oxygen Demand	mg/L	26.00	APHA 24 th Ed. 2023, 5220- C
05	Biochemical Oxygen Demand for 3 days at 27° C	mg/L	7.00	IS, 3025 (P 44)
06	Chlorides as Cl ⁻	mg/L	22.50	APHA 24 th Ed 2023, 4500 ClB
07	Sulphates as SO ₄	mg/L	12.15	APHA 24 th Ed 2023, 4500 SO ₄ E
08	Oil & Grease	mg/L	BDL (<2.0)	APHA 24 th Ed 2023, 5520 B
09	Phosphorus as P	mg/L	BDL (<0.05)	APHA 24 th Ed 2023, 4500- P D
10	Ammonical Nitrogen as NH ₃ -N	mg/L	0.60	APHA 24 th Ed 2023, 4500 NH ₃ B/C/F
11	Copper as Cu	mg/L	BDL (<0.1)	APHA 24 th Ed 2023, 3111 B
12	Zinc as Zn	mg/L	BDL (<0.1)	APHA 24 th Ed 2023, 3111 B
13	Lead as Pb	mg/L	BDL (<0.1)	APHA 24 th Ed 2023, 3111 B
14	Hexavalent Chromium as Cr ⁺⁶	mg/L	BDL (<0.05)	APHA 24 th Ed 2023, 3500 Cr B
15	Total Chromium as Cr	mg/L	BDL (<0.1)	APHA 24 th Ed 2023, 3111 B
16	Mercury as Hg	mg/L	BDL (<0.01)	APHA 24 th Ed 2023, 3112 B
17	Arsenic as As	mg/L	BDL (<0.005)	APHA 24 th Ed 2023, 3214 B
18	Sulphide as S ²⁻	mg/L	BDL (<0.5)	APHA 24 th Ed 2023, 4500-S ²⁻ F

DISCLAIMER

• Sample will be retained only for 15 days • Above results indicate to the parameters mentioned only • Liability limited till issue of test reports only
 • The test report shall not be produced for any legal identity or advertisement without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004
• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

19	Phenolic Compounds as C_6H_5OH	mg/L	BDL (<0.5)	APHA 24 th Ed 2023, 5530 D
20	Sodium Absorption Ratio	---	0.10	SOP No.: HALPL/NABL/WA/27
21	Silica as SiO_2	mg/L	BDL (<1.0)	APHA 24 th Ed 2023, 4500 SiO_2 C
22	Total Hardness as $CaCO_3$	mg/L	32.00	APHA 24 th Ed 2023, 2340 C

NOTE: BDL: Below Detectable Level

Verified.
(23.03.2026)

For HORIZON ANALYTICAL LABORATORY PVT. LTD




F MANISHA NARGOLKAR
(AUTHORISED SIGNATORY)

The effect of results relate
only to the item tested

Sampling Date: 26/02/2026

****End of Test Report****

DISCLAIMER

- Sample will be retained only for 15 days.
- Above results indicate to the parameters mentioned only.
- Liability limited to issue of test reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab Approved by MoEF, New Delhi. (Valid till 06/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

ANALYSIS REPORT

HALPL/LAB/NABL/F/7.8.2.1

HALPL/LAB/NABL/F/7.8.2.1


CLIENT'S NAME & ADDRESS	REPORT NO	HALPL/LAB/WA/16346
M/s. Cipla Ltd. (Unit -II- D27) MIDC Industrial Area, Kurkumbh, Tal- Daund, Pune, 413802	REPORT DATE	04/03/2026
	LAB REFERENCE NO	HALPL/LAB/WA/1500
	SAMPLING DATE	26/02/2026
	SAMPLE RECIEPT DATE	26/02/2026
	START DATE OF ANALYSIS	26/02/2026
	END DATE OF ANALYSIS	03/03/2026
	SAMPLING REF./SOP NO	HALPL/NABL/QC/02

DETAILS OF SAMPLE	SAMPLING DONE BY	SAMPLE CONTAINER & QUANTITY	NATURE	LOCATION
Wastewater Sample	The Client	Plastic Bottle-1000ml	Treated	RO Permeate

RESULTS OF ANALYSIS

SR. NO.	DESCRIPTION	UNIT	RESULT	TEST METHOD REFERENCE
01	Cyanide as CN	mg/L	NIL	APHA 24 th Ed 2023, 4500- Cn E
02	Benzene	µg/ml	BDL (<100.0)	APHA 24 th Ed 2023, 6200 C
03	Xylene	µg/ml	BDL (<100.0)	APHA 24 th Ed 2023, 6200 C
04	Methylene Chloride	µg/ml	BDL (<100.0)	APHA 24 th Ed 2023, 6200 C
05	Chlorobenzene	µg/ml	BDL (<100.0)	APHA 24 th Ed 2023, 6200 C
06	Bio-Assay test (Survival of fish upto 96 hours)	%	92.00	IS 6582 (Part 1): 1971

Verified,
26-02-2026



For HORIZON SERVICES

F MANISHA NARGOLKAR
(Lab Incharge)

****End of Test Report****



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email: kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

CLIENT'S NAME & ADDRESS		ULR NO	HALPL/LAB/NABL/F/7.8.2.1
M/s. Cipla Ltd. (Unit -II- D27) MIDC Industrial Area, Kurkumbh, Tal- Daund, Pune, 413802		REPORT DATE	TC1620826000016345
		LAB REFERENCE NO.	04/03/2026
		SAMPLING DATE	HALPL/LAB/WA/1500
		SAMPLING TIME	---
		CUSTOMER REF. DOCUMENT	---
		SAMPLE RECEIPT DATE	Yearly Contract
		DATE OF SAMPLE ANALYSIS	26/02/2026
		SAMPLING REF. / SOP NO.	26/02/2026 to 03/03/2026
		ENVIRONMENTAL CONDITION WHILE TESTING	---
			Ambient Temp. 27.9 °C & Humidity 31 %

DETAILS OF SAMPLE	SAMPLING & TRANSPORTATION DONE BY	SAMPLE CONTAINER QUANTITY & CONDITION	NATURE	LOCATION/ IDENTIFICATION
Domestic Wastewater Sample	The Client	Plastic Bottle-1000ml- Sealed	Treated	STP

RESULTS OF ANALYSIS

SR. NO.	DESCRIPTION	UNIT	RESULT	MPCB LIMITS	TEST METHOD REFERENCE
01	Total Suspended Solids	mg/L	6.00	<50.0	APHA 24 th Ed. 2023, 2540-D
02	Chemical Oxygen Demand	mg/L	17.20	<100.0	APHA 24 th Ed. 2023, 5220- C
03	Biochemical Oxygen Demand for 3 days at 27° C	mg/L	6.10	< 30.0	IS, 3025 (P 44)

Verified

25.03.2026



For HORIZON ANALYTICAL LABORATORY PVT. LTD

F MANISHA NARGOLKAR
(AUTHORISED SIGNATORY)

****End of Test Report****

The effect of results relate
only to the item tested

Sampling Date..26.02.2026

DISCLAIMER

- Sample will be retained only for 15 days.
- Above results indicate to the parameters mentioned only.
- Liability limited to issue of test reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab.



Lab NABL Accredited - Chemical Field, (Valid till 18/03/2026)

"Shree", K 3/4, S. No. 10, Erandawane Housing Society, Opposite Deenanath Mangeshkar Hospital, Pune 411 004.

• Mob.: 7249867318, 8378018710 • Email : kmn@hespl.co.in / md@hespl.co.in • www.hespl.co.in

TEST REPORT

HALPL/LAB/NABL/F/7.8.2.1


CLIENT'S NAME & ADDRESS	ULR NO	TC1620826000016344
M/s. Cipla Ltd. (Unit -II- D27) MIDC Industrial Area, Kurkumbh, Tal- Daund, Pune, 413802	REPORT DATE	04/03/2026
	LAB REFERENCE NO.	HALPL/LAB/WA/1500
	SAMPLING DATE	---
	SAMPLING TIME	---
	CUSTOMER REF. DOCUMENT	Yearly Contract
	SAMPLE RECEIPT DATE	26/02/2026
	DATE OF SAMPLE ANALYSIS	26/02/2026 to 03/03/2026
	SAMPLING REF. / SOP NO.	---
	ENVIRONMENTAL CONDITION WHILE TESTING	Ambient Temp. 27.9 °C & Humidity 31 %

DETAILS OF SAMPLE	SAMPLING & TRANSPORTATION DONE BY	SAMPLE CONTAINER QUANTITY & CONDITION	NATURE	LOCATION/ IDENTIFICATION
Wastewater Sample	The Client	Plastic Bottle-1000ml- Sealed	Untreated	ETP

RESULTS OF ANALYSIS

SR. NO.	DESCRIPTION	UNIT	RESULT	TEST METHOD REFERENCE
01	pH	---	7.76	APHA 24 th Ed 2023, 4500-H*B
02	Total Suspended Solids	mg/L	104.00	APHA 24 th Ed. 2023, 2540-D
03	Total Dissolved Solids	mg/L	920.00	APHA 24 th Ed. 2023, 2540 C
04	Chemical Oxygen Demand	mg/L	5567.20	APHA 24 th Ed. 2023, 5220 C
05	Biochemical Oxygen Demand for 3 days at 27° C	mg/L	2884.60	IS 3025 (P 44)
06	Chlorides as Cl ⁻	mg/L	136.75	APHA 24 th Ed 2023, 4500 Cl-B
07	Sulphates as SO ₄	mg/L	110.00	APHA 24 th Ed 2023, 4500 SO ₄ E
08	Oil & Grease	mg/L	BDL (<2.0)	APHA 24 th Ed 2023, 5520 B
09	Phosphorus as P	mg/L	10.00	APHA 24 th Ed 2023, 4500- P D
10	Sulphide as S ²⁻	mg/L	3.50	APHA 24 th Ed 2023, 4500-S ² -F
11	Phenolic Compounds as C ₆ H ₅ OH	mg/L	1.20	APHA 24 th Ed 2023, 5530 D
12	Total Chromium as Cr	mg/L	0.18	APHA 24 th Ed 2023 3111 B

For HORIZON ANALYTICAL LABORATORY PVT. LTD



MANISHA NARGOLKAR
(AUTHORISED SIGNATORY)

****End of Test Report****

Verified
23.03.2026

The effect of results relate
only to the item tested

Sampling Date: 26/02/2026

DISCLAIMER:

- Sample will be retained only for 15 days. • Above results indicate to the parameters mentioned only. • Liability limited till issue of test reports only.
- The test report shall not be produced for any legal identity or advertised without permission of lab.

ANNEXURE - II

CER Expenditure & Implementation Plan

No.	CER Activity Details	Amount	Expenditure in Rs. Lakhs		
			Yr. 2024	Yr. 2025	Yr. 2026
1.	Installing & Commissioning Solar Photovoltaic Energy Generation Systems on Roof Tops/ in Premises of Z.P. School & PHC in Study Area: 2 Systems X 5 KW X Rs. 1 Lakh/KW = Rs.10 Lakh	Rs. 10 Lakhs	5	5	--
2.	Provision of Solar Street Lights with gadget comprising of - 1 MS Pole, 18-20 W LED Lamp, Battery, Solar Panel, Wiring in 3 Villages. 3 Villages X 10 Solar Street Lights X Rs.30,000/-= Rs.9 Lakhs	Rs. 9 Lakhs	3	3	3
	TOTAL	Rs. 19 Lakhs	8	8	3

 महाराष्ट्र शासन जिल्हा नियोजन समिती जिल्हाधिकारी कार्यालय, पुणे	 जिल्हाधिकारी कार्यालय, पुणे
दूरध्वनी क्र.: 020-26121012	ई-मेल: dpopune85@gmail.com
जा.क्र.जिनिसपु/नि-४/ CRE/ २०२५	

आदेश

विषय :- Corporate Environment Responsibility (CER) अंतर्गत करण्यात येणाऱ्या कामांना मान्यता देणेबाबत....

संदर्भ: १. मा. जिल्हाधिकारी पुणे यांचे अध्यक्षतेखाली दि. २८/०८/२०२३ रोजीचे इतिवृत्त

२. Letter From Cipla Foundation Dated No.CIPLA/EHS-ENV/09/2024, Dt.26.11.2024

३. Jaison Jacob Banglavil, Cipla Foundation यांचा दि.१४/१२/२०२४ चा ई-मेल संदेश

उपरोक्त संदर्भ क्र.२ चे पत्रान्वये, Jaison Jacob Banglavil, Cipla Foundation यांनी Corporate Environment Responsibility (CER) अंतर्गत करावयाच्या कामांचा प्रस्ताव या कार्यालयास प्राप्त झालेला आहे. पर्यावरण, वन एवं जल वायू परिवर्तन मंत्रालय, नवी दिल्ली यांचे परिपत्रक दि.०६/०५/२०१८ नुसार स्थानिक गरजेनुसार नवीन कामे व अस्तित्वातील कामांमध्ये बदल करण्याचे अधिकार जिल्हाधिकारी यांना देण्यात आले आहेत.

त्यास अधिन राहून खालीलप्रमाणे कामास मान्यता देण्यात येत आहे.

Details are as follows:

No.	Interventions (Activities)	Intervention details	Quantity	Locations	Revised budget (Rs. In Lakhs)	Remarks from DC office
1	Technical, socio-economic, geohydrological survey, net planning water quality assessment: survey				1.00	
2	Soil and Water conservation measures	Area Treatment	335 Ha.		285.00	
		Desiltation of Water Resources Structure (Check Dam and NDW)	50 Nos.	Grampanchayat Pandharewadi, Girim, Jiregaon (Taluka Daund)		
		Repairing of Check dam	12 Nos.	Pandharewadi, Jiregaon & Girim		
3	Climate resilient agriculture practices	Soil Testing, Advisory and awareness, etc.	300 farmers		121.00	
		Water Footprint interventions (Drip irrigation, sprinklers)	50 revised to 300 farmers			
		Vegetable Model (Mulching, Organic Manure, Bio-Pesticide, etc.)	100 revised to 300 farmers			
4	Mobile Health Unit	Mobile Vans across villages	10,000 medical consultations	Rs.35 L per year X 2 years	70.00	Please submit proposal after consultation with District Health Officer. Amount

			per year	16 villages located near Kurkumbh MIDC		allotted for the same is huge. State Govt giving free of cost medicine to all the citizens. So cost of medicine can be utilised to some other area. Response: Cipla Foundation has been running Mobile Health vans since 2018 providing medical consultations by doctor and free medicines. This initiative have been supportive for the villagers has medical services are provided at their village level and home visits for old age population.
5	Mobile Science Lab	Science labs van across govt. schools	10,000 classroom exposure for students	Rs.17 L per year x 2 years 20 Schools located near Kurkumbh MIDC Prefer by ZP School	35.00	
6	Education Scholarships or Educational related support to schools or students	Scholarships or education related support to students from government	250+ students	Z.P. & Government Schools located in Daund Taluka	38.00	Please add only government schools only. Zilla Parishad School in nearby area.
7	Local Health Centres based on need of PHCs	Medical equipment, solar equipments, etc. to support the health centres	3 PHC's	PHC Kurkumbh, PHC Rawangaon and PHC Warvand,	20.00	We allotted enough fund to PHC equipment. Instead of that Some capital generation activity must be included in the project. Response: Basis need of the PHCs, we would plan. Nearby PHCs have requested some medical equipments which can be supported under the project.
8	Capacity building & exposure visits (farmers & staff)	Training and exposure visits for the famers and team on various interventions to undertaken in the project.	Interested Village farmers		12.00	
9	Review, Monitoring, Facilitation, Documentation and Communication	M&E on the project interventions and documentation for records			8.00	
10	Equipment (Survey, IT enabled, GPS, Desktop, laptop, printer etc.), Office setup and	Capital expenditure for project activities			5.00	

	office expenses					
11	Health & Sanitation	Public restroom near "Firangai Mata" Temple in Kurkumbh (will explore partnership with "Sulabh" for cleanliness and maintenance of community sanitation block)	4+4 Toilets (Male/Female)	Execute by M. Sulabh International Organization Mumbai	31.00	Please tie up with NGO/Institute like Sulabh international for construction and maintenance for Sanitation facilities . only construction not solving the issue. (Added the maintenance cost – Rs.25,000 per month X 2 years = 6 L)
13	Introduction Renewable Energy	Solar power system (only for BPL family and utilization done on actual basis. Budget mentioned is Indicative)	30 Households		26.00	Please get approved list from Block Development Officer, Daund .
14	Cancer screening camps	Camps to be organized in Pune rural. Engagement and proposal to be sought for Pune hospital		Ambewadi & Daund Taluka DHO,CS	25.00	Please increase the amount and area for the Cancer Screening.
15	Salary and associated costs for project team	(Project leader, Engineer, Agriculture expert, Social Expert, Supervisors, Accounts, Honorarium, etc.)			59.00	Management and Salary cost of project team is 15.90 % of project cost also in + Miscellaneous activities 17.00 lakh amount is added. Need to reduce this cost to give more funds availability to actual purpose.
16	Management cost (8% on activity cost)	(to be discussed with PIA)			54.00	
				Total	790.00	
				+ Miscellaneous activities	0.00	
				Grand Total	790.00	

तसेच वरील प्रस्तावित कामांचे सनियंत्रण व अभिलेख हे उपसंचालक, माध्यमिक शिक्षण विभाग पुणे, जिल्हा आरोग्य अधिकारी, जि.प.पुणे , जिल्हा शल्य चिकित्सक, पुणे व मे.सुलभ इंटरनॅशनल ऑर्गनायझेशन मुंबई यांनी ठेवावयाचे असून त्याबाबतचा अहवाल यथावकाश जिल्हाधिकारी पुणे यांचेकडे सादर करावयाचा आहे.

Signed by
Jitendra Dudi
(जितेंद्र दूडि)
जिल्हाधिकारी, पुणे
Date: 24/03/2025 14:21:11

प्रति :- मुख्य कार्यकारी अधिकारी, जिल्हा परिषद, पुणे

प्रत:- १. उपसंचालक, माध्यमिक शिक्षण विभाग, पुणे विभाग, पुणे

२. जिल्हा आरोग्य अधिकारी, जि.प.पुणे

३. जिल्हा शल्य चिकित्सक, पुणे

४. मे.सुलभ इंटरनॅशनल ऑर्गनायझेशन मुंबई

५. कार्यकारी संचालक, भीमशंकर सहकारी साखर कारखाना लि, दत्तात्रयनगर, पारंगव तर्फे अवसरो बु., ता. आंबेगाव, जि.पुणे

Project : Water & environment sustainability
Implementing Partner - BAIF Institute for Sustainable Livelihoods and Development (BAIF Livelihoods)



Gabion structure



Gabion structure



Loose boulder structure



Farmers trainings



Recharge farm pond



Desiltation of ENB

STANDING STRONG • *Caring for life* •

Project : Water & environment sustainability

Implementing Partner - BAIF Institute for Sustainable Livelihoods and Development (BAIF Livelihoods)



Support for Solar Insect Traps

Support for bio-fertilizer



Exposure visit



Drip irrigation



Mulching Farming

Project : Water & environment sustainability

Implementing Partner - BAIF Institute for Sustainable Livelihoods and Development (BAIF Livelihoods)



Solar roof top system



Visit to Baramati Krishi Mahotsav (Agriculture exhibition)

Project : Mobile Healthcare Unit
Implementing Partner – HelpAge India



Mobile Healthcare Unit



Specialize health camp at village Girim

Project : Mobile Science Lab
Implementing Partner – Agastya International Foundation



Employee volunteering event



Hands on Science classroom session

[illegible]

E

PURCHASE ORDER

Cipla

Purchase Order No: 4520041624 Date: 30.11.2022	Delivery Address (Ship to): CIPLA/KKB-II/API/EOU EOU D-27, MIDC Industrial Area, Kurkumbh, Tal. Daund, Pune Daund Maharashtra -413802 State code : State Name : GSTIN/Unique : 27AAACC1450B1ZE ISD GSTIN : IEC number : PAN no : AAACC1450B	Buyer (Bill To): CIPLA LIMITED D-27,MIDC INDUSTRIAL AREA,KURKUMBH,TAL. DAUND,PUNE,-413802 State code : 27 State Name : Maharashtra GSTIN/Unique : 27AAACC1450B1ZE ISD GSTIN : Drug lic no : PAN no : AAACC1450B IEC number :
Vendor Code : 100082176 Name : Lombardyne Industries Address : 123, Sub Plot 15, Nr Opp Jaws Mfg Comp, Ramtekdi Industrial Estate, Hadapsar, Pune Pune 411028 Maharashtra Vendor Reference : Ms. Bharati GSTIN/Unique ID : 27ABQPL1208E3ZS Vendor References : Registered		

Excise Invoice should be in the Name of CIPLA LTD KURKUMBH(API/EOU)D27 A/C CIPLA Ltd.
Invoice to be sent : SCANNING CELL, CIPLA LTD, SB -901,902,9TH FLOOR,EMPIRE TOWER,RELIABLE TECH PARK,OFF THANE BELAPUR ROAD,AIROLI, NAVI MUMBAI - 400708
Helpline for payment queries- visit our vendor portal <https://vss.cipla.com/> and for further queries write to Payables. Heldpesk@cipla.com
For Goods Receipt and Service confirmation Please send delivery challan, transport invoice copy,e way bill,measurement sheet and other documents required for Goods Receipt / Service Confirmation to the unit /location where the goods are being delivered or service rendered.

For any change notification please share mail communication on id- Change.notification@cipla.com
We are pleased to place our purchase order for the supply of the items described below. This Purchase Order is governed by the Terms & Conditions attached.

Delivery Terms: Free delivery within 6 months upto site from the date of receipt of advance (1 Month considered for release of advance). Penalty.

SN	Material Code	Material Description	Qty	Unit	Unit Price	Net Item Value
10		Supply of Vacuum Evaporator unit	1.000	No	10,133,525.00	10,133,525.00 INR

HSN/SAC/UQC :- 84198990

& Inbuilt concentrator unit. System suitable for 2000 LPH effluent intake flow rate,
 MOC of SS316L & Heat Exchanger SS316Ti, Working Hours: 20 with include
 Transportation charges

CER No. : CKUEB21E4

Delivery Date : 11.07.2023

Input:GST Credit

SGST @ 9%: 912,017.25
 CGST @ 9% : 912,017.25
 Tax value :1,824,034.50
 Net Rate : 11,957,559.50
 Total Value : 11,957,559.50

20		Supply of Feed tank 4000 Liters,	1.000	No	150,000.00	150,000.00 INR
----	--	----------------------------------	-------	----	------------	----------------

HSN/SAC/UQC :- 84198990

MOC SS304

CER No. : CKUEB21E4

Delivery Date : 11.07.2023

Input:GST Credit

SGST @ 9%: 13,500.00
 CGST @ 9% : 13,500.00
 Tax value :27,000.00
 Net Rate : 177,000.00
 Total Value : 177,000.00

Purchase Order No:4520041624 Date: 30.11.2022

30	Supply of Additional Requirement :	4.000 NOS	471,500.00	1,886,000.00 INR
HSN/SAC/UQC :- 84198990				SGST @ 9%: 169,740.00
Feed pump, Condensate pump, Concentrate pump - KSB & Vacuum pump - Atlas Copco				CGST @ 9% : 169,740.00
(As per your quotation no:- LI/1128/2022-23 & Dtd:- 01/04/2022 / E-mail Dtd:- 30/11/2022)				Tax value :339,480.00
CER No. : CKUEB21E4				Net Rate : 556,370.00
Delivery Date : 11.07.2023				Total Value : 2,225,480.00
Input:GST Credit				

Gross Total Value : 14,360,039.50 INR

Terms of Payment : - 40% Advance with PO without GST


- 40% against inspection and before dispatch of material
- 100% GST tax amount after submission of invoice and receiving of material at site within 15 days
- 10% against commissioning
- 10% PBG.

Header Note : CER NO. CKUEB21E4

As per below Terms & Conditions


1. Kindly acknowledge the receipt of this PO.
2. Please Mention the P O Number on the challan as well as on the invoice.
3. Kindly mention the accounting location GST registration numbers (Receiving state Registration number) on the invoice/bills.
4. ''All Govt. Registration No's Including PAN NO to be mentioned on Invoices & Challans before Submitting to Accounts Department''.
5. please send soft copy of invoices to email ID - Cipla.Invoices@cipla.com & sulochana.talashilkar@cipla.com Also send hard copies to Vikhroli address.
6. In case the invoices is digitally signed then the same need to be sent

ANNEXURE- VI RWH System

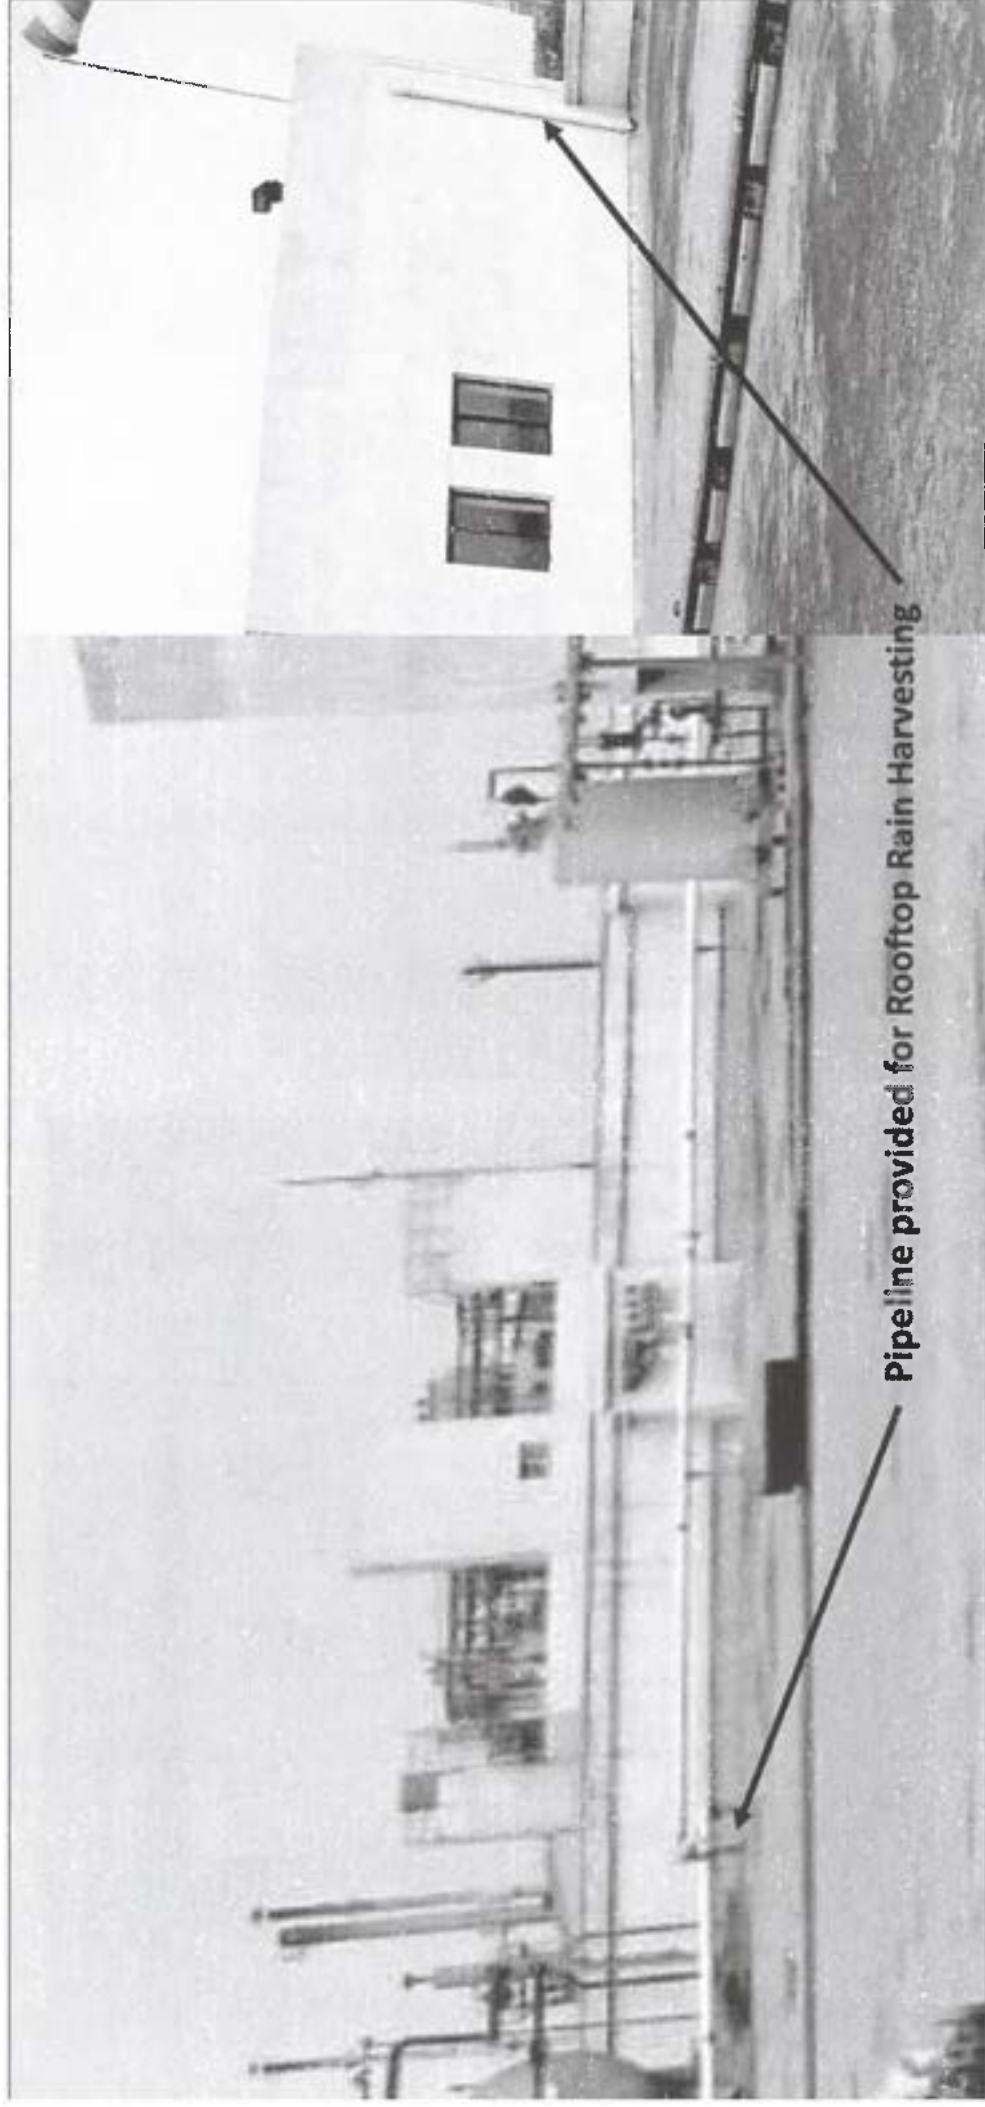




**Pipeline provided for Rooftop
Rain Harvesting**

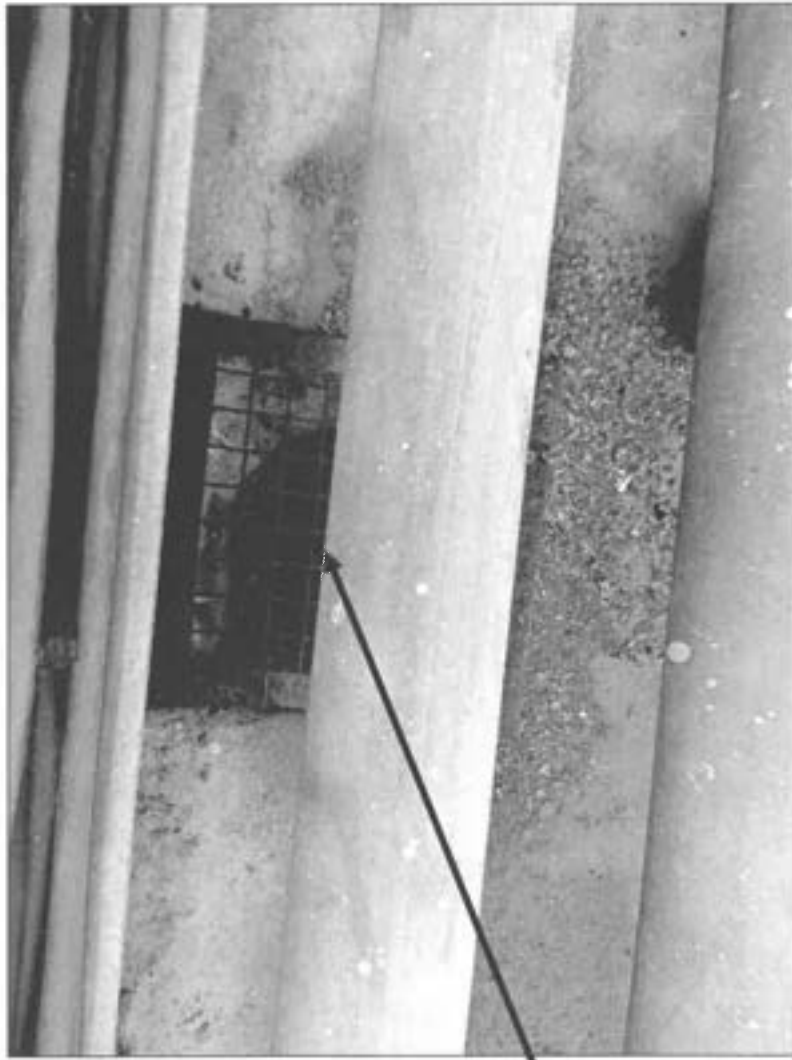

Photographs of Sliding Gate & Turning
Radius provided in the industry premises

ANNEXURE - VII

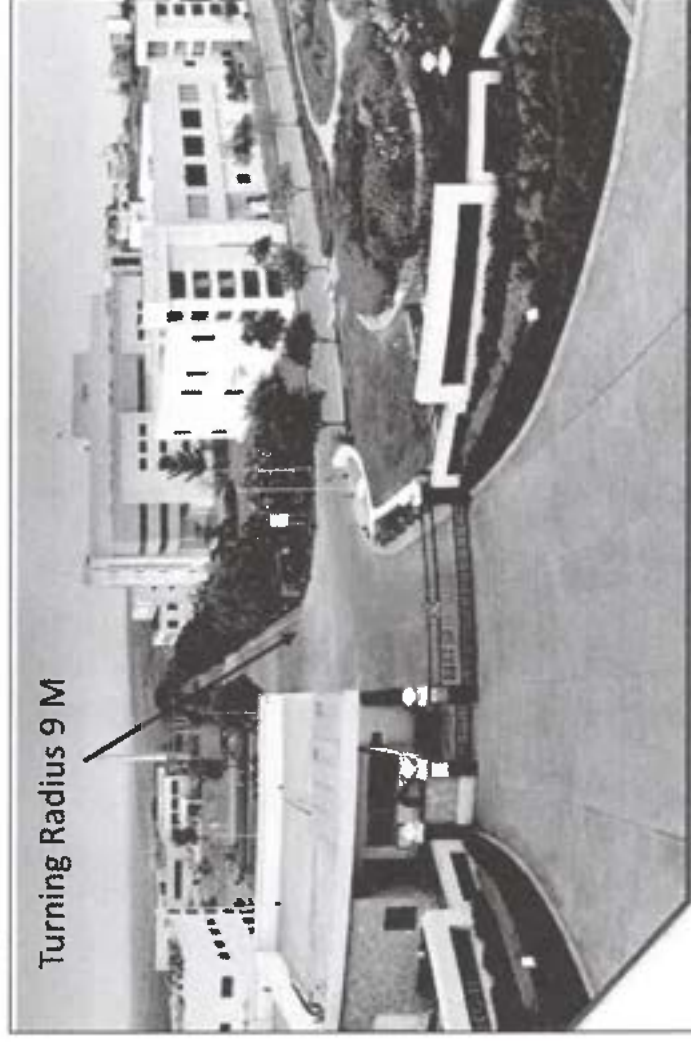

Annexure-VII

Green belt development Miyawaki plantation at Roti



Doc No.: SMS/MEPL/IMS/MKT/PMC
Issue/Rev. No.: 04/00
Rev. Date: 01.02.2020


MAHARASHTRA
ENVIRO POWER LTD

This is to certify that: **M/S. CIPLA LTD.**
Address: UNIT-II, D-27 MIDC Kurkumbh, Tal.-Daund, Dist-Pune
413802 413802 a Valid member of CHWTSDF (As per MOU with MIDC &
MPCB), at Plot No. P-56, Ranjangaon MIDC, Taluka - Shirur, Pune - 412
220.

Membership No. : MEPL/33003270

Membership Period: 02 May 2023 to 01 May 2028

For Maharashtra Enviro Power Ltd.


Authorized signatory


Marketing Coordinator



CHWTSDF : Plot No. P-56, Ranjangaon, Tal. Shirur, Dist. Pune. Pin - 412220. Ph - 401 - 00048421125

Pune Office : 101, Indraprastha, 1st Floor, Marolund, Goregaon, Maharashtra
Pune 411 004. Maharashtra. Ph - 401 - 00048421125
Email : info@mahenviro.com Web : www.mahenviro.com www.environmentalindia.com
Road Office : 101, Indraprastha, 1st Floor, Marolund, Goregaon, Maharashtra
Chandrapur Office : 101, Indraprastha, 1st Floor, Marolund, Goregaon, Maharashtra

Marketing Office : 101, Indraprastha, 1st Floor, Marolund, Goregaon, Maharashtra
Mumbai Office : 101, Indraprastha, 1st Floor, Marolund, Goregaon, Maharashtra
Corporate Office : 101, Indraprastha, 1st Floor, Marolund, Goregaon, Maharashtra
Ph - 401 - 00048421125 Telex - 401 - 00048421125 Web : www.mahenviro.com



भारत सरकार

Government of India

वाणिज्य और उद्योग मंत्रालय

Ministry of Commerce & Industry

पेट्रोलियम तथा विस्फोटक सुरक्षा संगठन (पैसो)

Petroleum & Explosives Safety Organisation (PESO)

E-mail : jtcemumbai@explosives.gov.in

Phone/Fax No : 022 - 27575946, 27573881

संख्या /No. P/HQ/MH/15/5768 (P182874)

दिनांक /Dated : 05/12/2017

सेवा में /To

✓
M/s. Cipla Limited,
Plot No. D-27, M.I.D.C. Industrial Area,
Kurkumbh,
Distt. Pune - 413 802,
District: PUNE,
State: Maharashtra
PIN: 413802

विषय /Sub Plot No. Unit no. II, Plot No. D-27, M.I.D.C. Industrial Area, NA, Kurkumbh, Tehsil Daund, District: PUNE, State: Maharashtra, PIN: 999999 में स्थित विद्यमान पेट्रोलियम वर्ग A,B,C अविष्ठापन में अनुमति सं P/HQ/MH/15/5768 (P182874) के नवीकरण के संदर्भ में ।
Existing Petroleum Class A,B,C Installation at Plot No. Unit no. II, Plot No. D-27, M.I.D.C. Industrial Area, NA, Kurkumbh, Tehsil Daund, District: PUNE, State: Maharashtra, PIN: 999999 - Licence No. P/HQ/MH/15/5768 (P182874) - Renewal regarding.

सहायक /Sir
(s).

कृपया आपके पत्र क्रमांक - दिनांक 27/11/2017 का अवलोकन करें ।
Please refer to your letter No. , dated 27/11/2017

अनुमति संख्या P/HQ/MH/15/5768 (P182874) दिनांक 05/02/2015 को दिनांक 31/12/2027 तक नवीनीकृत कर इस पत्र के साथ अर्पित की जा रही है ।
Licence No. P/HQ/MH/15/5768 (P182874) dated 05/02/2015 is forwarded herewith duly renewed upto 31/12/2027.

कृपया पेट्रोलियम नियम 2002 के अधीन बनाए गए नियम 148 में दी गई प्रक्रिया का कड़ाई से पालन करें । अनुमति के नवीकरण हेतु सम्स्त दस्तावेजों को अनुमति की वैधता समाप्त होने की तिथि से कम से कम 30 दिन पूर्व Jt. Chief Controller of Explosives, West Circle, Mumbai कार्यालय को प्रेषित करें ।

Please follow the procedure strictly as laid down in rule 148 of the Petroleum Rules, 2002 and submit complete documents for the Renewal of the licence to Jt. Chief Controller of Explosives, West Circle, Mumbai, so as to reach his office on or before the date on which Licence expires.

कृपया पावती दें।
Please acknowledge the receipt.

भवदीय /Yours faithfully,

(kanak singh Meena))

Dy. Controller of Explosives
कृते संयुक्त मध्य विस्फोटक नियंत्रक
For Jt. Chief Controller of Explosives
Mumbai

(अधिक जानकारी जैसे आवेदन की स्थिति, शुल्क तथा अन्य विवरण के लिए हमारी वेबसाइट : <http://peso.gov.in> देखें)
(For more information regarding status, fees and other details please visit our website: <http://peso.gov.in>)



ANNEXURE - XI



महाराष्ट्र शासन

औद्योगिक सुरक्षा व आरोग्य संचालनालय (कामगार विभाग)

परवाना क्रं : १०००५७९७

नमूना क्रमांक ४

(नियम ६ व ८ पाहणे)

कारखान्याची नोंदणी व कारखाना चालविण्याचा संबंधीचा परवाना

नोंदणी क्रमांक : ११२१०२१००३००६४८



कारखाने अधिनियम, १९४८ आणि त्यासंबंधी असलेले नियम यांच्या तरतुदीप्रमाणे सिप्ला लिमिटेड यांना खाली वर्णन केलेल्या जागेत कारखाना चालविण्यास परवाना देण्यात आला आहे.

या परवान्यान्वये या जागेत कोणत्याही एका दिवशी ५०० पर्यंत कामगार लावण्यास आणि २००० पेक्षा जास्त अश्वशक्ति उपयोगात आणण्यास परवानगी आहे.

या परवान्याची मुदत ३१ डिसेंबर २०२२ पर्यंत आहे.

Digitally Signed by
Akhil Arun Ghogare
Date: 5/10/2022 7:22:55 AM

परवान्याचे नूतनीकरण १ जानेवारी २०२३ ते ३१ डिसेंबर २०२६ पर्यंत करण्यात आले आहे.
शुल्क रु. - ५७७५०३.६० पोहोचल

दिनांक : १०-०५-२०२२

Signature valid



सह संचालक
औद्योगिक सुरक्षा व आरोग्य,
महाराष्ट्र राज्य, सातारा

परवाना दिलेल्या जागेचे वर्णन

परवाना दिलेल्या कारखान्याचे

सिप्ला लिमिटेड

Factory Name :

Cipla Limited

पत्ता :

सिप्ला लिमिटेड, D-२७, पुणे- सोलापूर हाईवे, कुरकुंभ

एमआईडीसी, कुरकुंभ, दोंड, पुणे, महाराष्ट्र, ४१३८०२

Address :

Cipla Limited, D-27, Pune- Solapur Highway, Kurkumbh
MIDC, Kurkumbh, Daund, Pune, MAHARASHTRA, 413802

कलम :

२(m)(i)

औद्योगिक वर्गीकरण :

२१००३

कारखान्याच्या इमारतीचे नकाशे दिनांक २७.०६.२०२० च्या जावक क्रमांक ११२१००००००२१८५३ खाली मंजूर केले गेले आहेत.

This Certificate is digitally signed by on.

टिप : हा कारखान्याची नोंदणी व कारखाना चालविण्याचा परवाना आहे. हा परवाना देण्यात आल्यामुळे ज्या जागेत हा कारखाना स्थित आहे, त्या जागेस कोणतीही वैधता आपोआप बहाल होत नाही तसेच ज्या जागेत हा कारखाना स्थित आहे ती जागा आज दिनांक वेळेस अस्तित्वात असल्या संबंधात या परवान्यामुळे कोणताही हक्क व स्वामित्व सदरहू भोगवटदारास प्राप्त होत नाही

MOCK DRILL REPORT

Date: 18.02.2026

Time: 11:38 Hrs.

Location: API I RST/MST Area

Scenario: Overflow of RST tank and fire observed in the same area.

Description:

On **February 18, 2026**, Shift Officer **Mr. Manoj Pathare** was performing routine operations on the first floor of the Crystallization Area. At the same time, he was taking a round in the **API-I RST/MST area** for tank level checking. During the inspection, Mr. Manoj observed an **overflow in the RST-204 tank**, so he decided to check the exact cause of the issue.

Meanwhile, Mr. Manoj immediately communicated the situation by calling the **emergency contact number 999**. Simultaneously, he **activated the MCP (Manual Call Point)**. Shortly after, he noticed a fire had started.

The **safety squad members** Mr. Suvasis Mohanty, Satish Kurhekar Mohammad Amir, promptly initiated **foam firefighting** and deployed a **water monitor** to cool the nearby tank. Once the fire was successfully extinguished and all associated risks were eliminated, **Incident Controller Mr. Sunil Appani** control of the situation. **Site Controller Mr. Rohan Parmar** arrived at the Emergency Control Centre and instructed **Communication Officer Mr. Dipak Baravkar** to announce the site evacuation and alert adjacent areas.

All employees, contractors, and visitors gathered at **Assembly Point 2**, where a headcount was conducted by Mr. Dipak Baravkar. After verifying the headcount, the Site Controller declared the site clear and instructed the **Security Officer** to sound the **all-clear siren**.

Following this, the **mock drill scenario** was explained to all participants, and all positive points and findings were discussed thoroughly.

Key Person involved in Mock Drill:

Sr No.	Key Responsibility	Name
01	Site Controller	Mr. Rohan Parmar
02	Incident Controller	Mr. Sunil Appani.
03	Safety Squad Member	Mr. Manoj Pathare, Suvasis Mohanty, Satish Kurhekar Mohammad Amir.
04	Engg.	Mr. Vishal Pharande, Deepak Naik.
05	Safety	Mr. Lalit Pawar/ Mr. Santosh Pagare/Mr. Pravin Kutwal/Ajay Survade/Saurav Patil.

MOCK DRILL REPORT

06	Communication Officer	Mr. Dipak Baravkar.
----	-----------------------	---------------------

Observer for Mock Drill:

Sr. No	Name of Person	Dept for Observations
01	Mr. Ankur Sharma / Dilip Bhagwat	Incident location
02	Mr. Kamlesh Ambulkar	OHC & ECC
03	Mr. Amandeep Singh	Contract Shed
04	Mr. Lalit Pawar	Overall observation
05	Mr. Sunil Baravkar	Infront of API I
06	Mr. Sanjay Mohite	Pump House

Event Summary: -

Time in Hrs.	Action / Event	Action By
11:35	Shift Officer Mr. Manoj Pathare was working on the first floor of the crystallization Area.	Mr. Manoj Pathare.
11:37	At the same time, he was taking a round in the API-I RST/MST area for tank level checking.	Mr. Manoj Pathare.
11:38	During the inspection, Mr. Manoj observed an overflow in the RST-204 tank , so he decided to check the exact cause of the issue.	Mr. Manoj Pathare.
11: 39	Meanwhile, Mr. Manoj immediately communicated the situation by calling the emergency contact number 999	Mr. Manoj Pathare.
11: 40	Simultaneously, he activated the MCP (Manual Call Point) . Shortly after, he noticed a fire had started	Mr. Manoj Pathare.
11:41	The safety squad members Mr. Suvasis Mohanty, Satish Kurhekar Mohammad Amir, promptly initiated foam firefighting and deployed a water monitor to cool the nearby tank	Mr. Suvasis Mohanty, Satish Kurhekar Mohammad Amir,
11:42	Incident Controller Mr. Sunil Appani control of the situation.	Mr. Sunil Appani.

MOCK DRILL REPORT

11:43	Site Controller Mr. Rohan Parmar arrived at the Emergency Control Centre and instructed Communication Officer Mr. Dipak Baravkar to announce the site evacuation and alert adjacent areas.	Mr. Rohan Parmar.
11:45	Safety Squad members ensured the complete evacuation of the block	Mr. Sachin Jadhav/ Siddheshwar Sawant.
11:50	All members reached at assembly point 2	All
11:53	All Clear siren declared Mr. Dipak Baravkar	All
11:55	Details of mock-drill were discussed by the incident controller & Site controller. Mr. Sunil Appani, Rohan Parmar (API Head) & Lalit Pawar (EHS Head) /Ankur Sharma/ Sanjay Mohite/Kamlesh Ambulkar/ Hanmant Shike/Amandeep Singh shared their observations.	All

Head Count at Assembly Point was taken by Security Officer:

Department	Available in Plant	Came to	In Dept. for critical Operations.
	Total	Assembly Point	
API I	20	15 nos.	05
API II	27	24 nos.	03
Store	08	08 nos.	00
QA	18	16 nos.	02
CQA	01	01 nos.	00
QC	25	21 nos.	04
Engg	27	25 nos.	02
EHS	07	07 nos.	00
HR/Admin	02	02 nos.	00
MSTG	03	02 nos.	01
At main Gate	01	00 nos.	01 (Main Gate)

MOCK DRILL REPORT

Unit Head	01	00 nos.	01 (Going for Unit I)
Total Employee	140	121	19
Contractor employees -			
Jay- Vijay	32	32 nos.	00
Sodexo	14	14 nos.	00
Security	08	04 nos.	04
OHC	02	02 nos.	00
Outside another Unit	06	06 nos.	00
Engg Contractor	55	55 nos.	00
Driver	04	04 nos.	00
Other Visitor	02	02 nos.	00
Total	123	119	04
Total Company Employee	140	121	19
Total Contractor Employee	123	119	04
Total	263	240	23

Positive points.

- Emergency call 999 dialed immediately and clear communication to Security.
- The security officer promptly communicated on the PA system announcing.
- Total time required 14 minutes for mock drill including Headcount & all clear sirens.
- API, other dept employee & contract employee in API I immediately evacuated by using staircase after announcement.
- The observer shared their findings with all those present at the assembly point.

MOCK DRILL REPORT

- Evacuation time 7 mins.
- Total Head count 240 Nos
- Points for improvement:

<u>SN.</u>	<u>Observation / Improvement</u> <u>Point</u>	<u>Action Plan</u>	<u>Responsibility</u>	<u>Target Date</u>
1.	During the mock drill, it was identified that the siren/Hooter voice was not audible in the contract shed area, indicating a need for improvement in the emergency alarm audibility system.	Place an extra hooter/siren closer to the contractor shed.	Mr. Mandeep Kashyap.	TCD- 20.05.2026
2.	The hooter was not audible in the QA Office and Meeting Room areas.	Place an extra hooter/siren to be provided.	Mr. Mandeep Kashyap.	TCD- 20.05.2026
3.	It was observed that the engineering contractor workmen did not respond seriously during the emergency.	To be need for improved awareness and training related to emergency preparedness.	Mr. Ankur Sharma/ Lalit Pawar.	TCD- 20.02.2026
4.	It was observed that the headcount process took more time than expected.	Security should maintain a employee/visitor/contractor logbook that is easy to cross-check.	Mr. Dipak Baravkar.	TCD- 25.02.2026
5.	visitors and employees from other units do not know where the emergency assembly point is located.	Provide a safety card/pamphlet at the gate showing emergency exits/emergency number and assembly points.	Mr. Brijesh Yadav.	TCD- 20.05.2026

MOCK DRILL REPORT

6.	It was observed that the QC employee did not respond seriously during the emergency.	To be need for improved awareness and training related to emergency preparedness.	Mr. Lalit Pawar/ Girish Bendale.	TCD- 25.02.2026
7.	During emergency siren activation (60 seconds up–down cycle), the security team does not have a stopwatch or timing device to ensure accurate duration.	Issue a digital stopwatch to the security control room.	Mr. Brijesh Yadav.	TCD- 20.03.2026

Mock Drill Photos:

MOCK DRILL REPORT

Cipla
Kurkumbh



RST 204 tank overflow and fire catch



MCP activated

MOCK DRILL REPORT



Emergency dial - 999



PA system announcement at ECC



Site Controller given instructions to security officer at ECC.



Head Count taken by Security Team

PUBLIC NOTICE

WE ARE PLEASED TO INFORM THAT 'MINISTRY OF ENVIRONMENT, FOREST AND CLIMATE CHANGE (MoEFCC)', GOVERNMENT OF INDIA, [ISSUED BY THE STATE ENVIRONMENT IMPACT ASSESSMENT AUTHORITY (SEIAA), MAHARASHTRA] HAS ACCORDED AN "ENVIRONMENTAL CLEARANCE" VIDE ITS EC IDENTIFICATION NO - EC23B021MH194305 DATED 18th MAY, 2023 TO "M/S. CIPLA LIMITED", (UNIT - II), PLOT NO. D-27, MIDC KURKUMBH, TALUKA: DAUND, DISTRICT: PUNE, STATE: MAHARASHTRA FOR EXPANSION OF BULK DRUGS AND INTERMEDIATES MANUFACTURING UNIT. COPIES OF THE ENVIRONMENTAL CLEARANCE LETTER ARE AVAILABLE WITH THE MAHARASHTRA POLLUTION CONTROL BOARD (MPCB). WEBSITE OF THE INDUSTRY AND MAY ALSO BE SEEN AT THE WEBSITE OF MINISTRY OF ENVIRONMENT, FOREST AND CLIMATE CHANGE, NEW DELHI. AT

<http://parivesh.nic.in>
FOR, M/S. CIPLA LIMITED
(UNIT - II),
MIDC KURKUMBH, TALUKA:
DAUND, DISTRICT: PUNE.

VICE PRESIDENT
TECHNICAL

पुण्य नगरी**जाहीर निवेदन**

आम्हाला कर्तव्यप्राप्त आनंद होतो की "पर्यावरण, वने व हवामान बदल मंत्रालय": भारत सरकार [राज्य पर्यावरण आघात मूल्यांकन प्राधिकरण (रापआमूपा), महाराष्ट्र, द्वारे जारी] यांच्या दि. १८.०५.२०२३ रोजीच्या पर्यावरणीय स्वीकृती पत्र. क्र EC23B021MH194305 द्वारे "मे. सिप्ला लिमिटेड" (युनीट २) यांच्या प्लॉट नं. डी २७, एम. आय. डी. सी. कुरकुंभ, तालुका दौंड, जिल्हा पुणे, महाराष्ट्र राज्य येथील विस्तारित बल्क ड्रग्स आणि इंटरमिडीएट्स मॅन्युफॅक्चरिंग प्रकल्पास 'पर्यावरण स्वीकृती' मिळाली आहे. संबंधित पर्यावरण स्वीकृती कागदपत्रांच्या प्रती महाराष्ट्र राज्य प्रदुषण निवंत्रण मंडळ, प्रकल्प संकेतस्थळ आणि पर्यावरण, वने व हवामान बदल मंत्रालय, नवी दिल्ली यांच्या खालील संकेतस्थळावर उपलब्ध आहेत.

<http://parivesh.nic.in>

मे. सिप्ला लिमिटेड
(युनीट २) करीता,
एम. आय. डी. सी. कुरकुंभ,
तालुका - दौंड, जिल्हा- पुणे
उपाध्यक्ष तांत्रिक





ANNEXURE-IVX

FW: Half yearly compliance report Cipla Unit 2 (Jun-25 to Nov-25)

From Sanjay Mohite/EHS/KKB-II <Sanjay.Mohite@Cipla.com>

Date Fri 5/15/2026 12:30 PM

To Bapu Dendage/EHS/KKB-II <Bapu.Dendage@Cipla.com>

2 attachments (17 MB)

Half yearly compliance report (New EC 2023)Cipla Unit 2 (Jun-25 to Nov-25).pdf; Half yearly compliance report (old EC 2007)Cipla Unit 2 (Jun-25 to Nov-25).pdf;

FYI

From: Sanjay Mohite/EHS/KKB-II

Sent: 01.12.2025 15:29

To: ecompliance-mh@gov.in

Subject: Half yearly compliance report Cipla Unit 2 (Jun-25 to Nov-25)

Respected Sir,

Please find the attached Half Yearly EC compliance report for EC No **SIA/MH/IND3/70271/2018** dated **18th May 2023(new EC)** & EC No **J-11011/368/2006-IA-II(I)** dated **31st July 2007** of M/s Cipla Ltd, Unit II Plot-No. D-27, MIDC Kurkumbh Tal-Daund, Dist Pune., Maharashtra , for the period of **June 2025 to Nov. 2025.**

Regards

Sanjay Mohite


EHS Dept.

Cipla Ltd
D-27 , MIDC Area, Kurkumbh
Tal-Daund, Dist-Pune

Screenshot of Website

ANNEXURE - XIV

Please find link URL :: <https://www.cipla.com/about-us/manufacturing>

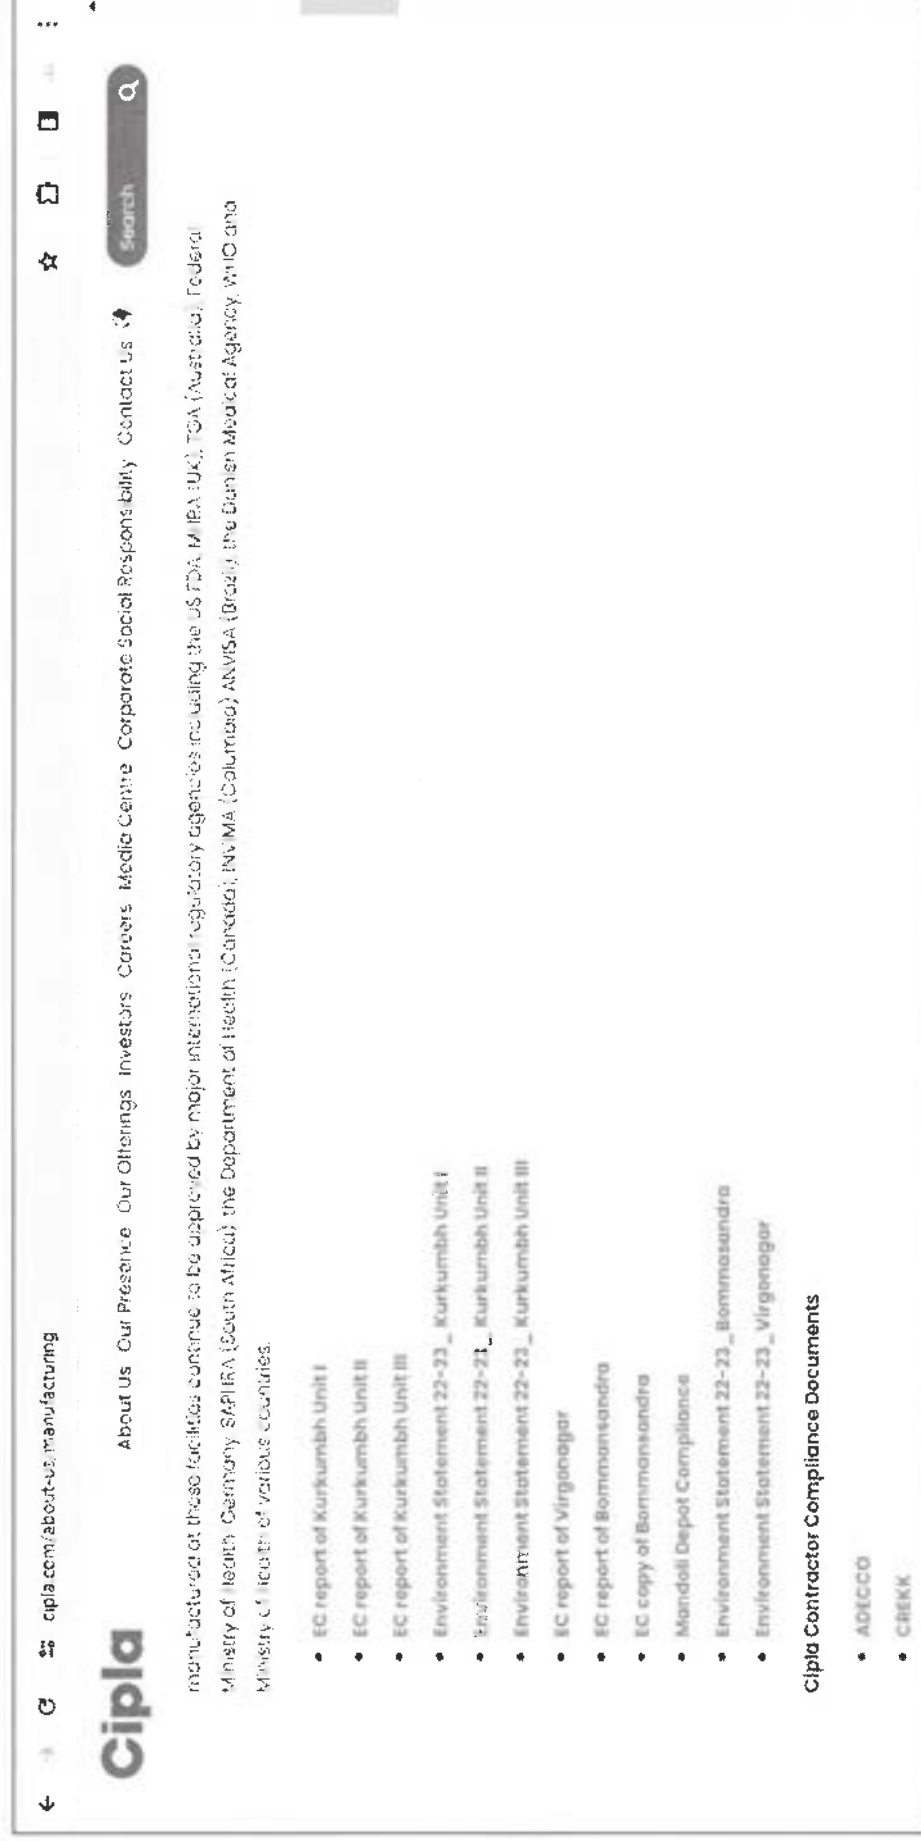

Environment Management Cell KKB - Unit-II

Mr.Amol Sarmandal
(Site Head)

Mr.Narendra Raut
(Unit Head)

Mr. Gyanesh Singh
(Site EHS head)

Mr.Gaurav Patil-M.tech
Environment
(Environment Head)

Mr.Sanjay Mohite - Msc.Env.science
(Environment Section Head)


Mr. Bapu Dendage. M.Sc.
Env.Science /ADIS
(Asst. Manager)

Mr. Ganesh Supe. M.Sc.
Env.Science/ADIS
(Sr Executive)

Mr.Sunil Salunke - Bsc
chemistry
(Sr Executive)

Mr.Sanket Chaugule -M.Sc.
Env. Science (Sr Executive)

Mr. Arbaaz Khureshi - B tech
Chemical
(Trainee)

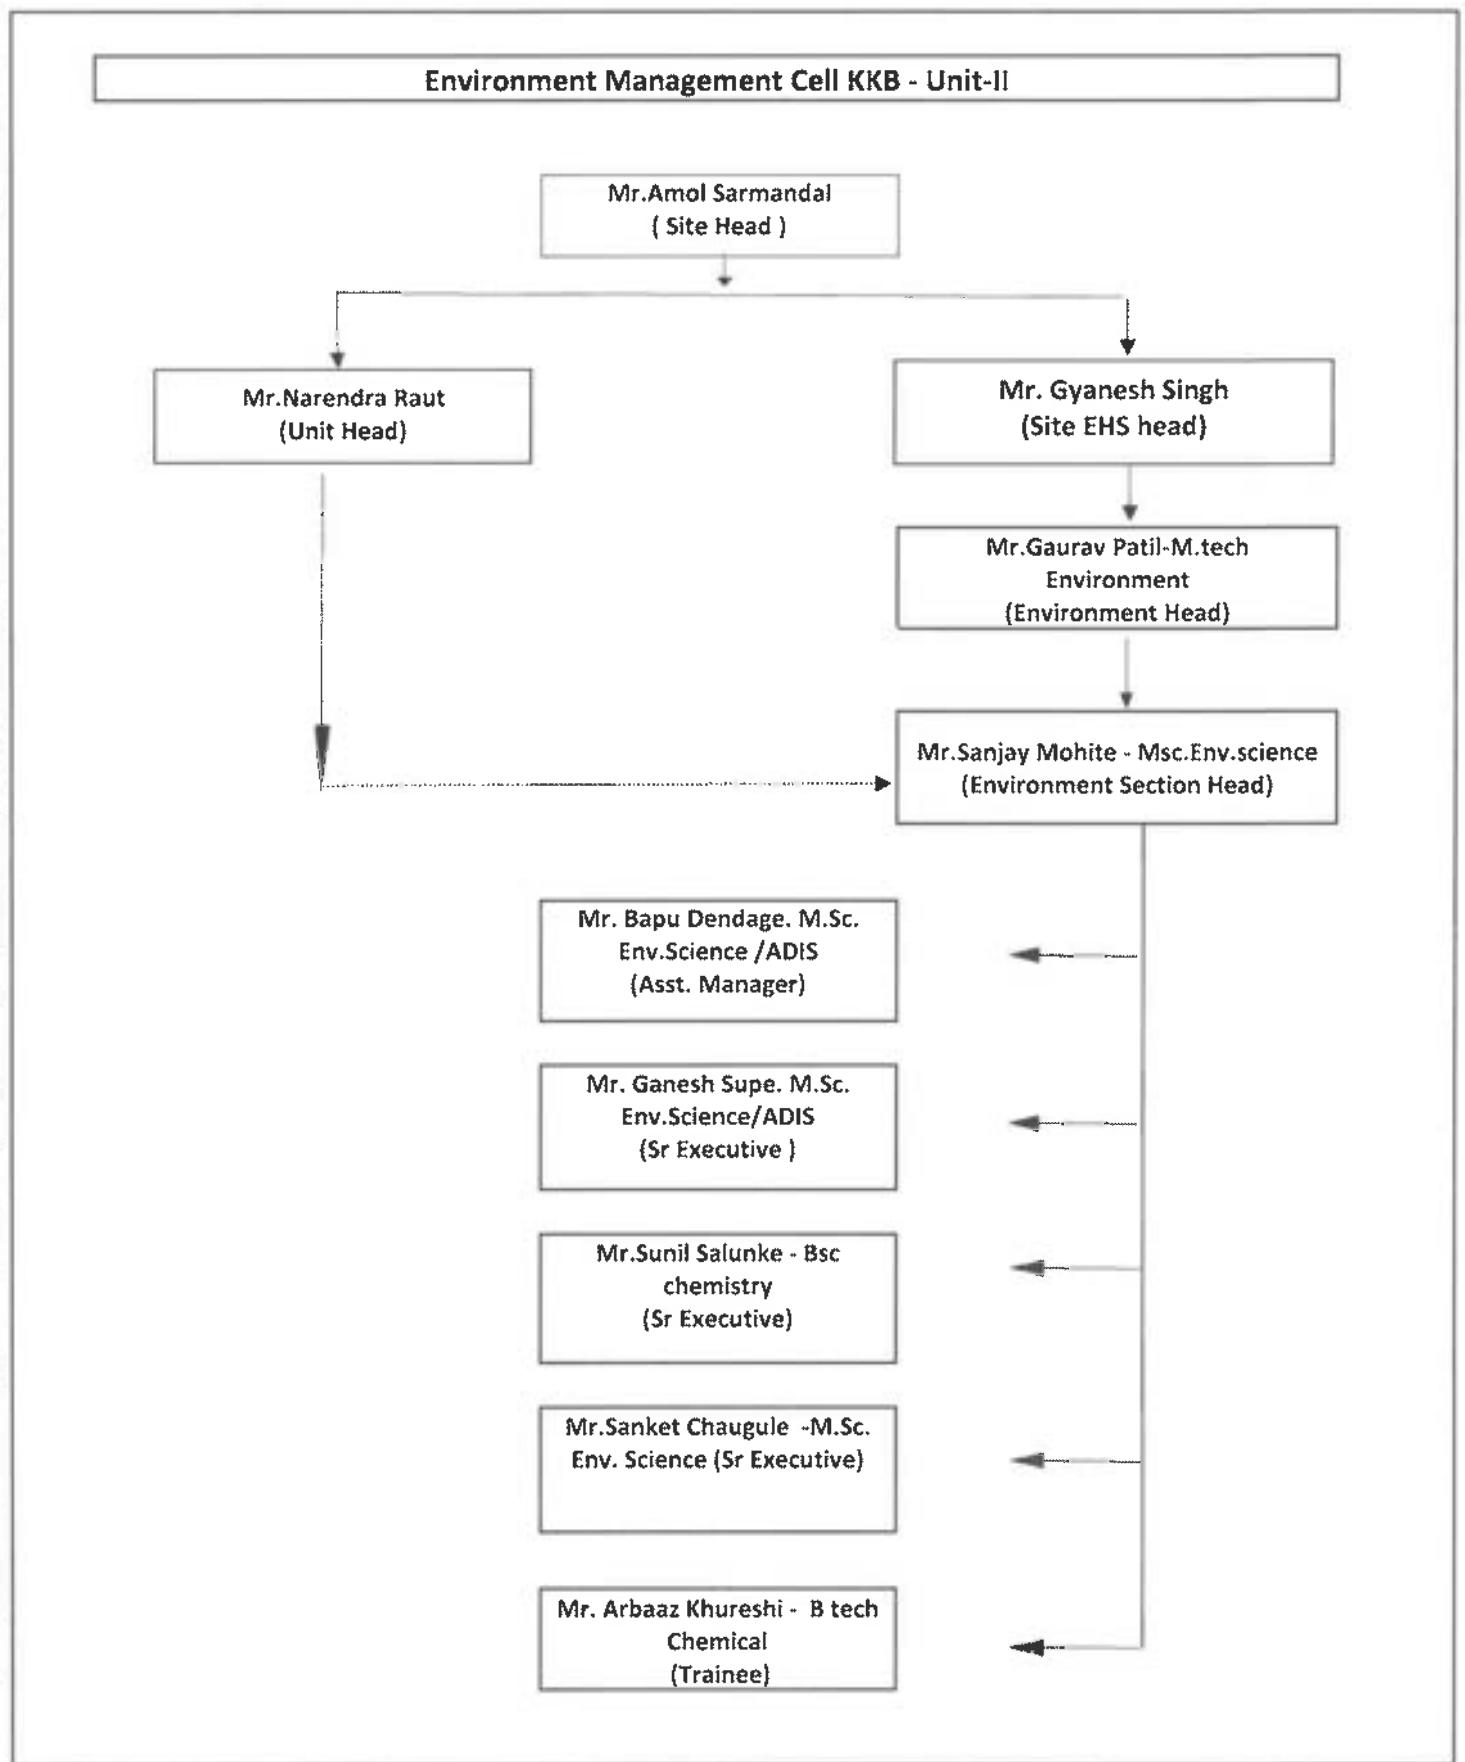



EHS SCANNER

Dr. Vaibhav Chakurkar
MBBS, AFIH, ADIS
DISH Authorised Certifying Surgeon
PUNE District

MAHARASHTRA FACTORIES RULES

FORM 6

(see rule 18)

CERTIFICATE OF MEDICAL EXAMINATION : JAN - FEB - 2026

Name : NILESH S PAWAR

KKB - 2

Sr. No : 119

Reg No. K 2125

EMP ID : 46265

Age : 39 Yrs/ Male

Job Profile : API Quality

Weight : 58 Kg

Company : CIPLA LIMITED

Height : 170 Cms

Address : Unit - II, Plot No. D27, MIDC Kurkumbh, Tal. Daund, Pune 413802

BMI : 20 Kg/m²

Medical And Occupational History	Present c/o : Nil Past h/o : Not significant Family h/o : Not significant			
General Examination	Pulse : 94 / min Blood Pressure : 129 / 87 mmHg in sitting position. No : Pallor/Edema/LN-pathy/Icterus/Cyanosis/Clubbing	Vision Test : Eye Examination		
Clinical Examination	RS : AEBE, clear, no any adventitious sound heard.	Specs :	YES	
Systemic Examination	CVS : S ₁ , S ₂ - heard, no murmur. CNS: Conscious, well oriented, no abnormality detected P/A : Soft, no organomegaly. Skin : Healthy, no abnormality detected.	Test done	Right Eye	Left Eye
		Distant vision	6/6	6/6
		Near vision	N6	N6
		Colour vision	Normal	

Blood & Urine Reports : as per the attached laboratory reports

X Ray Chest PA view : normal study

PFT : within normal limits

Advice -

Physical Fitness : I hereby certify that, I have personally examined ,
NILESH S PAWAR , Residing at Kurkumbh, Pune,
who is desirous of being employed in factory, and that his age
as nearly as can be ascertained from my examination is 39 years
and that he is FIT for Employment as an Adult.

Free from Skin & Infectious Diseases.

Date : 03/02/2026

C-104, Akshay Park, Thergaon, Pune 411 033

+ 91 9373069445

health@ehsscanner.com





डॉ. वैभव चाकुरकर MBBS, AFIH, ADIS (MVC Reg No. 2010/04/2019)
कारखाने अधिनियम १९४७ कलाग १०(२) प्रमाणे
पुणे जिल्ह्यावरिता दिनांक १६/१०/२०१८ पासून १०/१०/२०२६ पर्यंत
प्राशस्त प्रमाणक शस्त्र चिकित्सक क्र. AC528-VC/2019
64856

PULMONARY FUNCTION TEST

EMS SCANNER

Patient: NILESH S PAMAR
Refd. By:
Pred.Eqns: RECORDERS
Date : 02-Feb-2026 12:20 PM

Age : 39 Years Gender : Male
Height : 170 Cms Smoker : No
Weight : 58 Kgs Eth. Corr: 100
ID: K 2125 Temp :

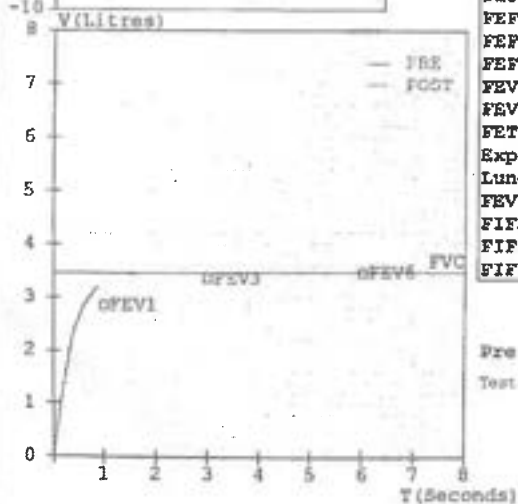

Spirometry (FVC Results)						
Parameter	Pred	M.Pre	%Pred	M.Post	%Pred	%Imp
FVC (L)	03.46	03.21	093	---	---	---
FEV1 (L)	02.85	03.21	113	---	---	---
FEV1/FVC (%)	82.37	100.00	121	---	---	---
FEF25-75 (L/s)	03.98	05.30	133	---	---	---
PEFR (L/s)	08.88	06.85	077	---	---	---
FIVC (L)	---	03.01	---	---	---	---
FEV.5 (L)	---	02.63	---	---	---	---
FEV3 (L)	03.36	03.21	096	---	---	---
PIFR (L/s)	---	03.76	---	---	---	---
FEF75-85 (L/s)	---	02.57	---	---	---	---
FEF.2-1.2 (L/s)	06.96	06.14	088	---	---	---
FEF 25% (L/s)	07.90	06.79	086	---	---	---
FEF 50% (L/s)	05.65	05.60	099	---	---	---
FEF 75% (L/s)	02.76	03.36	122	---	---	---
FEV.5/FVC (%)	---	81.93	---	---	---	---
FEV3/FVC (%)	97.11	100.00	103	---	---	---
FET (Sec)	---	00.90	---	---	---	---
ExptTime (Sec)	---	00.09	---	---	---	---
Lung Age (Yrs)	039	034	087	---	---	---
FEV6 (L)	03.46	---	---	---	---	---
FIF25% (L/s)	---	03.71	---	---	---	---
FIF50% (L/s)	---	03.30	---	---	---	---
FIF75% (L/s)	---	03.05	---	---	---	---

Pre Test COPD Severity
Test within normal limits

Pre Medication Report Indicates
Spirometry within normal limits as (FEV1/FVC) %Pred >95 and FVC %Pred >80.

AARAV PATHOLOGY LABORATORY

Focussed on Quality... Always !!!



PATIENT NAME : K 2125 Nilesh S Pawar

AGE / SEX : 39 Years / Male

REG. ID 3001262125

REFERRAL : EHS SCANNER

119

REG ON : 03/02/2026 05:30 PM

COLLECTED ON : 03/02/2026 09:30 PM

REPORTED ON : 05/02/2026 05:30 PM

SAMPLE ID



033001262125

CBC (COMPLETE BLOOD COUNT)

Test Name	Result	Unit	Reference Range
HAEMOGLOBIN	14.6	gm/dl	M : 13.0 - 17.0, F : 12.0 - 15.0
RED BLOOD CELLS			
TOTAL RBC COUNT	5.46	10 ⁶ /uL	M : 4.5 - 5.5, F : 3.8 - 4.8
HCT (PCV)	45.8	%	M : 40.0 - 50.0, F : 36.0 - 46.0
MCV	84	fL	83.0 - 101.0
MCH	26.7	Pg	27.0 - 32.0
MCHC	31.8	g/dl	31.5 - 34.5
RDW-CV	13.1	%	116 - 14.0
WHITE BLOOD CELLS			
TOTAL WBC COUNT	8700	/cmm	4000 - 10000
WBC DIFFERENTIAL COUNT			
NEUTROPHILS	69.3	%	40.0 - 80.0
LYMPHOCYTES	23.5	%	20.0 - 40.0
MONOCYTES	4.8	%	2.0 - 10.0
EOSINOPHILS	2.4	%	1.0 - 6.0
BASOPHILS	0	%	0 - 1.0
ABSOLUTE DIFFERENTIAL COUNTS			
ABSOLUTE NEUTROPHILS COUNT	6029.1	/cmm	2000 - 7400
ABSOLUTE LYMPHOCYTES COUNT	2044.5	/cmm	1300 - 3600
ABSOLUTE MONOCYTES COUNT	417.6	/cmm	300 - 1000
ABSOLUTE EOSINOPHILS COUNT	208.8	/cmm	40 - 400
ABSOLUTE BASOPHILS COUNT	0	/cmm	0 - 100
PLATELET COUNT	332000	/cmm	150000 - 410000
MPV	10	fL	8.6 - 12.3

-----END OF REPORT-----

Handwritten signature

DR. JAYA CHABUKSWAR
M.B.B.S. MD Pathology, AFHM
Reg. No.3708

* samples processed on automated haematology analyser - MISPA COUNT X PLUS -AGAPPE DIAGNOSTIC

For Home Visit - Call No. : 9168688740

Add. : Plot - 10, C-Section, N-13, CIDCO, Dharavi Nagar, Near Hudson Centre, Aurangabad-431001 E-mail : aaravpath@gmail.com

Dr. Jaya Chabukswar
M.B.B.S. M.D. (Path.)
Reg. No. 3708

AARAV PATHOLOGY LABORATORY

Focussed on Quality... Always !!!



PATIENT NAME : K 2125 Nilesh S Pawar

REG ON : 03/02/2026 05:30 PM

AGE / SEX : 39 Years / Male

COLLECTED ON : 03/02/2026 09:30 PM

REG. ID 3001262125

REPORTED ON : 05/02/2026 05:30 PM

REFERRAL : EHS SCANNER

119

SAMPLE ID



143001262125

URINE ROUTINE ANALYSIS

Test Name	Result	Unit	Reference Range
PHYSICAL EXAMINATION			
QUANTITY	10	ml	
COLOUR	Pale Yellow		-
APPEARANCE	Clear		-
REACTION (PH)	Acidic		4.8 - 7.6
SPECIFIC GRAVITY	1.015		1.002 - 1.030
CHEMICAL EXAMINATION			
PROTEIN / ALBUMIN	Absent		
GLUCOSE	Absent		
UROBILINOGEN	Normal		0.5 - 4.0
BILE SALTS	Absent		
BILE PIGMENTS	Absent		
KETONE	Absent		
NITRATE	Absent		
MICROSCOPIC EXAMINATION			
PUS CELLS	Absent	/HPF	0 - 5
EPITHELIAL CELLS	Absent	/HPF	0 - 15
RBCS	Absent	/HPF	Absent
CAST	Absent		Absent
CRYSTALS	Absent		Absent
PARACITES	Absent		
BACTERIA	Absent		

-----END OF REPORT-----

DR. JAYA CHABUKSWAR
M.B.B.S. MD Pathology, AFIH
Reg. No.3708

For Home Visit Call No. : 9168883740

Add. : Plot 15, C-Sector, N-13, CIDCO, Bharat Nagar, Near Hudco Corner, Aurangabad-431001 E-mail : aaravpath@gmail.com

Dr. Jaya Chabukswar
M.B.B.S., M.D. (Path.)
Reg. No. 3708

AARAV PATHOLOGY LABORATORY

Focussed on Quality... Always !!!



PATIENT NAME : K 2125 Nilesh S Pawar

AGE / SEX : 39 Years / Male

REG. ID : 3001262125

REFERRAL : EHS SCANNER

119

REG ON : 03/02/2026 05:30 PM

COLLECTED ON : 03/02/2026 09:30 PM

REPORTED ON : 05/02/2026 05:30 PM

SAMPLE ID



013001262125

PLASMA GLUCOSE-RANDOM

Test Name	Result	Unit	Reference Range	Method
PLASMA GLUCOSE-RANDOM	100	mg/dl	Upto 140.0	GOD-POD

HBA1C -GLYCOSYLATED HEMOGLOBIN

Test Name	Result	Unit	Reference Range	Method
HBA1C -GLYCOSYLATED HEMOGLOBIN	5.11	%	Normal : 4.5 - 6.3 In Diabetes Excellent Control : 4.5 - 6.3 Good Control : 6.3 - 7.0 Fair Control : 7.1 - 8.0 Poor Control : Above 8.0	HPLC

LFT (LIVER FUNCTION TEST) - SERUM

Test Name	Result	Unit	Reference Range	Method
BILIRUBIN TOTAL	0.56	mg/dl	0.3-1.2	Diazo
BILIRUBIN DIRECT	0.27	mg/dl	< 0.4	Diazo
BILIRUBIN INDIRECT	0.29	mg/dl	< 0.7	Calculated
SGPT	16.9	U/L	0.0 - 40.0	IFCC
SGOT	18.6	U/L	0.0 - 45.0	IFCC
ALKALINE PHOSPHATASE	42.2	mg/dl	30.0 - 115.0	IFCC - AMP
GGT (GAMMA GT)	10.1	mg/dl	10.0 - 45.0	IFCC
PROTEIN TOTAL	7.19	g/dl	6.0 - 8.0	Biuret-EP
ALBUMIN	4.23	g/dl	3.5 - 4.8	BCG-EP
GLOBULIN	2.96	g/dl	2.8 - 3.4	Calculated

(RENAL FUNCTION TEST) - SERUM

Test Name	Result	Unit	Reference Range	Method
BLOOD UREA LEVEL	19.4	mg/dl	14.0 - 45.0	UV-Kinetic
CREATININE	0.93	mg/dl	0.4 - 1.5	Jaffes-Kinetic
BLOOD UREA NITROGEN	9.24	mg/dl	7.0 - 23.0	Calculated
URIC ACID	4.44	mg/dl	2.5 - 8.0	Uricase-EP

(LIPID PROFILE) - SERUM

Test Name	Result	Unit	Reference Range	Method
CHOLESTEROL TOTAL	176.5	mg/dl	Optimal < 200.0	CHOD-POD/CHOD-PAP
TRIGLYCERIDES	69.1	mg/dl	< 150.0	GPO-PAP
CHOLESTEROL HDL	43.9	mg/dl	> 40	Selective Detergent
CHOLESTEROL VLDL	13.8	mg/dl	0.00 -30.0	Calculated
CHOLESTEROL LDL	118.7	mg/dl	Optimal < 100.0	Calculated

-----END OF REPORT-----

DR. JAYA CHABUKSWAR
M.B.B.S. MD Pathology, AFIH
Reg. No.3708

* samples processed on fully automated biochemistry analyser - MESA NANO PLUS-AGAPPE DIAGNOSTIC

For Home Visit - Call No. : 9188688740

Add. / Plot : 15 G-Sector, N-13, CIDCO, Bhamburda Nagar, Near Huda Corner, Aurangabad-431001 E-mail : aaravpath@gmail.com

Dr. Jaya Chabukswar
M.B.B.S., M.D. (Path)
Reg. No. 3708



EHS SCANNER

MAHARASHTRA FACTORIES RULES

FORM 6

Dr. Vaibhav Chakurkar
MBBS, AFIH, ADIS
DISH Authorised Certifying Surgeon
PUNE District

(see rule 18)

CERTIFICATE OF MEDICAL EXAMINATION : JAN - FEB - 2026

Name : PRASHANT B MENGAWADE

KKB - 2

Sr. No : 16

Reg No. K 2017

EMP ID : 109548

Age : 36 Yrs/ Male

Job Profile : API

Weight : 64 Kg

Company : CIPLA LIMITED

Height : 167 Cms

Address : Unit - II, Plot No. D27, MIDC Kurkumbh, Tal. Daund, Pune 413802

BMI : 22.9 Kg/m²

Medical And Occupational History	Present c/o : Nil Past h/o : Not significant Family h/o : Mother - Hypertension			
General Examination	Pulse : 73 / min Blood Pressure : 107 / 81 mmHg in sitting position. No : Pallor/Edema/LN-pathy/Icterus/Cyanosis/Clubbing	Vision Test : Eye Examination		
Clinical Examination	RS : AEBE, clear, no any adventitious sound heard.	Specs :	No	
Systemic Examination	CVS : S ₁ , S ₂ - heard, no murmur. CNS: Conscious, well oriented, no abnormality detected P/A : Soft, no organomegaly. Skin : Healthy, no abnormality detected.	Test done	Right Eye	Left Eye
		Distant vision	6/6	6/6
		Near vision	N6	N6
		Colour vision	Normal	

Blood & Urine Reports : as per the attached laboratory reports

X Ray Chest PA view : normal study

PFT : within normal limits

Advice -

Physical Fitness : I heareby certify that, I have personally examined ,
PRASHANT B MENGAWADE , Residing at Kurkumbh, Pune,
who is desirous of being employed in factory, and that his age
as nearly as can be ascertained from my examination is 36 years
and that he is FIT for Employment as an Adult.

Free from Skin & Infectious Diseases.

Date : 02/02/2026

डॉ. वैभव चाकुरकर MBBS, AFIH, ADIS MMC Reg No. 2018/04/2019
कारखाने अधिनियम १९४८ का कलाम १०(२) प्रमाणे
पुणे जिल्ह्याकरिता दिनांक १६/१०/२०२२ पासून १५/१०/२०२६ पर्यंत
प्राधिकृत प्रमाणक शल्य चिकित्सक. ACS२४-VC/२०१९

64856

AARAV PATHOLOGY LABORATORY

Focussed on Quality... Always !!!



PATIENT NAME : K 2017 Prashant B Mengawade
AGE / SEX : 36 Years / Male
REG. ID : 3001262017
REFERRAL : EHS SCANNER 16

REG ON : 02/02/2026 05:30 PM
COLLECTED ON : 02/02/2026 09:30 PM
REPORTED ON : 04/02/2026 05:30 PM
SAMPLE ID : 
033001262017

CBC (COMPLETE BLOOD COUNT)

Test Name	Result	Unit	Reference Range
HAEMOGLOBIN	14.7	gm/dl	M : 13.0 -17.0, F : 12.0-15.0
RED BLOOD CELLS			
TOTAL RBC COUNT	4.71	$10^6/\mu\text{L}$	M : 4.5 - 5.5, F : 3.8 - 4.8
HCT (PCV)	45.2	%	M : 40.0 - 50.0, F : 36.0 - 46.0
MCV	96	fL	83.0 - 101.0
MCH	31.3	Pg	27.0 - 32.0
MCHC	32.6	g/dl	31.5 - 34.5
RDW-CV	14.7	%	116 - 14.0
WHITE BLOOD CELLS			
TOTAL WBC COUNT	6000	/cmm	4000 - 10000
WBC DIFFERENTIAL COUNT			
NEUTROPHILS	61.6	%	40.0 - 80.0
LYMPHOCYTES	30.8	%	20.0 - 40.0
MONOCYTES	5.1	%	2.0 - 10.0
EOSINOPHILS	2.5	%	1.0 - 6.0
BASOPHILS	0	%	0 - 1.0
ABSOLUTE DIFFERENTIAL COUNTS			
ABSOLUTE NEUTROPHILS COUNT	4065.6	/cmm	2000 - 7400
ABSOLUTE LYMPHOCYTES COUNT	2032.8	/cmm	1300 - 3600
ABSOLUTE MONOCYTES COUNT	334.4	/cmm	300 - 1000
ABSOLUTE EOSINOPHILS COUNT	167.2	/cmm	40 - 400
ABSOLUTE BASOPHILS COUNT	0	/cmm	0 - 100
PLATELET COUNT	325000	/cmm	150000 - 410000
MPV	9.1	fL	8.6 - 12.3

-----END OF REPORT-----

Handwritten signature

DR. JAYA CHABUKSWAR
M.B.B.S. MD Pathology, AFIH
Reg. No.3708

* samples processed on automated haematology analyser - MISPA COUNT X PLUS -AGAPPE DIAGNOSTIC

For Home Visit : Call No. : 9185622740

Add : Plot - 18, G-Scheme, N-13, CIDCO, Bhamburda Nager, Near Huda's Corner, Aurangabad-431001 E-mail : aaravpathology@gmail.com

Dr. Jaya Chabukswar
M.B.B.S., M.D. (Path.)
Reg. No. 3708

AARAV PATHOLOGY LABORATORY

Focussed on Quality... Always !!!



PATIENT NAME : K 2017 Prashant B Mengawade

REG ON : 02/02/2026 05:30 PM

AGE / SEX : 36 Years / Male

COLLECTED ON : 02/02/2026 09:30 PM

REG. ID : 3001262017

REPORTED ON : 04/02/2026 05:30 PM

REFERRAL : EHS SCANNER

16

SAMPLE ID



143001262017

URINE ROUTINE ANALYSIS

Test Name	Result	Unit	Reference Range
PHYSICAL EXAMINATION			
QUANTITY	10	ml	
COLOUR	Pale Yellow		-
APPEARANCE	Clear		-
REACTION (PH)	Acidic		4.8 - 7.6
SPECIFIC GRAVITY	1.015		1.002 - 1.030
CHEMICAL EXAMINATION			
PROTEIN / ALBUMIN	Absent		
GLUCOSE	Absent		
UROBILINOGEN	Normal		0.5 - 4.0
BILE SALTS	Absent		
BILE PIGMENTS	Absent		
KETONE	Absent		
NITRATE	Absent		
MICROSCOPIC EXAMINATION			
PUS CELLS	Absent	/HPF	0 - 5
EPITHELIAL CELLS	Absent	/HPF	0 - 15
RBCS	Absent	/HPF	Absent
CAST	Absent		Absent
CRYSTALS	Absent		Absent
PARACITES	Absent		
BACTERIA	Absent		

-----END OF REPORT-----

DR. JAYA CHABUKSWAR
M.B.B.S., MD Pathology, AFIH
Reg. No.3708

Dr. Jaya Chabukswar
M.B.B.S., M.D. (Path.)
Reg. No. 3708

or Home Visit Call No. : 9168889740

Add : 16/2, Sector, N-13, CIDCO, Bhamburda Nagar, Near Hukam Chowk, Aurangabad-431001 E-mail : aaravpathology@gmail.com

AARAV PATHOLOGY LABORATORY

Focussed on Quality... Always !!!



PATIENT NAME : K 2017 Prashant B Mengawade
AGE / SEX : 36 Years / Male
REG. ID : 3001262017
REFERRAL : EHS SCANNER 16
REG ON : 02/02/2026 05:30 PM
COLLECTED ON : 02/02/2026 09:30 PM
REPORTED ON : 04/02/2026 05:30 PM
SAMPLE ID : 013001262017

PLASMA GLUCOSE-RANDOM

Test Name	Result	Unit	Reference Range	Method
PLASMA GLUCOSE-RANDOM	97	mg/dl	Upto 140.0	GOD-POD

HBA1C -GLYCOSYLATED HEMOGLOBIN

Test Name	Result	Unit	Reference Range	Method
HBA1C -GLYCOSYLATED HEMOGLOBIN	5	%	Normal : 4.5 - 6.3 In Diabetes Excellent Control : 4.5 - 6.3 Good Control : 6.3 - 7.0 Fair Control : 7.1 - 8.0 Poor Control : Above 8.0	HPLC

LFT (LIVER FUNCTION TEST) - SERUM

Test Name	Result	Unit	Reference Range	Method
BILIRUBIN TOTAL	1.31	mg/dl	0.3-1.2	Diazo
BILIRUBIN DIRECT	0.62	mg/dl	< 0.4	Diazo
BILIRUBIN INDIRECT	0.69	mg/dl	< 0.7	Calculated
SGPT	18.9	U/L	0.0 - 40.0	IFCC
SGOT	23.3	U/L	0.0 - 45.0	IFCC
ALKALINE PHOSPHATASE	47.3	mg/dl	30.0 - 115.0	IFCC - AMP
GGT (GAMMA GT)	20.8	mg/dl	10.0 - 45.0	IFCC
PROTEIN TOTAL	7.33	g/dl	6.0 - 8.0	Biuret-EP
ALBUMIN	4.31	g/dl	3.5 - 4.8	BCG-EP
GLOBULIN	3.02	g/dl	2.8 - 3.4	Calculated

(RENAL FUNCTION TEST) - SERUM

Test Name	Result	Unit	Reference Range	Method
BLOOD UREA LEVEL	15.4	mg/dl	14.0 - 45.0	UV-Kinetic
CREATININE	0.74	mg/dl	0.4 - 1.5	Jaffes-Kinetic
BLOOD UREA NITROGEN	7.35	mg/dl	7.0 - 23.0	Calculated
URIC ACID	4.82	mg/dl	2.5 - 8.0	Uricase-EP

(LIPID PROFILE) - SERUM

Test Name	Result	Unit	Reference Range	Method
CHOLESTEROL TOTAL	154.7	mg/dl	Optimal < 200.0	CHOD-POD/CHOD-PAP
TRIGLYCERIDES	44.3	mg/dl	< 150.0	GPO-PAP
CHOLESTEROL HDL	38.5	mg/dl	> 40	Selective Detergent
CHOLESTEROL VLDL	8.8	mg/dl	0.00 - 30.0	Calculated
CHOLESTEROL LDL	107.3	mg/dl	Optimal < 100.0	Calculated

END OF REPORT

DR. JAYA CHABUKSWAR
M.B.B.S. MD Pathology, AFIH
Reg. No. 3708

* samples processed on fully automated biochemistry analyser - MISPA NANO PLUS-AGAPPE DIAGNOSTIC

For Home Visit - Call No. : 9108688740

Add. : Plot : 15, G-Sector, N-13, CIDCO, Bhamburda Nagar, Near Huda's Corner, Aurangabad-431001 E-mail : aaravpath@gmail.com





Dr. Jaya Chabukswar
M.B.B.S., M.D. (Path.)
Reg. No. 3708

EHS SCANNER

Pulmonary Function Test

Patient: PRASHANT MENGAWADE
Refd. By:
Pred.Eqns: RECORDERS
Date : 02-Feb-2026 04:55 PM

Age : 36 Years Gender : Male
Height : 167 Cms Smoker : No
Weight : 64 Kgs Eth. Corr: 100
ID: K 2017 Temp :

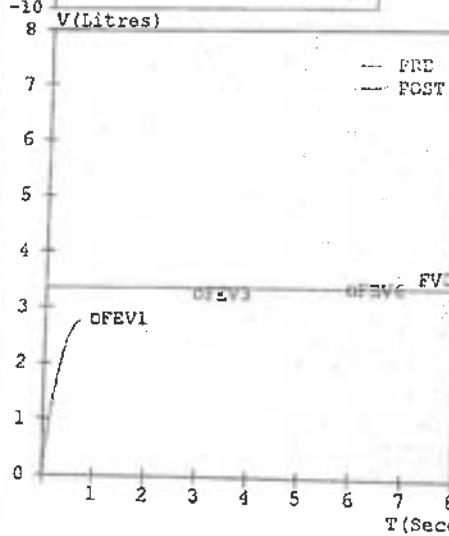

Spirometry (FVC Results)

Parameter	Pred	M. Pre	%Pred	M. Post	%Pred	%Imp
FVC (L)	03.36	02.80	083	---	---	---
FEV1 (L)	02.79	02.80	100	---	---	---
FEV1/FVC (%)	83.04	100.00	120	---	---	---
FEF25-75 (L/s)	04.06	05.15	127	---	---	---
PEFR (L/s)	08.78	08.53	097	---	---	---
FIVC (L)	---	02.29	---	---	---	---
FEV.5 (L)	---	02.56	---	---	---	---
FEV3 (L)	03.26	02.80	086	---	---	---
PIFR (L/s)	---	06.20	---	---	---	---
FEF75-85 (L/s)	---	03.35	---	---	---	---
FEF.2-1.2 (L/s)	07.01	07.26	104	---	---	---
FEF 25% (L/s)	07.86	07.45	095	---	---	---
FEF 50% (L/s)	05.66	05.43	096	---	---	---
FEF 75% (L/s)	02.84	03.60	127	---	---	---
FEV.5/FVC (%)	---	91.43	---	---	---	---
FEV3/FVC (%)	97.02	100.00	103	---	---	---
FET (Sec)	---	00.76	---	---	---	---
ExptTime (Sec)	---	00.04	---	---	---	---
Lung Age (Yrs)	036	036	100	---	---	---
FEV6 (L)	03.36	---	---	---	---	---
FIF25% (L/s)	---	00.68	---	---	---	---
FIF50% (L/s)	---	05.26	---	---	---	---
FIF75% (L/s)	---	06.14	---	---	---	---

Pre Test COPD Severity
Test within normal limits

Pre Medication Report Indicates
Spirometry within normal limits as (FEV1/FVC)%Pred >95 and FVC%Pred >80.

The contents of this report require clinical co-relation before any clinical action.

<http://www.rasindia.com> © RPS Spirometer (Helios_v3.1.85)



ANNEXURE - XVIII

Maharashtra Pollution Control Board

महाराष्ट्र प्रदूषण नियंत्रण मंडळ

FORM V

(See Rule 14)

Environmental Audit Report for the financial Year ending the 31st March 2025

Unique Application Number

MPCB-ENVIRONMENT_STATEMENT-0000087338

Submitted Date

29-09-2025

PART A

Company Information

Company Name

M/s Cipla Ltd.

Application UAN number

UAN No. 0000238363

Address

Plot no D-27, Kurkumbh MIDC
Kurkumbh, Tal-Daund, Dist. - Pune
413802

Plot no

D-27

Taluka

Daund

Village

Kurkumbh

Capital Investment (In lakhs)

255.58

Scale

L.S.I.

City

Pune

Pincode

413802

Person Name

Mr. Narendra Raut

Designation

Associate Director

Telephone Number

02117230601

Fax Number

02117235532

Email

sanjay.mohite@cipla.com

Region

SRO-Pune I

Industry Category

Red

Industry Type

R58 Pharmaceuticals

Last Environmental statement submitted online

yes

Consent Number

Format1.0/CAC/UAN No. MPCB-
CONSENT-0000238363/CR/2508003428

Consent Issue Date

2025-08-26

Consent Valid Upto

2030-04-30

Establishment Year

2007

Date of last environment statement submitted

Sep 26 2024 12:00:00:000AM

Industry Category Primary (STC Code) & Secondary (STC Code)

Product Information

Product Name

Anti-Retroviral, Anti-Inflammatory, Proton Pump Inhibitors, Anti-Diabetic, Anti-Psychotic,
Anti-Convulsant, Anti-Depressant, Anti-Hypertensive, Anti-Anginal

Consent Quantity

220.0

Actual Quantity

28.526

UOM

MT/A

By-product Information

By Product Name

NA

Consent Quantity

0

Actual Quantity

0

UOM

MT/A

Part-B (Water & Raw Material Consumption)

1) Water Consumption in m3/day

Water Consumption for Process	Consent Quantity in m3/day	Actual Quantity in m3/day
	158.89	39.93
Cooling	168.00	43.51
Domestic	45.00	13.92
All others	255.00	3.65
Total	626.89	101.01

2) Effluent Generation in CMD / MLD

Particulars	Consent Quantity	Actual Quantity	UOM
Daily quantity of trade Effluent	138.04	44.1	CMD
Daily quantity of sewage Effluent	35	4.8	CMD

2) Product Wise Process Water Consumption (cubic meter of process water per unit of product)

Name of Products (Production)	During the Previous financial Year	During the current Financial year	UOM
Anti-Retroviral, Anti-Inflammatory, Proton Pump Inhibitors, Anti-Diabetic, Anti-Psychotic, Anti -Convulsant, Anti- Depressant, Anti-Hypertensive, Anti- Anginal	471	497	

3) Raw Material Consumption (Consumption of raw material per unit of product)

Name of Raw Materials	During the Previous financial Year	During the current Financial year	UOM
11001376	0.16	0.13	Ton/Ton
11000106	6.01	4.19	Ton/Ton
11000934	0.39	0.34	Ton/Ton
11001336	0.56	0.37	Ton/Ton
11001352	0.06	0	Ton/Ton
11001435	0.02	0.026	Ton/Ton
11001527	0.89	0.17	Ton/Ton
11001546	0.27	0.072	Ton/Ton
11001594	0.06	0	Ton/Ton
11001652	1.90	0.046	Ton/Ton
11001654	3.62	3.93	Ton/Ton
11000145	0.67	1.0	Ton/Ton
11001830	0.12	0	Ton/Ton
11002026	26.43	12.5	Ton/Ton
11002139	0.13	0.068	Ton/Ton
11002143	0.39	0.57	Ton/Ton
11002415	0.36	0.44	Ton/Ton
11002626	0.03	0.0	Ton/Ton
11002639	0.43	0.0	Ton/Ton

11002894	0.15	0.0	Ton/Ton
11003042	0.91	0.0	Ton/Ton
11004537	0.24	0.0	Ton/Ton
11003348	0.98	0.53	Ton/Ton
11003350	0.20	0.0	Ton/Ton
11003374	0.02	0.0	Ton/Ton
11003376	3.98	3.07	Ton/Ton
11003411	0.27	0.33	Ton/Ton
11003419	0.01	0.0	Ton/Ton
11001539	0.30	0.18	Ton/Ton
11001809	0.03	0.0	Ton/Ton
11003199	0.18	0.16	Ton/Ton
12000084	0.17	0.0	Ton/Ton
12000164	0.26	0.0	Ton/Ton
12000458	0.00	0.0	Ton/Ton
12000623	0.00	0.0	Ton/Ton
11000121	0.01	0.0003	Ton/Ton
12000723	0.08	0.0	Ton/Ton
12000580	0.01	0.0	Ton/Ton
11000121	0.01	0.0004	Ton/Ton
11000140	0.12	0.0	Ton/Ton
11001019	0.40	0.053	Ton/Ton
11001541	0.004	0.0	Ton/Ton
11002109	0.22	0.26	Ton/Ton
11002128	0.03	0.028	Ton/Ton
11002916	0.02	0.0	Ton/Ton
11003071	0.002	0.0	Ton/Ton
11003121	0.12	0.0	Ton/Ton
11003309	0.22	0.0	Ton/Ton
11003373	0.02	0.033	Ton/Ton
11007592	1.27	0.0	Ton/Ton
11008312	0.05	0.04	Ton/Ton
11008915	8.00	7.04	Ton/Ton
11010978	0.00	0.0	Ton/Ton
12000033	0.05	0.0	Ton/Ton
12000273	0.03	0.0	Ton/Ton
12003625	0.05	0.0	Ton/Ton
12004249	0.07	0.0	Ton/Ton
12004414	0.11	0.0	Ton/Ton
12005553	0.18	0.0	Ton/Ton
11001984	33.33	25.3	Ton/Ton

11003050	0.29	0.0	Ton/Ton
12001001	0.58	1.33	Ton/Ton
11000053	0.00	0.0	Ton/Ton
11000740	0.00	0.0	Ton/Ton
11002022	0.00	0.0	Ton/Ton
11003352	0.29	0.025	Ton/Ton
11011182	0.00	0.0	Ton/Ton
11011393	0.35	0.35	Ton/Ton
12000133	0.35	0.0	Ton/Ton
12000605	0.00	0.0	Ton/Ton
12001220	0.51	0.0	Ton/Ton
12003097	0.00	0.0	Ton/Ton
12003664	0.30	0.0	Ton/Ton
12004745	0.42	0.0	Ton/Ton
12005125	0.00	0.0	Ton/Ton
12005588	0.01	0.0	Ton/Ton
12005764	0.03	0.0	Ton/Ton
12005584	0.04	0.0	Ton/Ton
12004634	0.00	0.0	Ton/Ton
12006138	0.01	0.0	Ton/Ton
11000772	0.001	0.0	Ton/Ton
11001110	0.15	0.0617	Ton/Ton
11002836	0.001	0.0	Ton/Ton
11003581	0.05	0.0	Ton/Ton
11010012	0.01	0.0	Ton/Ton
11011282	0.05	0.0	Ton/Ton
11011423	1.92	2.61	Ton/Ton
11011622	1.62	5.47	Ton/Ton
12000498	0.04	0.0	Ton/Ton
12002175	0.73	0.1786	Ton/Ton
12002785	0.08	0.0	Ton/Ton
12004116	0.03	0.0	Ton/Ton
12004117	0.03	0.0	Ton/Ton
12004118	0.01	0.0	Ton/Ton
12004268	0.03	0.0	Ton/Ton
12005254	0.007	0.0	Ton/Ton
12005256	0.56	0.0	Ton/Ton
12005997	0.32	0.2354	Ton/Ton
12006026	0.14	0.4116	Ton/Ton
12006334	0.05	0.0111	Ton/Ton
12006336	0.01	0.0	Ton/Ton

12006464	0.03	0.0	Ton/Ton
12006314	0.0	0.018	Ton/Ton
91000279	0.0	0.0001	Ton/Ton

4) Fuel Consumption

Fuel Name	Consent quantity	Actual Quantity	UOM
LSHS	1868.8	143.13	KL/A
HSD	360	23.46	KL/A

Part-C

Pollution discharged to environment/unit of output (Parameter as specified in the consent issued)

[A] Water

Pollutants Detail	Quantity of Pollutants discharged (kL/day)	Concentration of Pollutants discharged(Mg/Lit) Except PH,Temp,Colour	Percentage of variation from prescribed standards with reasons	Standard	Reason
	Quantity	Concentration	%variation		
COD(kg/Day)	1.43	32.5	87	250	Within Limit plant having ZLD & trtad watr utilized to utility
BOD kg/day	0.34	7.8	74	30	Within Limit plant having ZLD & trtad watr utilized to utility
TSS (kg/Day)	0.22	5.0	95	100	Within Limit plant having ZLD & trtad watr utilized to utility
TDS (kg/Day)	6.14	139.1	93	2100	Within Limit plant having ZLD & trtad watr utilized to utility

[B] Air (Stack)

Pollutants Detail	Quantity of Pollutants discharged (kL/day)	Concentration of Pollutants discharged(Mg/NM3)	Percentage of variation from prescribed standards with reasons	Standard	Reason
	Quantity	Concentration	%variation		
DG Set TPM	2.31	35.1	77	150	Within Limit
LSHS Boiler TPM	7.32	33	78	150	Within Limit
LSHS Boiler SO2	18.25	82	80	NA	Within Limit
DG Set SO2	6.1	93.1	77	NA	Within Limit

Part-D

HAZARDOUS WASTES

1) From Process

Hazardous Waste Type	Total During Previous Financial year	Total During Current Financial year	UOM
5.1 Used or spent oil	2.34	0.376	KL/A
28.3 Spent carbon	0.31	0.409	MT/A
28.5 Date-expired products	0.54	0.0	MT/A
28.6 Spent organic solvents	1548.04	1445.115	KL/A
37.1 Sludge from wet scrubbers	0.0	0.02	MT/A

33.1 Empty barrels /containers /liners contaminated with hazardous chemicals /wastes	1782	1980	Nos./Y
28.4 Off specification products	4.32	5.216	MT/A

2) From Pollution Control Facilities

Hazardous Waste Type	Total During Previous Financial year	Total During Current Financial year	UOM
35.3 Chemical sludge from waste water treatment	50.25	122.1	MT/A
37.3 Concentration or evaporation residues	91.53	110.64	MT/A

Part-E

SOLID WASTES

1) From Process

Non Hazardous Waste Type	Total During Previous Financial year	Total During Current Financial year	UOM
Wooden scrap,Glass scrap,Platic scrap,Metal Scrap	90.22	138.657	MT/A

2) From Pollution Control Facilities

Non Hazardous Waste Type	Total During Previous Financial year	Total During Current Financial year	UOM
NA	0	0	MT/A

3) Quantity Recycled or Re-utilized within the unit

Waste Type	Total During Previous Financial year	Total During Current Financial year	UOM
0	0	0	MT/A

Part-F

Please specify the characteristics(in terms of concentration and quantum) of hazardous as well as solid wastes and indicate disposal practice adopted for both these categories of wastes.

1) Hazardous Waste

Type of Hazardous Waste Generated	Qty of Hazardous Waste	UOM	Concentration of Hazardous Waste
5.1 Used or spent oil	0.376	KL/A	--
28.3 Spent carbon	0.409	MT/A	--
28.4 Off specification products	5.216	MT/A	--
28.6 Spent organic solvents	1445.115	KL/A	--
33.1 Empty barrels /containers /liners contaminated with hazardous chemicals /wastes	1980	Nos./Y	--
35.3 Chemical sludge from waste water treatment	122.1	MT/A	--
37.1 Sludge from wet scrubbers	0.02	MT/A	--
37.3 Concentration or evaporation residues	110.64	MT/A	--

2) Solid Waste

Type of Solid Waste Generated	Qty of Solid Waste	UOM	Concentration of Solid Waste
0	0	MT/A	--

Part-G

Impact of the pollution Control measures taken on conservation of natural resources and consequently on the cost of production.

Description	Reduction in Water Consumption (M3/day)	Reduction in Fuel & Solvent Consumption (KL/day)	Reduction in Raw Material (Kg)	Reduction in Power Consumption (KWH)	Capital Investment(in Lacs)	Reduction in Maintenance(in Lacs)
API plants Flash steam recovery	10	0.0	0	0	0.0	2.0
Methanol and water saving through reduction in centrifuge PM frequency	2.0	0	0	0	4.5	5.0
Volute plant installed instead of Decanter	0.0	0.0	0	7.8	22	4.0

Part-H

Additional measures/investment proposal for environmental protection abatement of pollution, prevention of pollution.

[A] Investment made during the period of Environmental Statement

Detail of measures for Environmental Protection	Environmental Protection Measures	Capital Investment (Lacks)
Vertical pump for E2 stream installation.	Energy consumption optimization	7.5

[B] Investment Proposed for next Year

Detail of measures for Environmental Protection	Environmental Protection Measures	Capital Investment (Lacks)
OCMS installation for boiler stack	Environment Protection.	7.0
ROCHEM RO plant upgradation	Energy consumption optimization .	18.5

Part-I

Any other particulars for improving the quality of the environment.

Particulars

Celebrated World Environment Day June 2025 and planted 1500 Nos . Plant samples for green belt area development.

Name & Designation

Sanjay.Mohite,Deputy Manager

UAN No:

MPCB-ENVIRONMENT_STATEMENT-0000087338

Submitted On:

29-09-2025

